



**PLAINS**  
ALL AMERICAN  
PIPELINE, L.P.


## Weekly Construction Progress Report

Case # **PU-12-40**

Project: Nelson to Ross

Week Ending: 7/15/2012

Report # 3

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	
Project Coordinator	Terry Wainwright	PPI	501-940-0672	
Contractor Spread	Ron Marsh	Pro-Pipe	406-239-0996	
<b>Brief Description of Week's Activities</b>				
Gridding RoW, Started M/L stringing Started M/L Bending, Started M/L welding. Continued installing ECD as moving forward.				
<b>Project Completion Spread</b>				
Description	Week Complete	% Week Complete	Total Complete	% Total Complete
Clear & Grade lft.	16,900ft		42,100ft	47.00%
ROW Finished lft.				
Stringing B/P	24,678ft		26,466ft	29.00%
Welding	6,683ft		6,683ft	7.00%
Ditching	n/a			
Lowering In	n/a			
Backfill	n/a			
Clean-up	n/a			
Coating (Welds)	n/a			
<b>ECDs Installed</b>	n/a			
Silt Fence lft.	2,798ft	n/a	7,236ft	7,236ft
Hay bales ea.	n/a	n/a		n/a
Mats ea.	99ea	n/a	192ea	192ea
Waddles ea.	92ea	n/a	174ea	174ea
<b>Project construction / reclamation activities</b>				
Description	Week Complete	% Week Complete	Total Complete	% Total Complete
Roadway / Bores ea.	n/a	n/a		n/a
Erosion / Sediment	n/a	n/a		n/a
Topsoil	n/a	n/a		n/a
Restoration/Cleanup	n/a	n/a		n/a
Roadway Restoration	n/a	n/a		n/a
Fence / Gate	n/a	n/a		n/a
Fertilizing / Seeding	n/a	n/a		n/a
<b>Project Site Safety</b>				
On Staff personal, we are acting as Safety, working together & good communication to head off any safety concerns				
Signature: 		Date: <u>7-16-2012</u>		



**PLAINS**  
**ALL AMERICAN**  
**PIPELINE, L.P.**

## Weekly Construction Progress Report

**Case #** PU-12-40 Report # 3  
**Project:** Nelson to Ross  
**Week Ending:** 7/15/2012

Dates of construction	Startup	Shutdown
	6/15/2012	

Temperature high and low for week.	High	Low
	99	61

Landowner / Public Concerns	Addressing Individual	Phone
none		

**Suspension of project activities (when, where, why ,how long)**  
ON 7-10-2012, the decision was made that we are NOT allowed in area til after 8-30-2012, Extra precautions have been made to keep this area clear due to Pipping Plover.

**Identify Cultural Resources not previously identified.**  
n/a

**Critical Habitat or Threatened or Endangered Species.**  
All proper authorities have been notified, & all area's of concern has been taped off on count of Piping Plover, main areas of interest seems to be between 86th & 87th. Extra Precautions have been made to keep area clear.

Cathodic Protection Installed	When	Where
n/a		


Special Coordination	Who	When
n/a		

Pipeline in-service date	Date
n/a	


92<sup>nd</sup> Ave Build ROW station #761+00



92<sup>nd</sup> Ave ROW station # 763+00

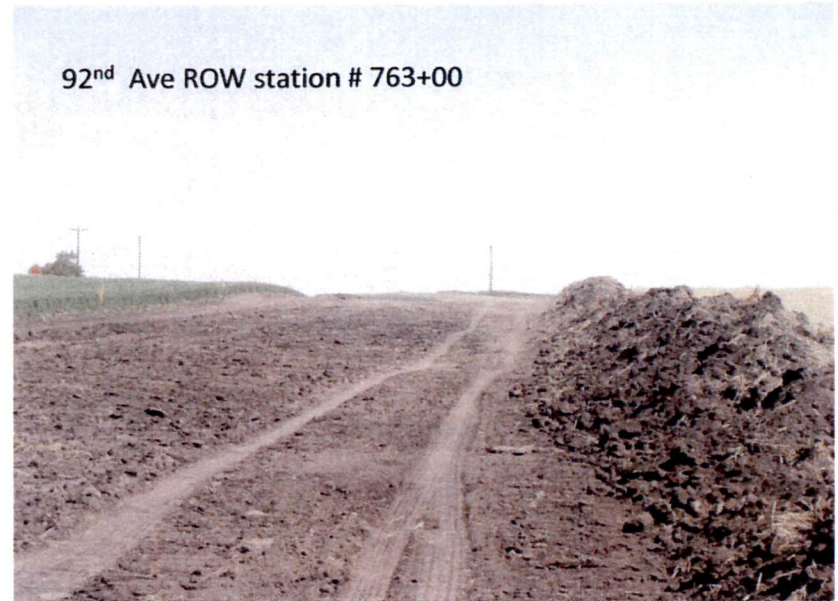

East side of 80<sup>th</sup> Ave strip topsoil station # 54+12

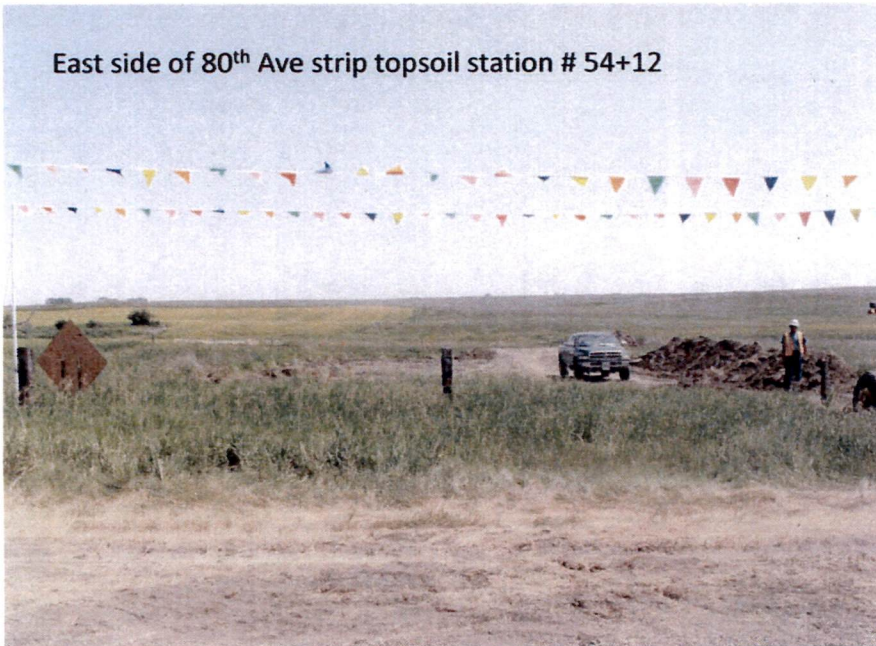

East side 80<sup>th</sup> Ave strip topsoil & approach for trucks



Christopher A. Leon  
July 13, 2012  
Sta# 256+43



**Seth Woodell**

**Date:7-13-12**

**AFE 15765**

**STA# 577+00 to 579+30**

**Silt fencing was installed on the edge of the ROW to prevent the flow of sediment off of the ROW during a rainfall event.**

