

Weekly Construction Progress Report

Case # **PU-12-40**

Project: Nelson to Ross

Week Ending: 11/18/2012

Report # 21

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	
Project Coordinator	Herbert Holder	QCS	303-748-3082	
Contractor Spread	Ron Marsh	Pro-Pipe	406-239-0996	
Office Manager	Jason Setser	QCS	918-399-2420	

Brief Description of Week's Activities

We have 3- R/bores & 1- HDD's left. We have Tie-ins, placement of the Valve setting's & Fabrication. Setting the launchers & receivers. Working on padding, backfilling as well rough grade clean-up. Getting line markers together as working with final cleanup. Discussing seeding as well ECD for final. Also getting with Landowners on options for the permanent placement of ECD's

Project Completion Spread

Description	Week Complete	% Week Complete	Total Complete	% Total Complete
Clear & Grade lft.	n/a	n/a	90,466ft	100.00%
ROW Finished lft.	n/a	n/a	n/a	n/a
Stringing B/P	n/a	n/a	90,466ft	100.00%
Tie-Ins/Valve/Fab	71ea welds	1,928ea x-rayed	1,933ea welds	n/a
Ditching	300ft	n/a	72,242ft	79.00%
Lowering In	n/a	n/a	71,271ft	78.00%
Backfill	850ft	n/a	70,521ft	77.00%
Clean-up	4,185ft	n/a	7,063ft	7.00%
Coating (Welds)ft.	Tie/In area's	n/a	90,466ft	left is Tie/Ins
ECDs Installed	n/a	n/a	n/a	n/a
Silt Fence lft.	n/a	n/a	28,196ft	n/a
Hay bales ea.	62ea	n/a	913ea	n/a
Mats ea.	25ea	n/a	744ea	n/a
Waddles ea.	19ea	n/a	328ea	n/a

Project construction / reclamation activities


Description	Week Complete	% Week Complete	Total Complete	% Total Complete
Roadway/Bores/HDD	1ea/1,622ft	Bore/HDD/4 Left	48ea	HDD+Bores=15,512ft
Erosion / Sediment	n/a	n/a	n/a	n/a
Topsoil	4,185ft	n/a	7,063ft	n/a
Restoration/Cleanup	9,876ft	n/a	Rough/In 25,812ft	28.00%
Roadway Restoration	n/a	n/a	n/a	n/a
Fence / Gate	n/a	n/a	4ea	n/a
Fertilizing / Seeding	n/a	n/a	n/a	n/a

Project Site Safety

On Staff personal, we are acting as Safety, working together & good communication to head off any safety concerns

Signature: 

Date: 11/19/2012



PLAINS

ALL AMERICAN
PIPELINE, L.P.

Weekly Construction Progress Report

Case # PU-12-40

Report # 21

Project: Nelson to Ross

Week Ending: 11/18/2012

Dates of construction	Startup	Shutdown
	6/15/2012	

Temperature high and low for week.	High	Low
	48	27

Landowner / Public Concerns	Addressing Individual	Phone
n/a		

Suspension of project activities (when, where, why ,how long)
n/a

Identify Cultural Resources not previously identified.
n/a

Critical Habitat or Threatened or Endangered Species.
n/a

Cathodic Protection Installed


Special Coordination	Who	When
Chevron line was successfully capped. Pictures are attached.		

Ryan Krapp reported to Nelson to Ross site and he conducted a PSC audit escorted by Seth Woodell
E.I Inspector

Christopher A. Leon
November 16, 2012
Sta# 25+00 +/- south
Final grade of topsoil



Christopher A. Leon
November 16, 2012
Sta# 25+00 +/- south
Final grade of topsoil

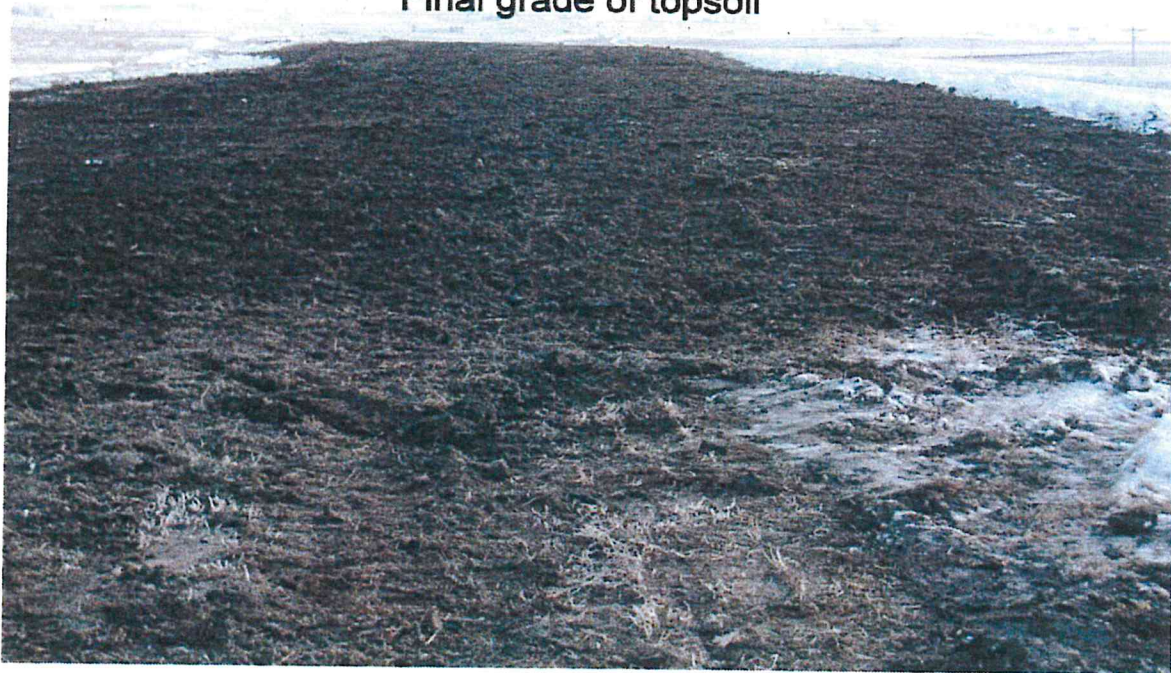



DSCF0032.JPG



DSCF0033.JPG



