

Attn: Jerry Lein
600 E. Boulevard, Dept. 408
Bismarck, ND 58505-0480

Submittal via email to ndpsc@nd.gov
Case Number: PU-14-105

Re: Sunflower Wind Project – Construction Activities Update

Dear Mr. Lein,

The Sunflower Wind Project has begun construction activities for 2016 and per the requirements set forth in the ND-03 Sunflower PSC 2014-06-25 Cert Site Compatibility (PSC 2014-05-09 Certification of Provisions item number 5) weekly construction updates are to be provided to the PSC and 3rd party consultant, Carlson McCain.

Please find the weekly construction update for the Sunflower Wind Project below.

Sincerely,



Aron Anderson
Senior Project Manager
Solas Energy Consulting

CC:
Jerry Lein
Todd Hartleben
Sean Garry
Evelyn Carpenter
Jed Dailey
Ryan Hartleben
Deron Lawrence
Cindy Whitney

Sunflower Wind Project, LLC.

Weekly Construction Update

Week of 7/22/16

- 1. Civil – Access Roads**
 - a. SWPPP inspection and maintenance
 - b. Cut/fill access road from turbine 45 to turbine 47

- 2. Civil – Turbine Pad Sites**
 - a. Cut/fill turbine pad sites – re-grading of pads completed last fall

- 3. Turbine Foundations**
 - a. Excavate turbine foundations 7,8,9,10,11,12,25,24,23,22,21,52,51,50
 - b. Place mud mats at foundations 7,8,9,10,11,12,25,24,23,22,21,52,51
 - c. Install rebar and anchor bolt cage at foundations 2,3,4,5,6,7,8,9,10,11
 - d. Place concrete at foundations 1 and 2

- 4. O&M Building**
 - a. Complete Well
 - b. Layout building footings


- 5. Substation**
 - a. Trench conduit and grounding
 - b. Begin erecting structural steel

See below for progress photos.

Access Road Check Dams



Bottom Mat and Anchor Bolt Cage

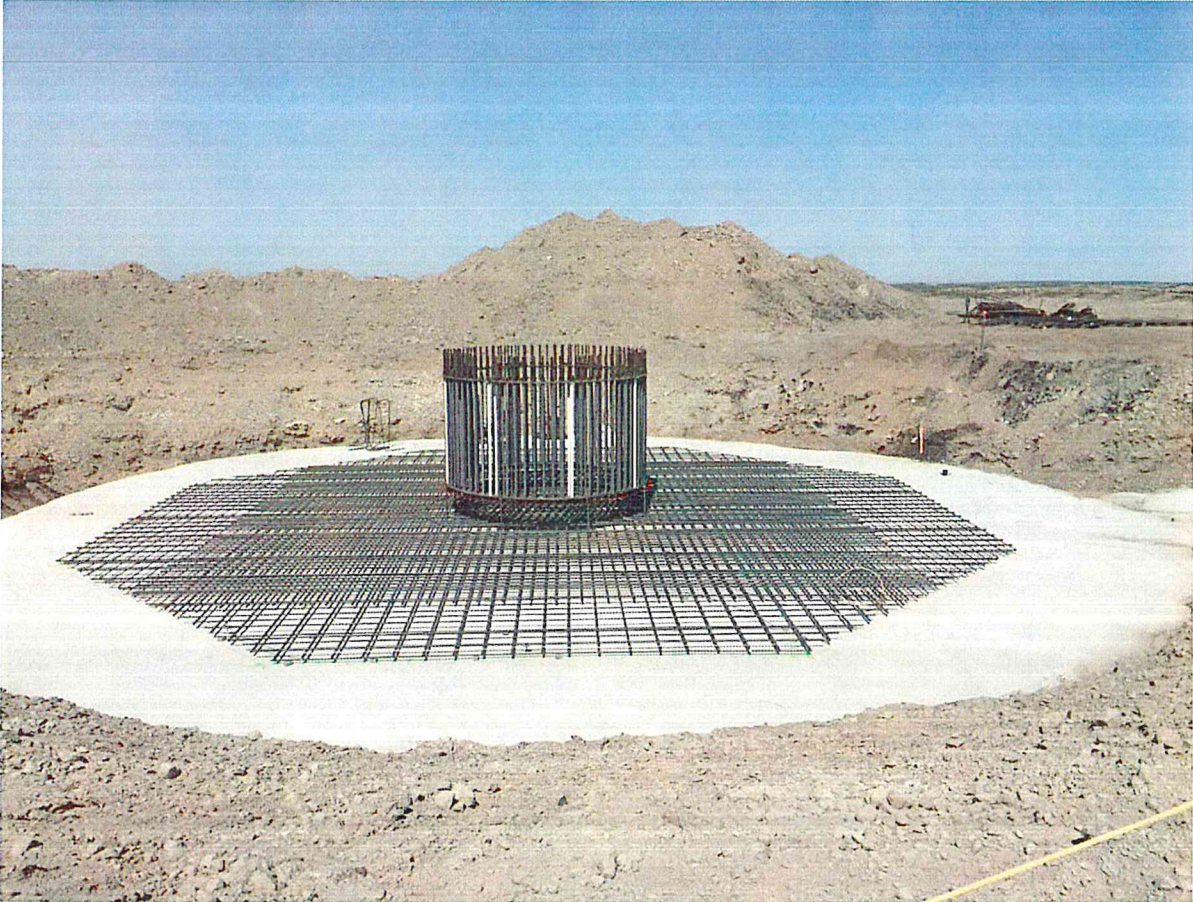

Concrete Pour



Substation Structural Steel

