



NST EXPRESS

**PSC Monthly Activity Report
May 2016
Case No. PU-15-232**

1. Summary

In the month of May 2016 on our NST Express Alexander site, the contractor completed the ring wall for Tank-100 and initiated the T200 ring wall foundation. Construction poured miscellaneous pads, Oneok relocated their line and the construction office was delivered to site.

The NST express pipeline has approximately 86000 feet of grading that has been completed, survey has staked the center line and HDD rig equipment has been mobilized, and began drilling on both sides of the river. The HDD crews have made approximately 300 linear feet of pilot on the crossing.

Fabrication work has initiated at the Fairview site.

2. Progress

For the month of May 2016:

At the Alexander site, the contractor will continue to complete the T200. Oneok relocated their 8" inch pipeline. Poured booster pump footers and drilled for helical piers.

Loenbro continues to clear topsoil as required. Pipe is being delivered on a daily basis. Loenbro has been receiving and stringing pipe as it arrives for bores and HDD on the river. 81% of grading completed, 40% pipe stringing are complete, and welding of pipeline has commenced. Fabrication started at the NST Express Fairview site for 24" manifold systems.


3. Construction

Pipeline Construction						
Task	Start	End	Complete	Remaining	% Complete	% Project
Clearing/Grade	0+00	980+00	98000	23488	81%	5%
Stringing	0+00	586+00	58600	62888	48%	5%
Welding	0+00	40+00	4000	117488	3%	20%
Trenching	0+00	0+00	0	121488	0%	15%
Lower	0+00	0+00	0	121488	0%	5%
HDD	0+00	0+00	0	121488	0%	10%
Tie-ins	0+00	0+00	0	121488	0%	10%
Hydro Test	0+00	0+00	0	121488	0%	5%
Clean/Dry	0+00	0+00	0	121488	0%	10%
Mech-Complete	0+00	0+00	0	121488	0%	5%
ROW Remediation	0+00	0+00	0	121488	0%	10%

Construction Progress for Spread Spread 1




PIPELINE CONSTRUCTION PROGRESS/TASK

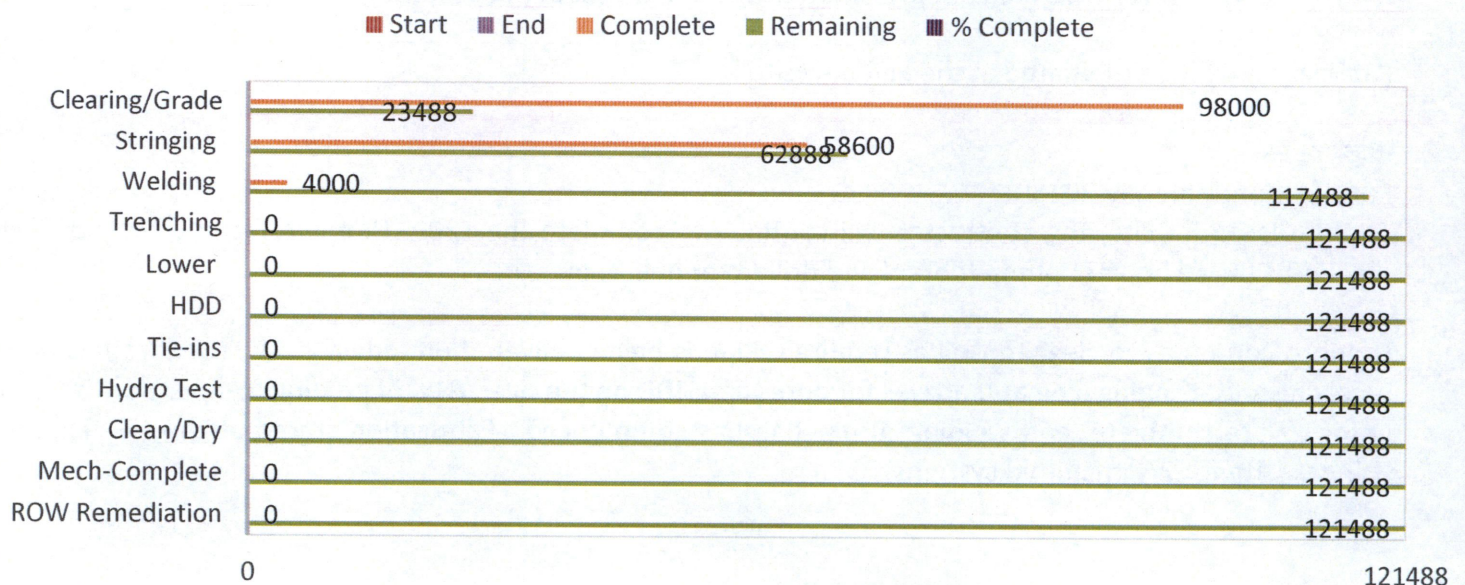

Alexander Construction Progress/Task

Tasks	Mobilization Date	Start Date	Days Working	Days Planned	Comp. %	Remaining %	Status
Site Prep & Grading	4/12/2016	4/12/2016	28	39	72%	28%	
Tank 100 Ring Wall	5/4/2016	5/04/2016	9	9	100%	100%	
Tank 200 Ring Wall	6/13/2016						
Civil Structural	5/4/2016	5/04/2016	20	49	40%	60%	
Major Electrical	6/16/2016						
Mechanical Piping	6/6/2016						
I&E	8/1/2016						
Sheds	8/15/2016						
Access Road	8/22/2016						
Landscape	9/1/2016						
Hydro test	9/1/2016						
Finish Grade	9/15/2016						
Fencing	10/1/2016						

ALEXANDER CONSTRUCTION PROGRESS/TASK

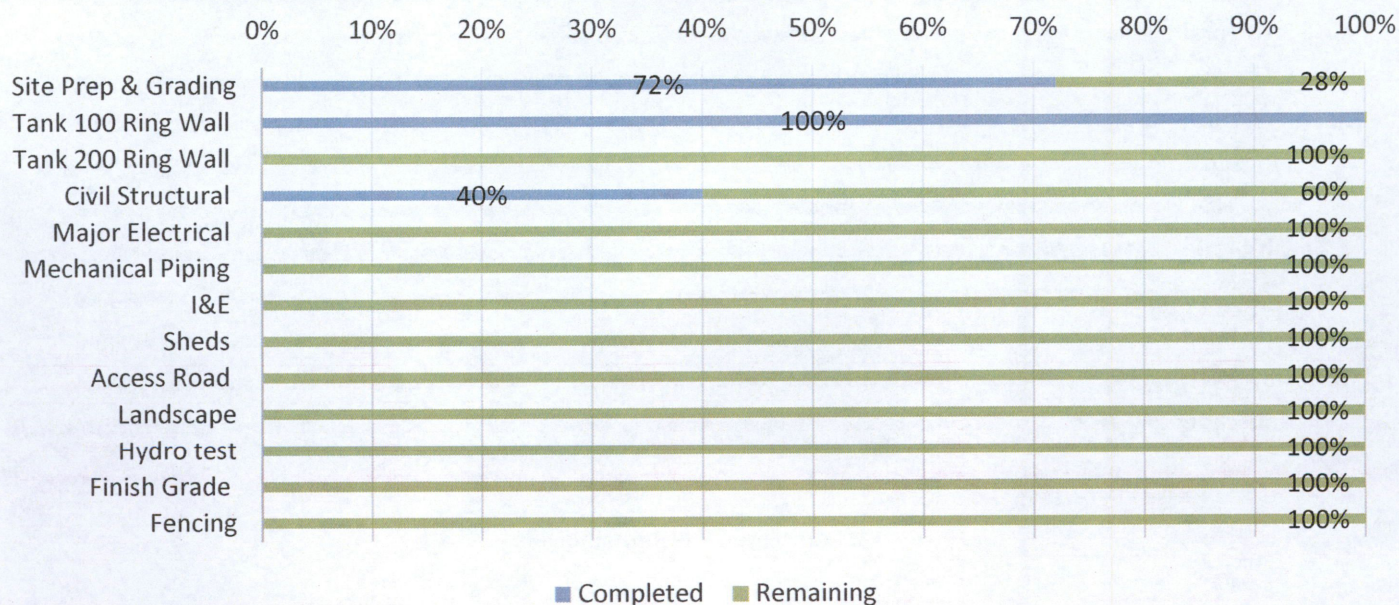

Fairview Construction Progress/Task

Tasks	Mobilization Date	Start Date	Days Working	Days Planned	Comp. %	Remaining %	Status
Mechanical Piping	5/2/2016	5/9/2016	19	24	80%	20%	
Civil Structural	6/6/2016						
Site Prep & Grading	6/15/2016						
Major Electrical	7/1/2016						
Hydro test	8/1/2016						
I&E	8/15/2016						
Finish Grade	9/5/2016						
Fencing	9/15/2016						
Sheds	9/30/2016						
Tank Ring Wall	NA						
Landscape	NA						

FAIRVIEW CONSTRUCTION PROGRESS/TASK

