

## 1. Summary

In the month of June 2016 at the Alexander facility, contractor initiated the LACT foundation, continued to pour miscellaneous pads, cured ring wall for Tank-200 and sand backfilled Tank-200. The construction contractor completed the MCC building and booster pump foundations. Preparation for equipment to be delivered has been initiated.

The NST Express pipeline construction crew has approximately backfilled 35,430 feet of pipe, Pre-Hydro tested HDD pipe, completed HDD across Hwy 58 and Yellowstone River HDD near completion.

Contractor continued fabrication work and installed underground piping in the Fairview facility. Local electric contractor installed unground electric lines and set the transformer.

## 2. Progress

At the Alexander site, contractor will continue to complete Tank-200 sand back fill, electrical equipment to arrive and initiate electrical installation, tank vendor will begin to erect Tank-100, and continue pipe fabrication.

Pipeline contractor work will continue to string pipe, lower and backfill. Clean up crew initiated on west side of the Yellowstone river.


Continue civil work at the Fairview facility. Underground pipe installation, preparation for helical pier installation at Fairview and Alexander facilities are in progress.

## 5. Construction

Pipeline Construction						
Task	Start	End	Complete	Remaining	% Complete	% Project
Clearing/Grade	0+00	1210+81	121488	0	100%	5%
Stringing	0+00	922+00	92200	29288	76%	5%
Welding	0+00	595+00	59500	61988	49%	20%
Trenching	0+00	80+00	8000	113488	7%	15%
Lower	0+00	80+00	8000	113488	7%	5%
HDD	0+00	182+00	677	9375	1%	10%
Tie-ins	0+00	80+00	7878	113610	6%	10%
Hydro Test	0+00	0+00			0%	5%
Clean/Dry	0+00	0+00			0%	10%
Mech-Complete	0+00	0+00			0%	5%
ROW Remediation	0+00	0+00			0%	10%


### PIPELINE CONSTRUCTION PROGRESS/TASK

■ Start ■ End ■ Complete ■ Remaining ■ % Complete

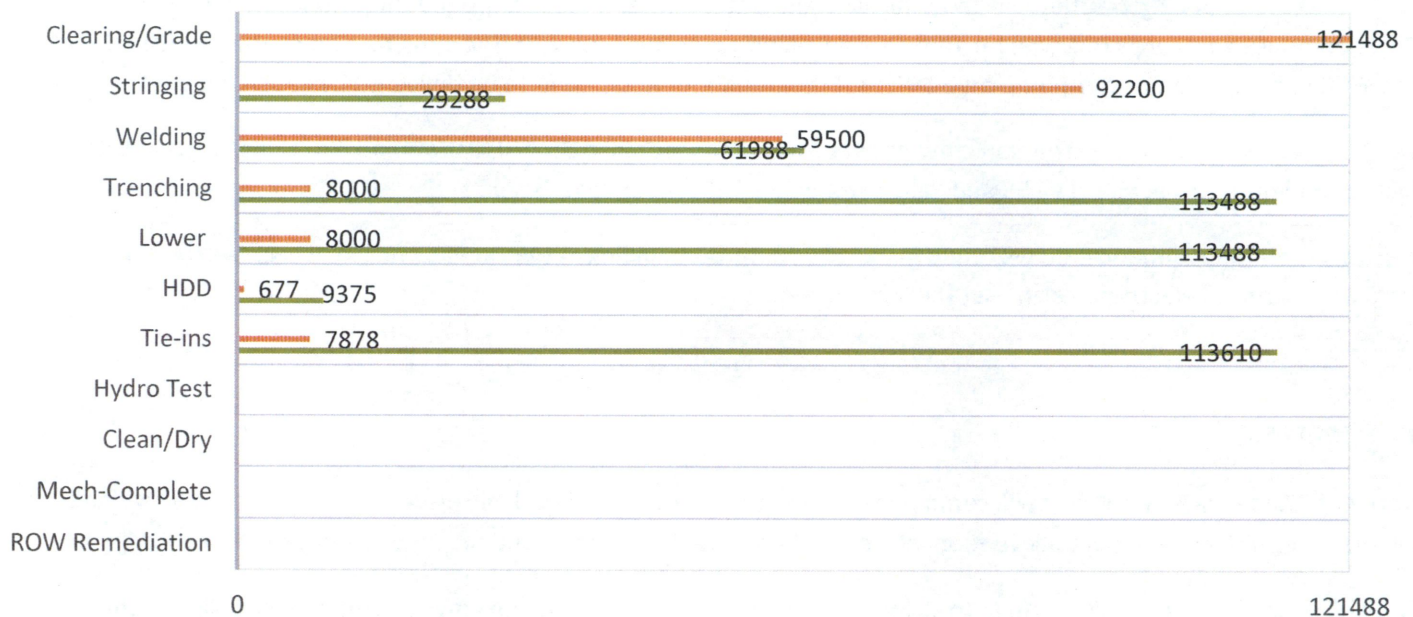


Alexander Construction Progress/Task							
Tasks	Mobilization Date	Start Date	Days Working	Days Planned	Comp. %	Remaining %	Status
Site Prep & Grading	4/12/2016	4/12/2016	24	20	100%	0	Completed 5/26
Tank 100 Ring Wall	5/04/2016	5/04/2016	9	9	100%	0	Complete
Tank 200 Ring Wall	6/13/2016	6/01/2016	9	23	74%	26%	
Civil Structural	5/04/2016	5/04/2016	20	83	40%	60%	
Major Electrical	6/16/2016	6/13/2016	13	162	8%	92%	
Mechanical Piping	6/06/2016	6/17/2016	9	64	15%	85%	
I&E	7/23/2016	7/23/2016		53			
Sheds	8/15/2016			24			
Access Road	8/22/2016			6			
Landscape	9/01/2016			10			
Hydro test	9/16/2016			10			
Finish Grade	9/15/2016			30			
Fencing	9/01/2016			36			


### ALEXANDER CONSTRUCTION PROGRESS/TASK

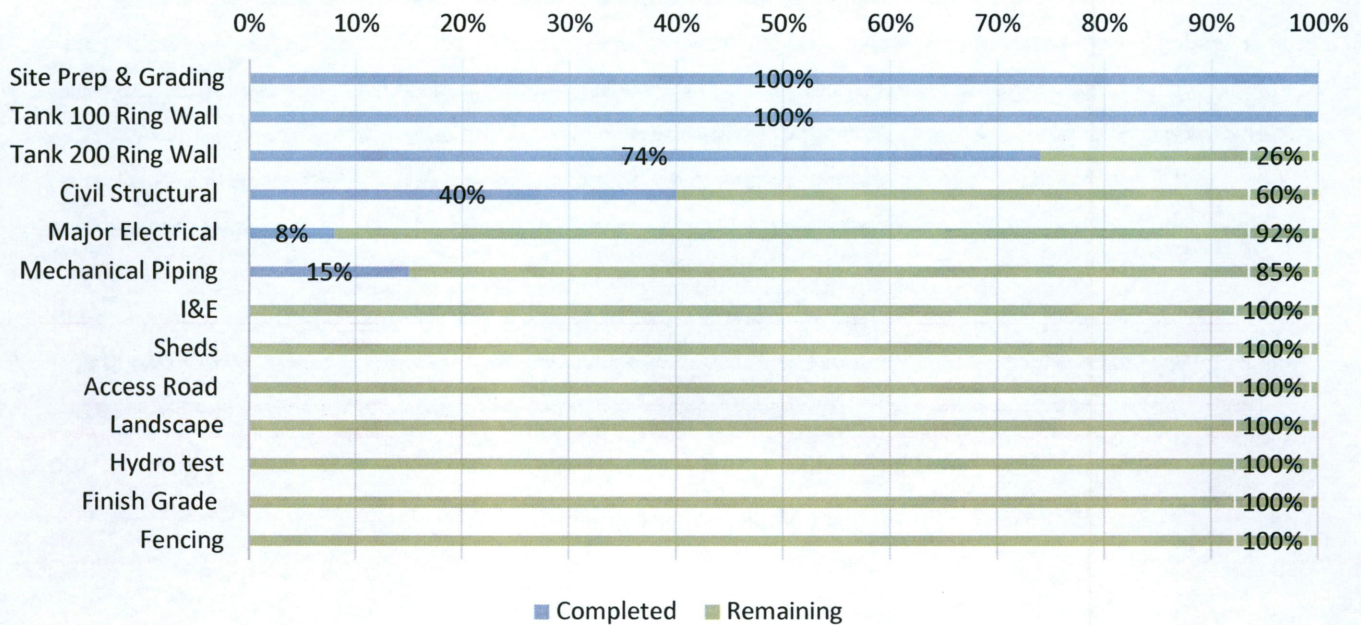

Fairview Construction Progress/Task							
Tasks	Mobilization Date	Start Date	Days Working	Days Planned	Comp. %	Remaining %	Status
Mechanical Piping	5/2/2016	5/9/2016	42	94	44%	56%	
Civil Structural	6/6/2016						
Site Prep & Grading	6/15/2016						
Major Electrical	7/1/2016						
Hydro test	8/1/2016						
I&E	8/15/2016						
Finish Grade	9/5/2016						
Fencing	9/15/2016						
Sheds	9/30/2016						
Tank Ring Wall	NA						
Landscape	NA						

### FAIRVIEW CONSTRUCTION PROGRESS/TASK

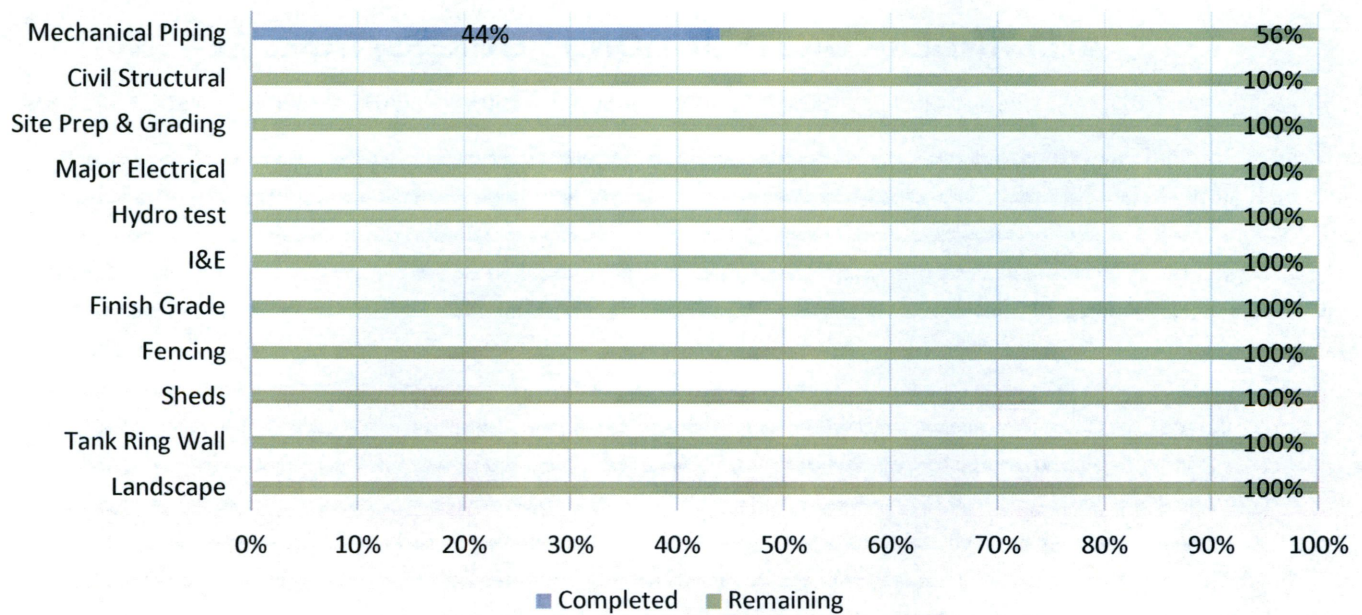

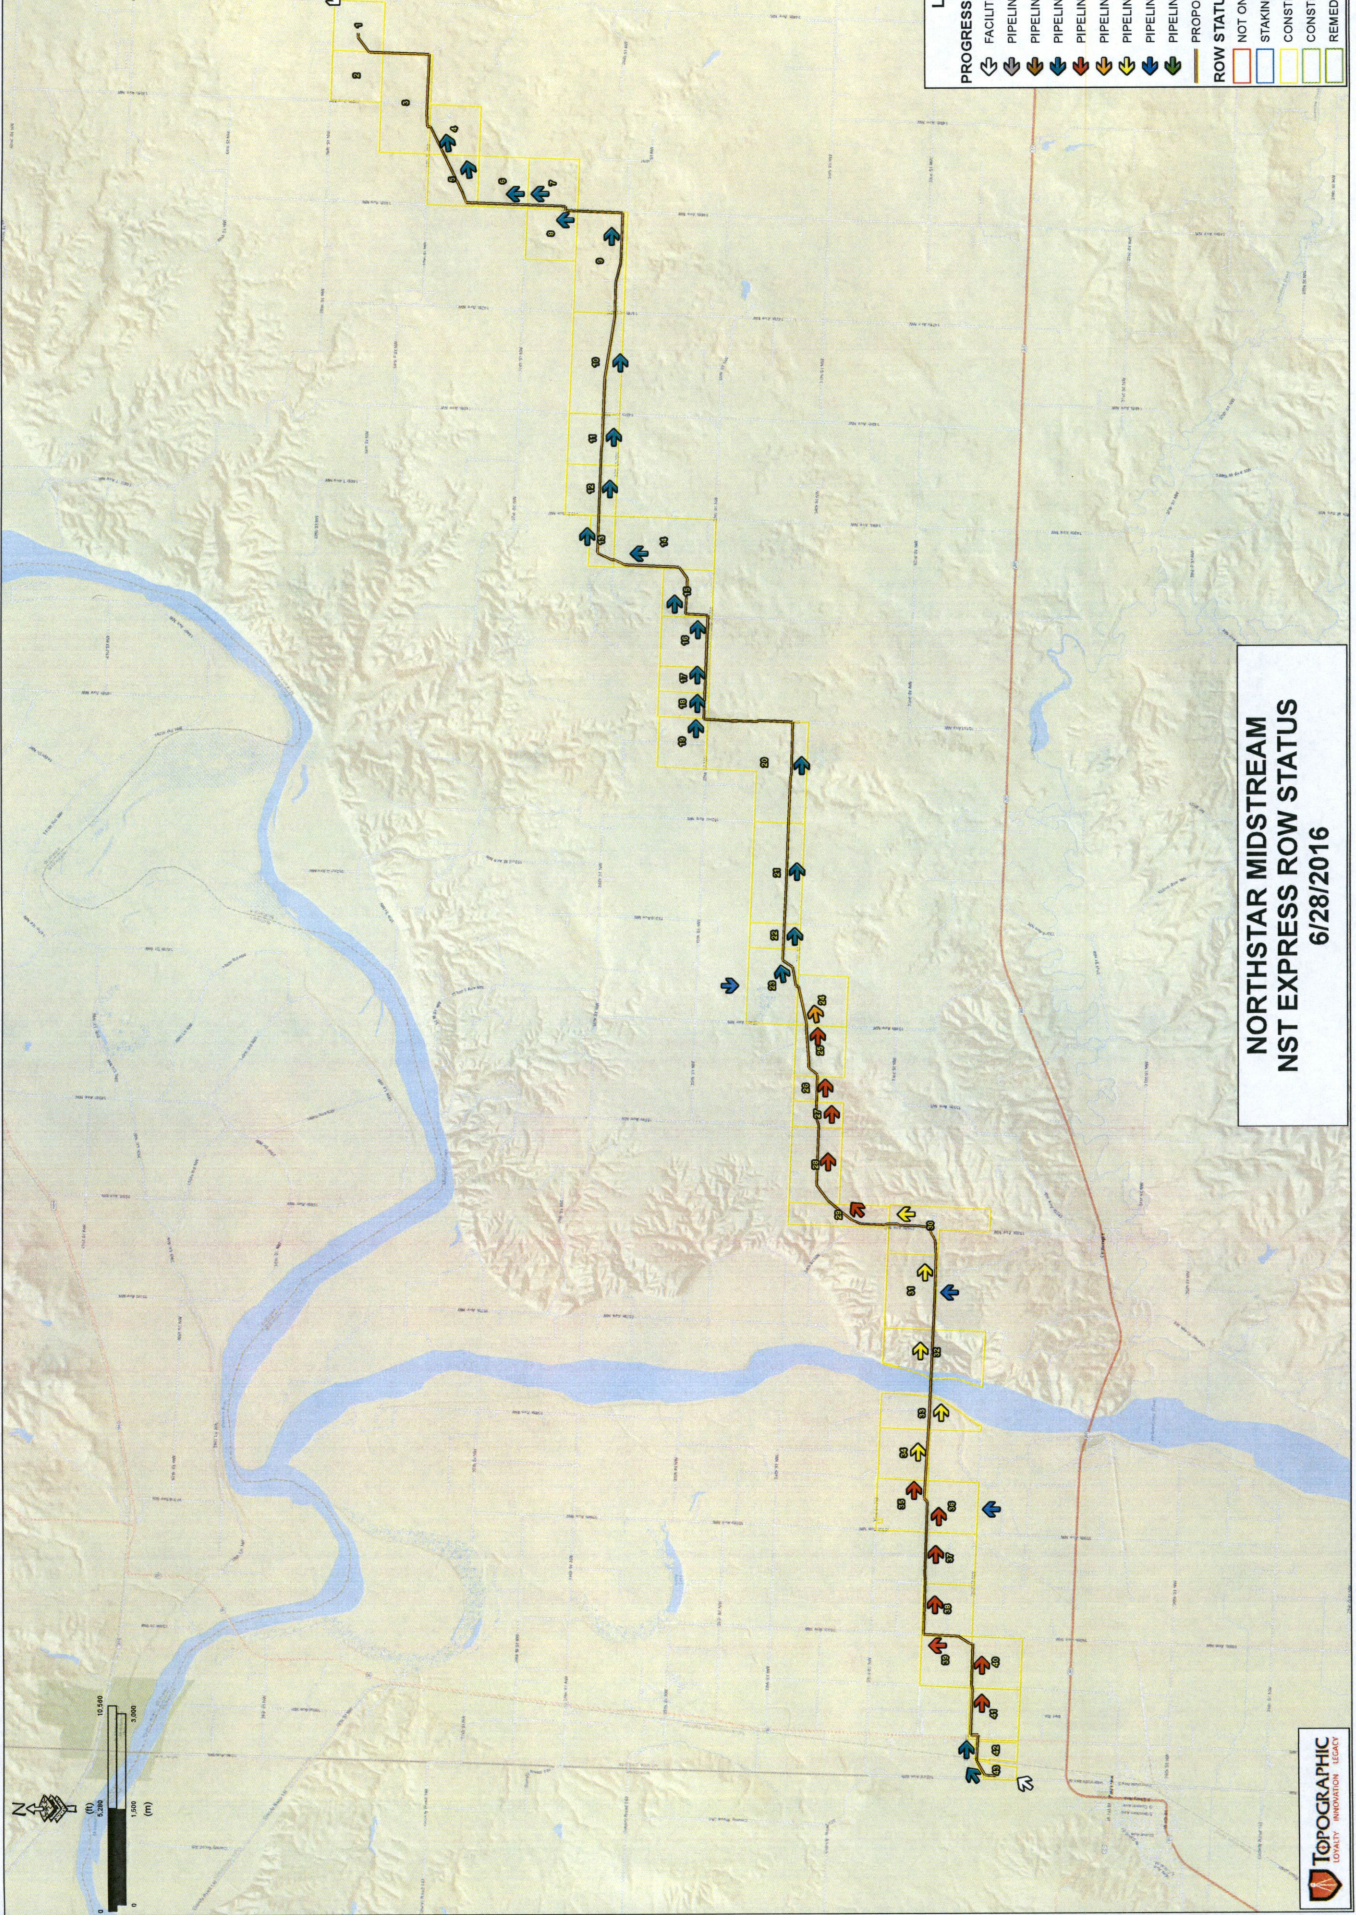

**Legend**

PROGRESS	
	FACILITIES GRADING
	PIPELINE CLEARING (100%)
	PIPELINE GRADING (100%)
	PIPELINE STRINGING
	PIPELINE WELDING
	PIPELINE TRENCHING
	PIPELINE LOWERING/FILLING
	PIPELINE TYING
	PIPELINE REMEDIATING
	PROPOSED PIPELINE
ROW STATUS	
	NOT ON
	STAKING (100%)
	CONSTRUCTION STARTED
	CONSTRUCTION COMPLETE
	REMEDIATED

**NORTHSTAR MIDSTREAM  
NST EXPRESS ROW STATUS  
6/28/2016**
