

1. Summary

In the month of August 2016 at the Alexander facility, initiated work for the LACT canopy steel beams, set mainline pump, cable tray work and began prefabrication piping. Work for above ground piping on pipe supports initiated. Tank contractor erected 5th ring wall on Tank-100 and erected 3rd ring wall on Tank-200 work.

The NST Express pipeline construction crew completed all tie-in's and road bores. Pipeline pig traps completed and set at facilities. Final cleanup is at 90 percent and pipeline will be prepared to hydrotest.

At the Fairview facility contractor set the MCC building on foundation piers, initiated work for cable tray support, prepared work for the 24 inch strainers and work on the tie in to the 24 inch headers. All underground piping for the Fairview facility is in place and work will continue on above ground piping.

2. Progress

At the Alexander site, contractor will continue to work on the LACT canopy, LACT skids to be installed, set pipe on above ground pipe supports, and continue to install pre fab piping. Electrical team to continue work on MCC building and set cable trays. Tank vendor will begin to erect Tank-200 3rd ring wall, work on manways and continue work on Tank-100 6rd ring wall.


Pipeline contractor will continue to complete work on right of way for final cleanup and pre-prepare for hydrotesting the NSTX Pipeline.

Contractor to continue to work on Fairview Metering piping, mainline pump piping, install all above ground piping, work on lighting conduits and erect all pipe supports.

3. Construction

Pipeline Construction						
Task	Start	End	Complete	Remaining	% Complete	% Project
Clearing/Grade	0+00	1210+81	121488		100%	5%
Stringing	0+00	1210+81	121488		100%	5%
Welding	0+00	1210+81	121488		100%	20%
Trenching	0+00	1210+81	121488		100%	15%
Lower	0+00	1210+81	121488		100%	5%
HDD	0+00	1210+81	121488		100%	10%
Tie-ins	0+00	1210+81	121488		100%	10%
Hydro Test	0+00	0+00			0%	5%
Clean/Dry	0+00	0+00			0%	10%
Mech-Complete	0+00	0+00			0%	5%
ROW Remediation	0+00	1210+81	121488		100%	10%


PIPELINE CONSTRUCTION PROGRESS/TASK

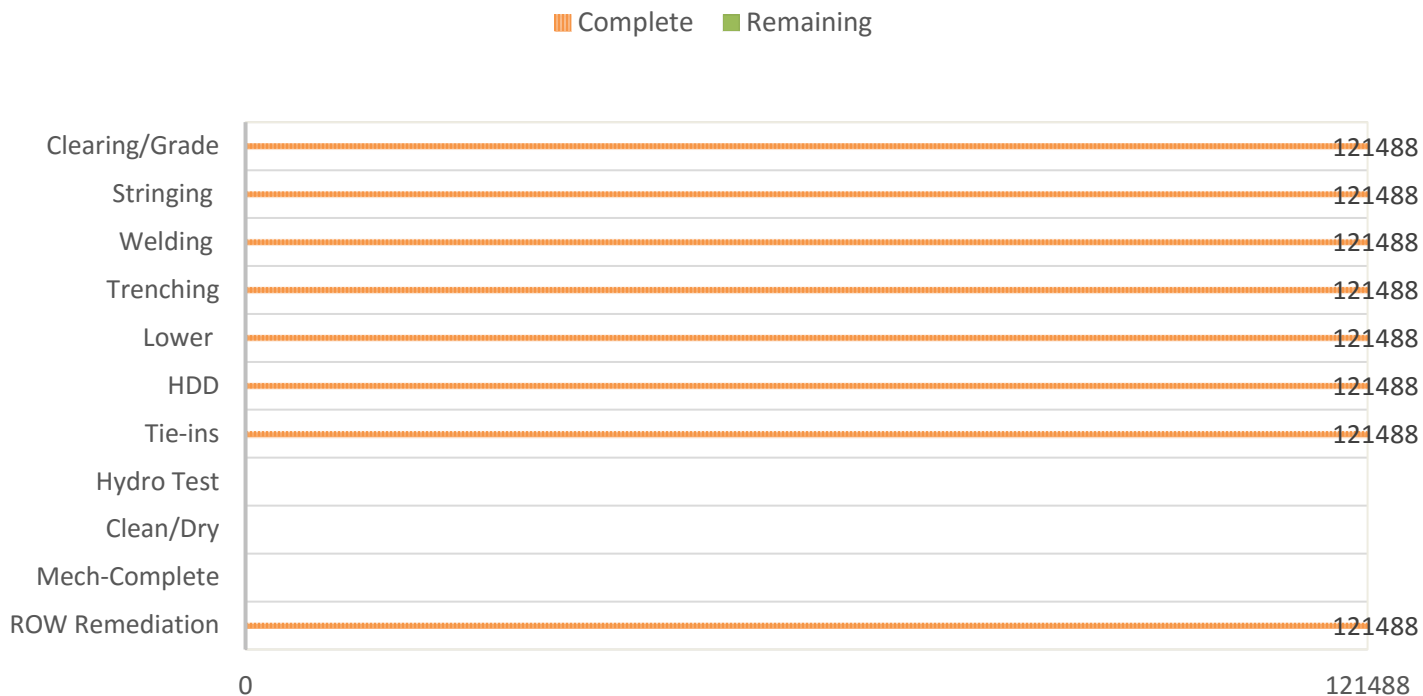

Alexander Construction Progress/Task

Tasks	Mobilization Date	Start Date	Days Working	Days Planned	Comp. %	Remaining %	Status
Site Prep & Grading	4/12/2016	4/12/2016	24	20	100%		Completed 5/26
Tank 100 Ring Wall	5/04/2016	5/04/2016	9	9	100%		Complete
Tank 200 Ring Wall	6/13/2016	6/01/2016	15	23	100%		Complete
Civil Structural	5/04/2016	5/04/2016	78	83	95%	5%	
Major Electrical	6/16/2016	6/13/2016	60	162	40%	60%	
Mechanical Piping	6/06/2016	6/17/2016	59	64	95%	5%	
I&E	7/23/2016	7/23/2016		53			
Sheds	8/15/2016		17	24	65%	45%	
Access Road	8/22/2016			3			
Landscape	9/01/2016			10			
Hydro test	9/16/2016			10			
Finish Grade	9/15/2016			30			
Fencing	9/01/2016	8/01/2016	14	36	65%	45%	


ALEXANDER CONSTRUCTION PROGRESS/TASK


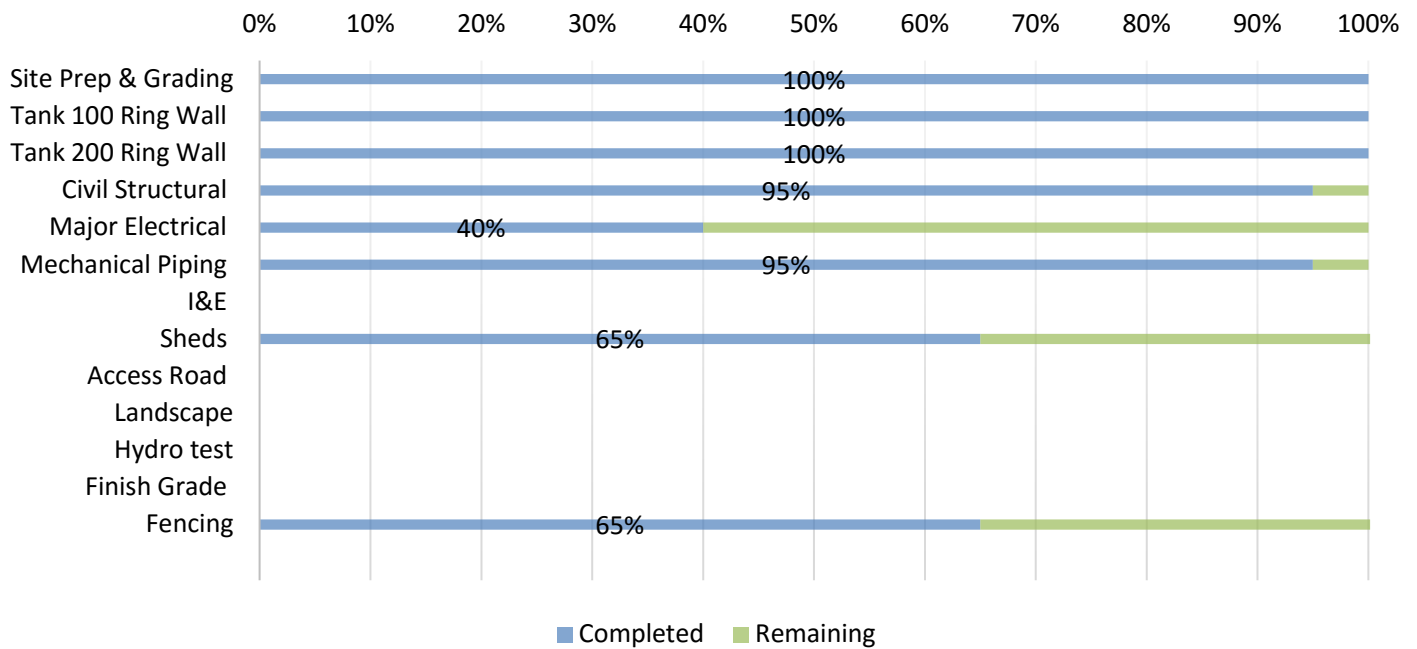


Fairview Construction Progress/Task

Tasks	Mobilization Date	Start Date	Days Working	Days Planned	Comp. %	Remaining %	Status
Mechanical Piping	5/2/2016	5/9/2016	75	94	80%	20%	
Civil Structural	6/6/2016	7/14/2016	36	45	98%	20%	
Site Prep & Grading	6/15/2016						
Major Electrical	7/1/2016	8/14/2016	24	54	30%	70%	
Hydro test	8/1/2016						
I&E	8/15/2016						
Finish Grade	9/5/2016						
Fencing	9/15/2016						
Sheds	9/30/2016						
Tank Ring Wall	NA						
Landscape	NA						

FAIRVIEW CONSTRUCTION PROGRESS/TASK

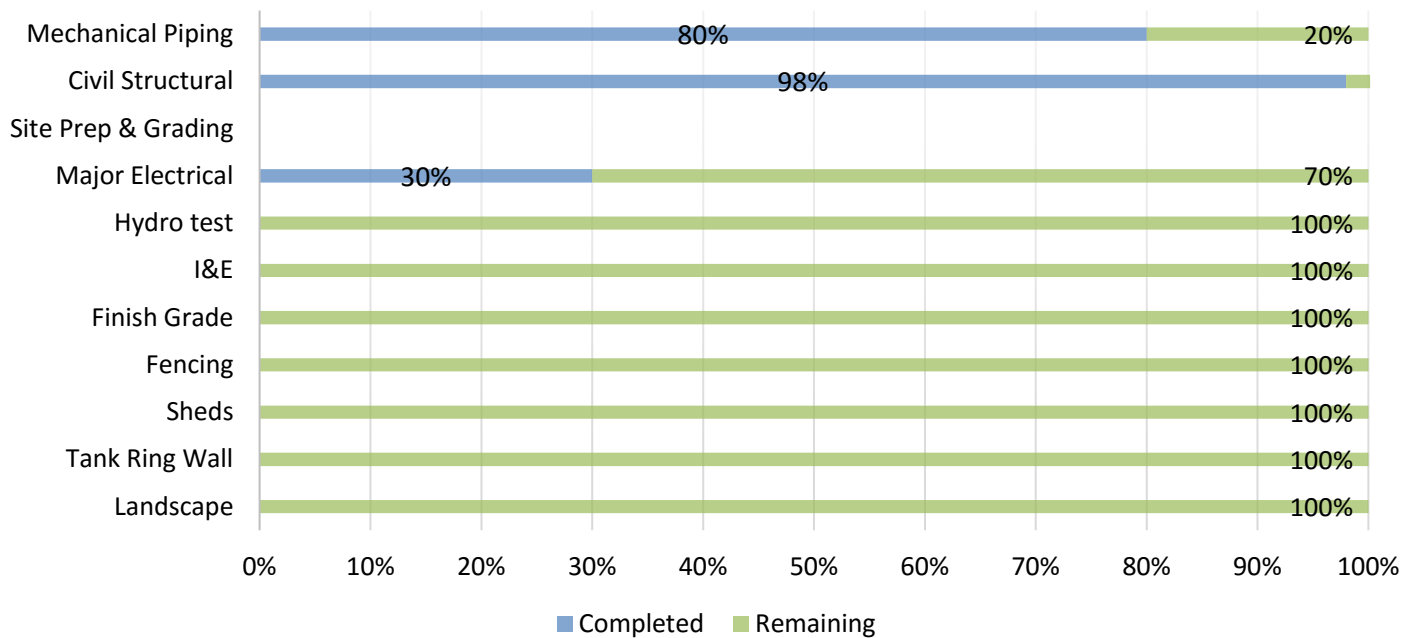

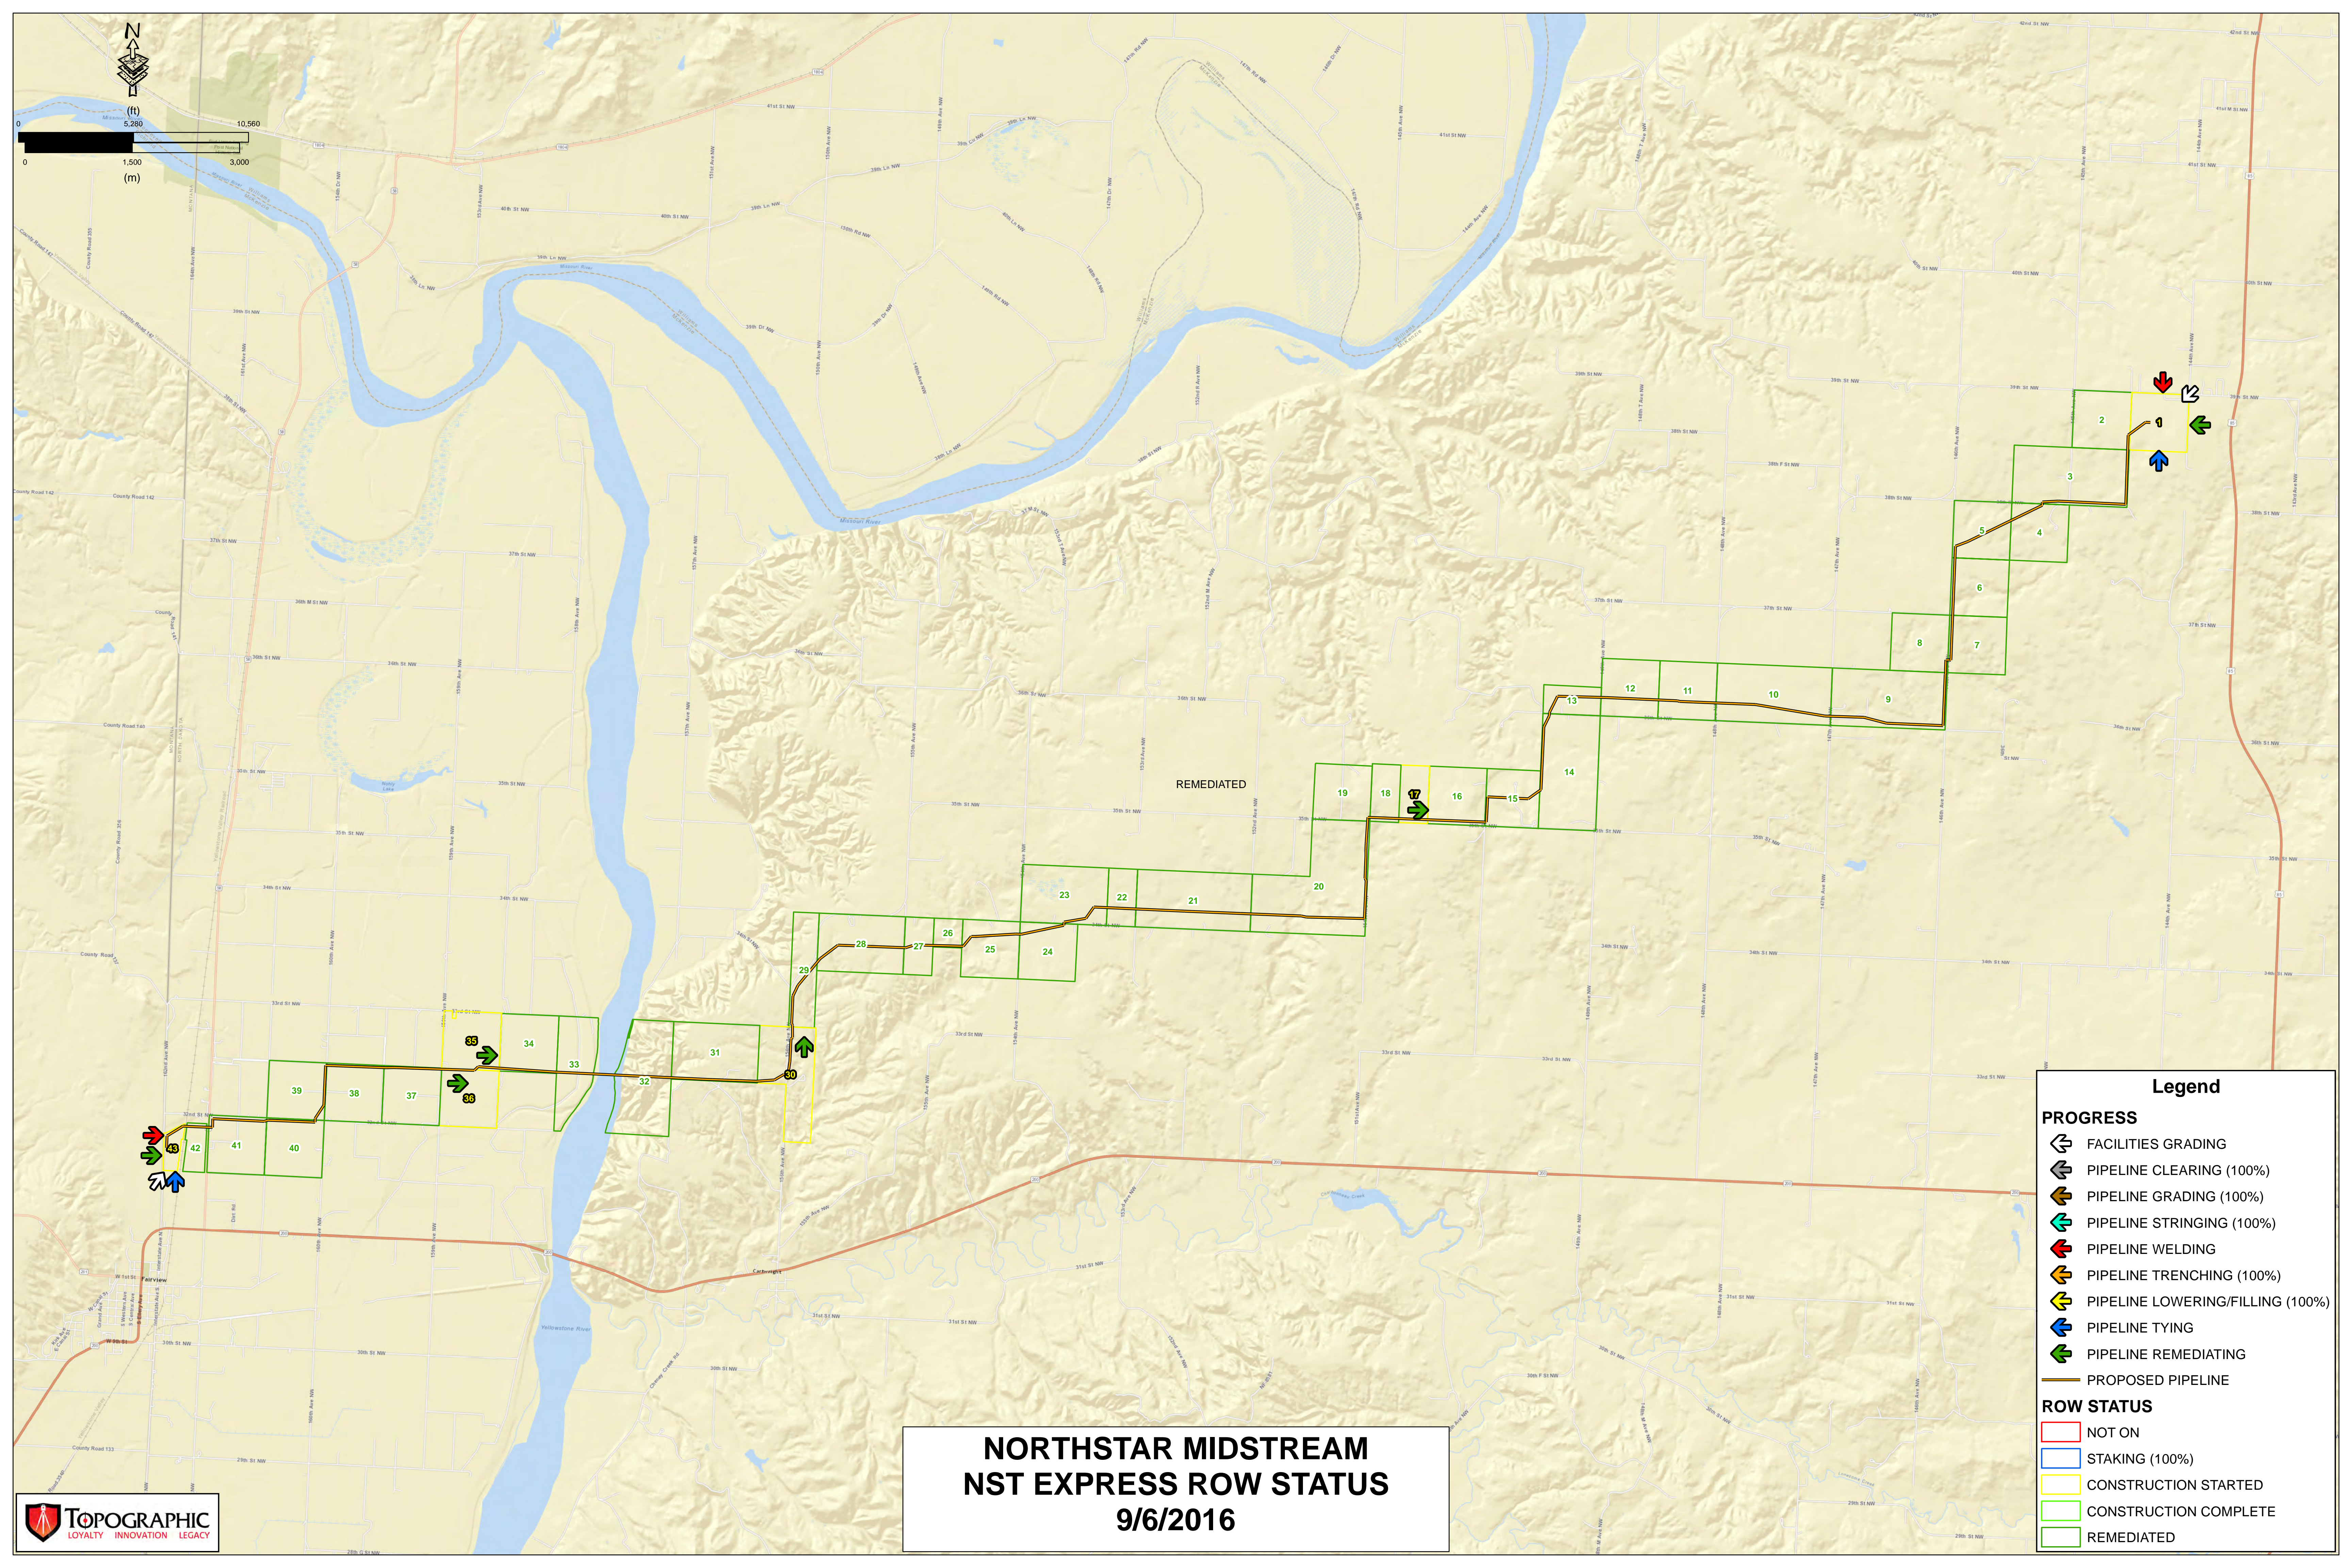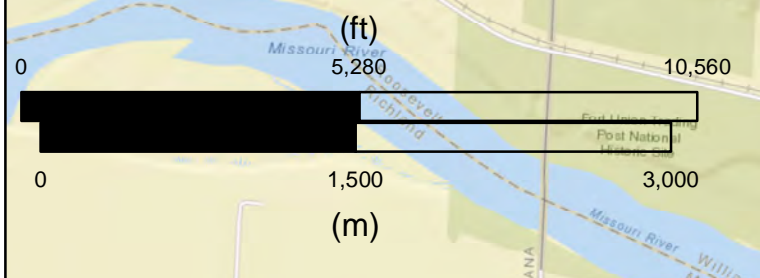

REMEDIATED

Legend

PROGRESS

- FACILITIES GRADING
- PIPELINE CLEARING (100%)
- PIPELINE GRADING (100%)
- PIPELINE STRINGING (100%)
- PIPELINE WELDING
- PIPELINE TRENCHING (100%)
- PIPELINE LOWERING/FILLING (100%)
- PIPELINE TYING
- PIPELINE REMEDIATING
- PROPOSED PIPELINE

ROW STATUS

- NOT ON
- STAKING (100%)
- CONSTRUCTION STARTED
- CONSTRUCTION COMPLETE
- REMEDIATED

**NORTHSTAR MIDSTREAM
NST EXPRESS ROW STATUS
9/6/2016**

