

**NST
EXPRESS**

**PSC Monthly Activity Report
October 2016
Case No. PU-15-232**

1. Summary

In the month of October 2016 at the Alexander facility, contractor worked on electrical wiring and lighting to the Alexander facility. Tank contractor successfully completed Tank-100 Hydrotest and Tank-200 crew worked on roof and internal piping. Tank-300 foundation work in progress. Fire suppression contractor began work on installing fire hydrant loop lines and place lines for the foam chambers.

The NST Express pipeline contractor completed installation of pig trap pipe supports, working on reseeding right of way and final clean up.

At the Fairview facility, contractor worked on torquing all bolts on valves, fittings and completing the site restoration.

2. Progress

At the Alexander site, construction contractor will continue to work on painting, grading and demobilization. Electrical team continued to work on wiring to all equipment. Tank contractor to finalize and prepare to hydrotest Tank-200.

Pipeline contractor will work on completing final cleanup and right of way fencing.

Fairview contractor will continue to work on restoring facility and final clean up.

3. Construction


Pipeline Construction						
Task	Start	End	Complete	Remaining	% Complete	% Project
Clearing/Grade	0+00	1210+81	121488		100%	5%
Stringing	0+00	1210+81	121488		100%	5%
Welding	0+00	1210+81	121488		100%	20%
Trenching	0+00	1210+81	121488		100%	15%
Lower	0+00	1210+81	121488		100%	5%
HDD	0+00	1210+81	121488		100%	10%
Tie-ins	0+00	1210+81	121488		100%	10%
Hydro Test	0+00	0+00	121488		100%	5%
Clean/Dry	0+00	0+00	121488		100%	10%
Mech-Complete	0+00	0+00	121488		100%	5%
ROW Remediation	0+00	1210+81	121488		100%	10%

PIPELINE CONSTRUCTION PROGRESS/TASK




Alexander Construction Progress/Task							
Tasks	Mobilization Date	Start Date	Days Working	Days Planned	Comp. %	Remaining %	Status
Site Prep & Grading	4/12/2016	4/12/2016	24	20	100%		Complete
Tank 100 Ring Wall	5/04/2016	5/04/2016	9	9	100%		Complete
Tank 200 Ring Wall	6/13/2016	6/01/2016	15	23	100%		Complete
Civil Structural	5/04/2016	5/04/2016	78	83	97%	3%	Structural for Tank 200 remaining
Major Electrical	6/16/2016	6/13/2016	60	162	97%	3%	Working punch list items and Tank 200
Mechanical Piping	6/06/2016	6/17/2016	59	64	97%	3%	Working punch list items and Tank 200
I&E	7/23/2016	7/23/2016	45	53	97%	3%	Working punch list items and Tank 200
Sheds	8/15/2016	8/15/2016	20	24	99%	1%	Working punch list items
Access Road	8/22/2016			3	0%	100%	Will be completed last
Landscape	9/16/2016	9/16/2016	9	10	99%	1%	Working punch list items
Hydro test	9/21/2016	9/21/2016	12	15	95%	5%	Tank 200 pipe remaining
Finish Grade	10/10/2016	10/10/2016	13	30	90%	10%	Complete
Fencing	8/01/2016	8/01/2016	14	36	65%	35%	Complete


ALEXANDER CONSTRUCTION PROGRESS/TASK

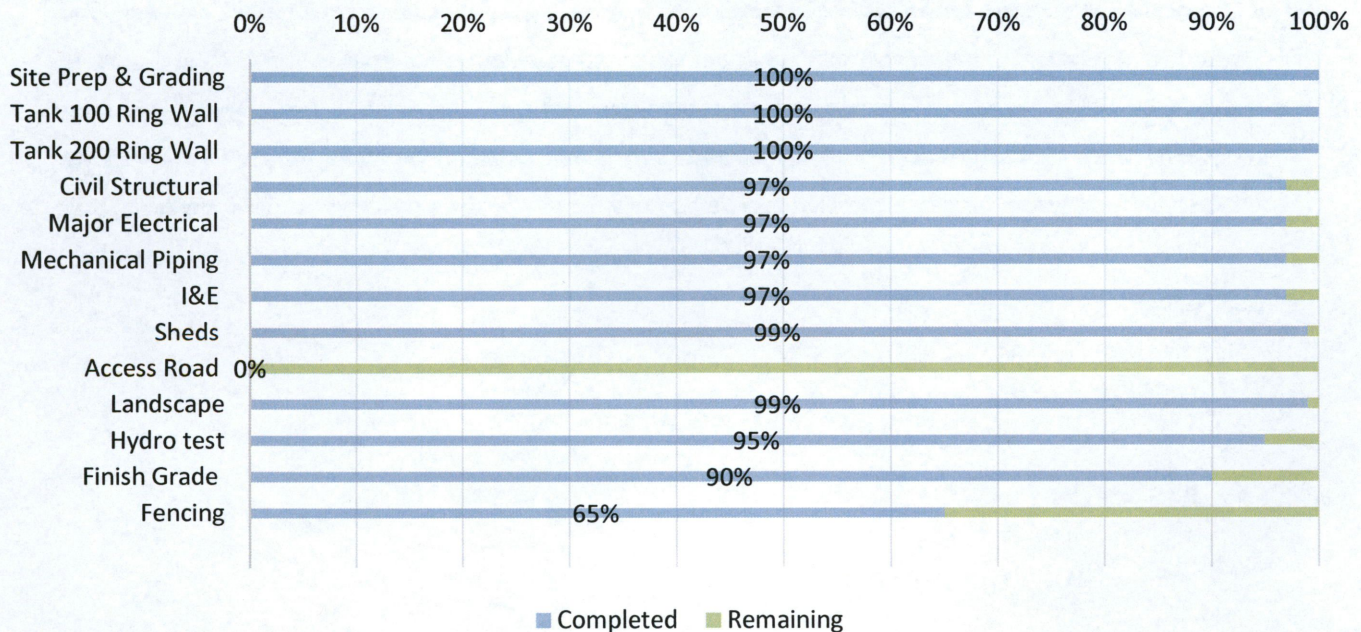

Fairview Construction Progress/Task							
Tasks	Mobilization Date	Start Date	Days Working	Days Planned	Comp. %	Remaining %	Status
Mechanical Piping	5/02/2016	5/02/2016	73	75	99%	1%	Working punch list
Civil Structural	6/06/2016	6/06/2016	42	36	95%	5%	24" manifold catwalk remaining
Site Prep & Grading	10/24/2016	10/24/2016	3	3	100%		
Major Electrical	7/01/2016	7/01/2016	30	36	99%	1%	Working punch list
Hydro test	9/27/2016	9/27/2016	12	7	100%		
I&E	8/15/2016	9/12/2016	15	12	99%	1%	Working punch list
Finish Grade	10/24/2016	10/24/2016	5	10	96%	4%	
Fencing				6		100%	
Sheds	9/15/2016	9/15/2016	17	13	100%		
Landscape	NA	NA					

FAIRVIEW CONSTRUCTION PROGRESS/TASK

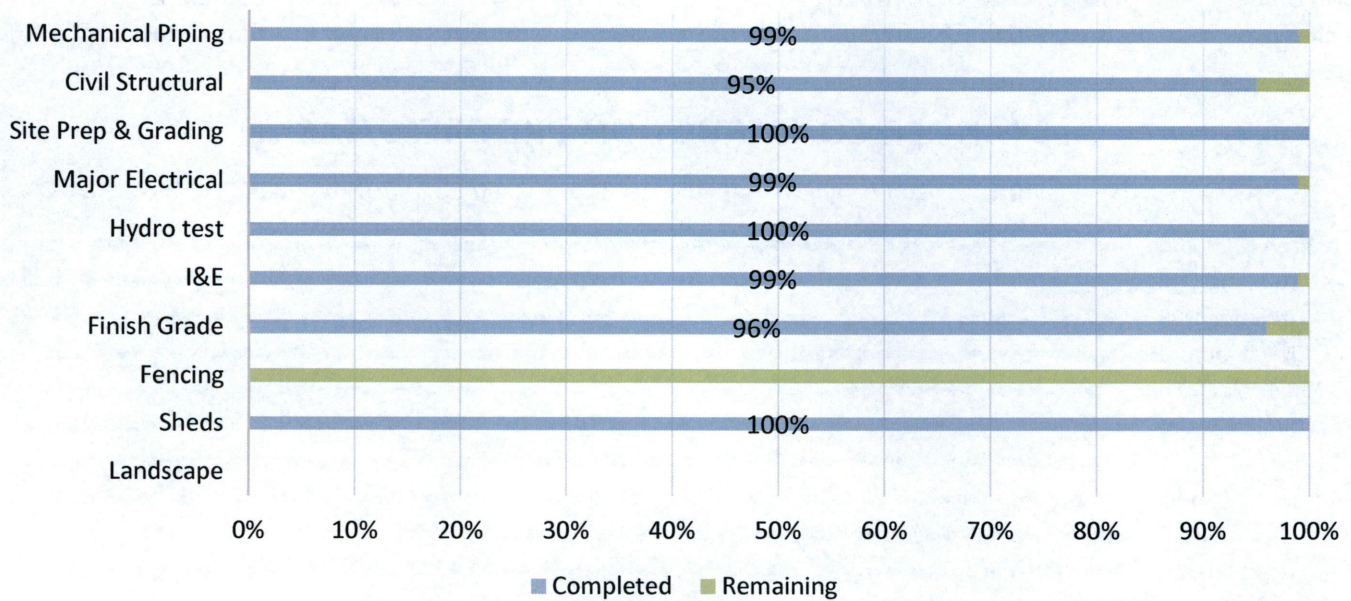

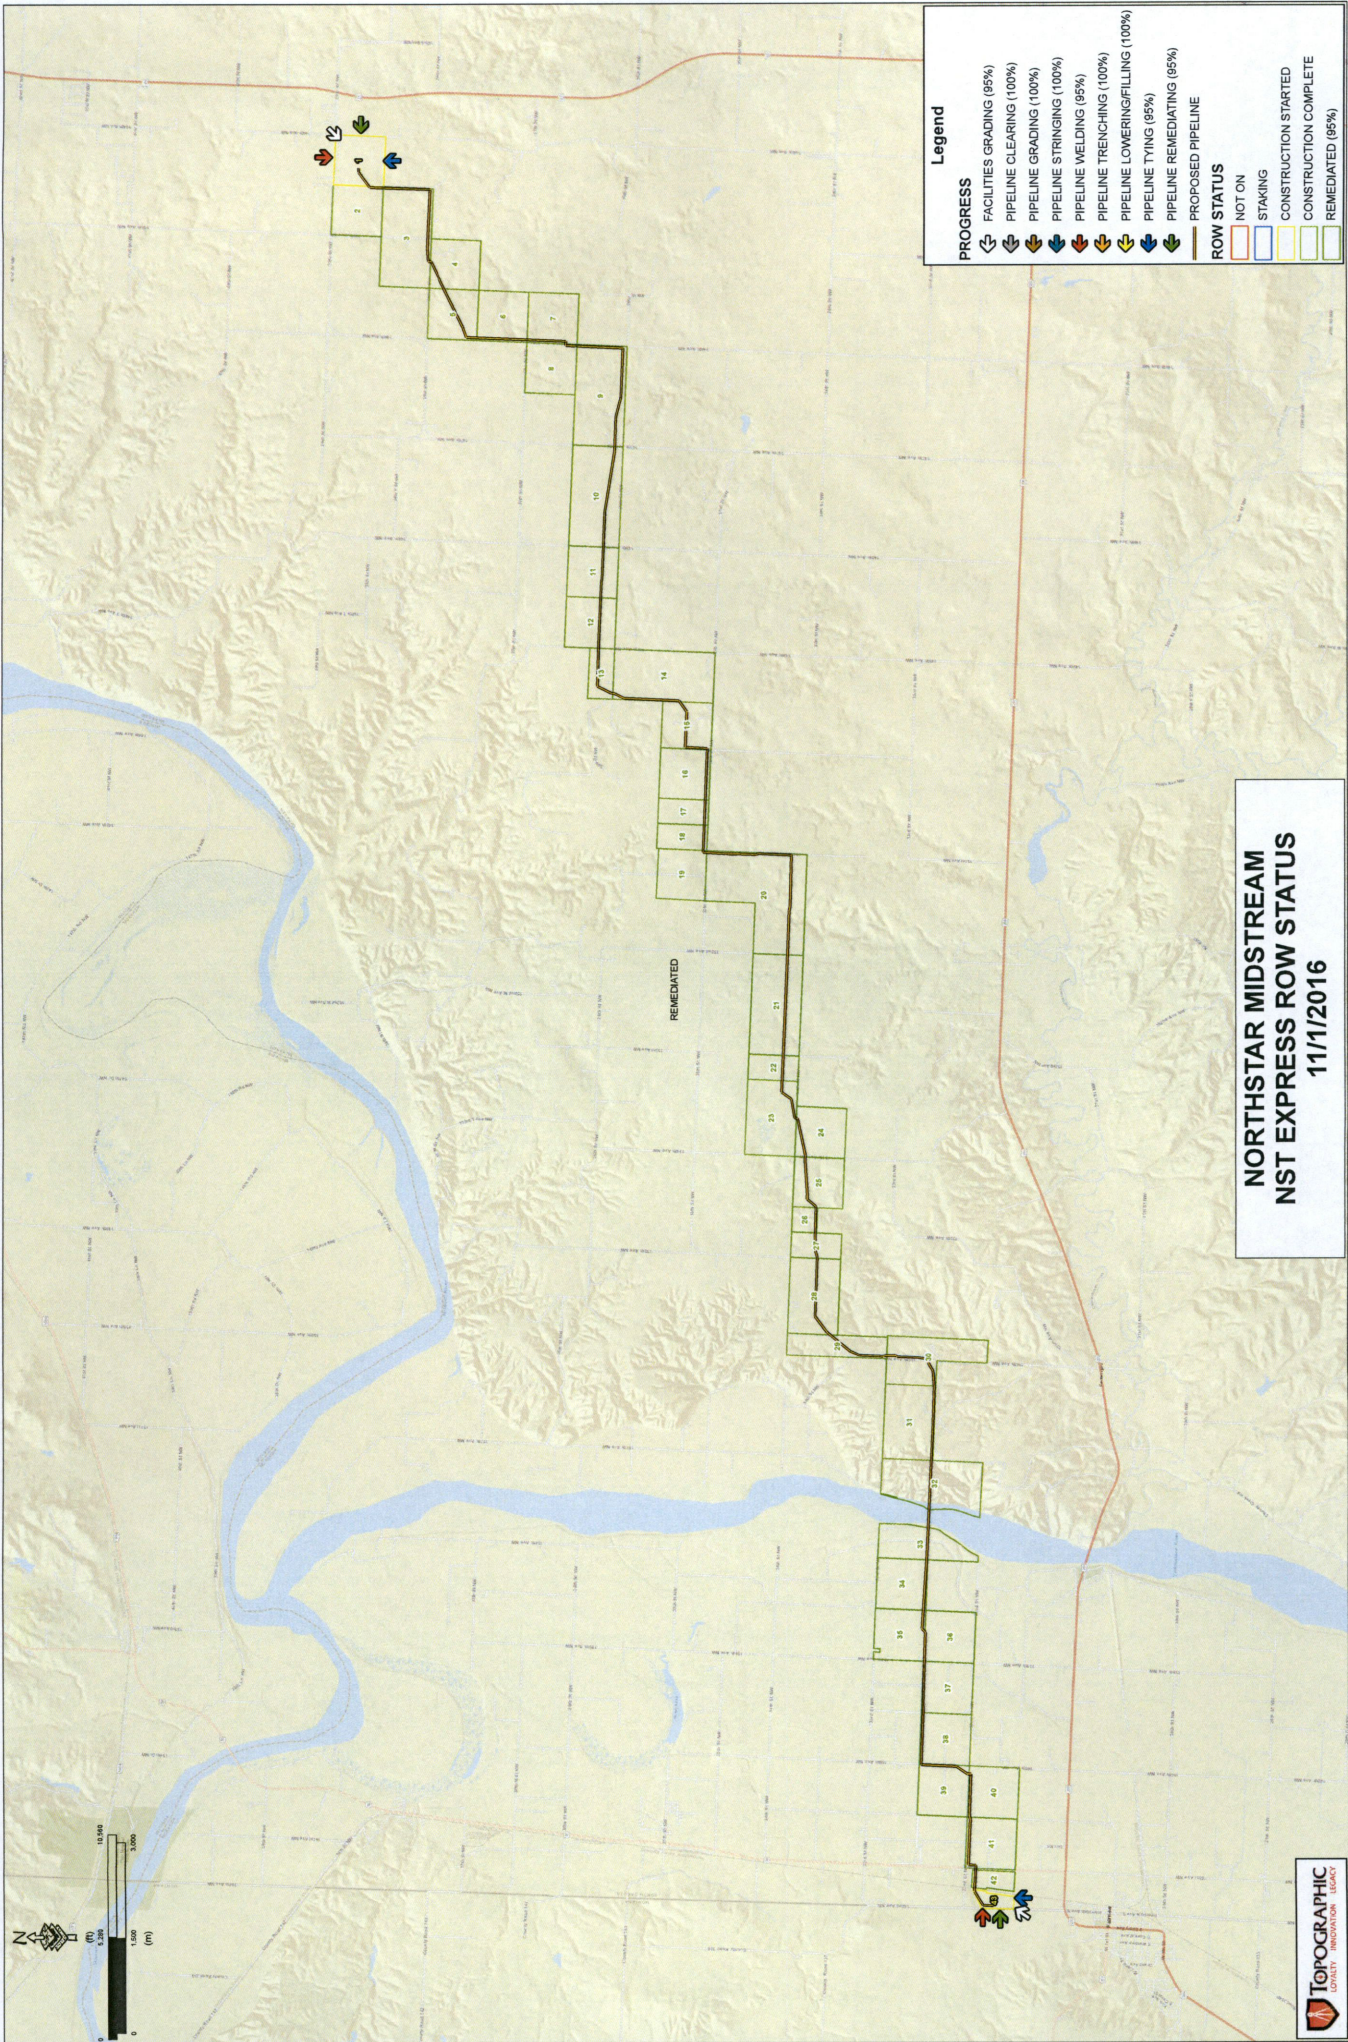

Legend

- PROGRESS**
- FACILITIES GRADING (95%)
 - PIPELINE CLEARING (100%)
 - PIPELINE GRADING (100%)
 - PIPELINE STRINGING (100%)
 - PIPELINE WELDING (95%)
 - PIPELINE TRENCHING (100%)
 - PIPELINE LOWERING/FILLING (100%)
 - PIPELINE TYING (95%)
 - PIPELINE REMEDIATING (95%)
- ROW STATUS**
- PROPOSED PIPELINE
 - NOT ON
 - STAKING
 - CONSTRUCTION STARTED
 - CONSTRUCTION COMPLETE
 - REMEDIATED (95%)

**NORTHSTAR MIDSTREAM
NST EXPRESS ROW STATUS
11/1/2016**

