

Hamre, John G.

From: Fahn, Patrick J.
Sent: Tuesday, December 01, 2009 1:51 PM
To: Hamre, John G.
Subject: FW: Enbridge Weekly Construction Update 11/19/09 to 11/25/09
Attachments: Enbridge Status Report 112609.pdf

John – please docket in 07-108 from Enbridge Energy and then forward to Commissioners, PU, and Legal

Patrick Fahn

Director-Compliance and Competitive Markets

Email: pfahn@nd.gov

Phone: (701) 328-4077

North Dakota Public Service Commission

600 E Boulevard

Bismarck ND 58505-0480

Fax: (701) 328-2410

From: Andrew Lane [<mailto:adlane@nrg-llc.com>]

Sent: Tuesday, December 01, 2009 12:13 PM

To: Fahn, Patrick J.

Cc: 'Paul Turner'; 'Jeffrey Wiklund'; 'Andrea Estevez'; 'Marc DeVarenes'; 'sally.joyce@enbridge.com'; 'claudia.schrull@enbridge.com'; 'thomas.hodge@enbridge.com'; Mandy Bohnenblust; Andrew Lane

Subject: Enbridge Weekly Construction Update 11/19/09 to 11/25/09

Mr. Fahn:

On behalf of Enbridge, in compliance with order number eight in the North Dakota Public Service Commission Finding of Fact, Conclusions of Law and Order issued December 31, 2007, please find attached the weekly update for construction of the Alberta Clipper Pipeline project in North Dakota. The update includes construction activities during the period of November 19 to November 25, 2009.

Please feel free to contact Paul Turner (715-398-4501) or me if you have any questions.

Regards,

Andy Lane

Andrew Lane


adlane@nrg-llc.com

(612) 349-4368 Direct

(612) 719-4379 Cell

(612) 347-6780 Fax

84 **PU-07-108** Filed: 12/1/2009 Pages: 7
Enbridge Pipeline Project Weekly Construction Update Nov. 19 to Nov. 25, 2009



ENBRIDGE™
ALBERTA CLIPPER PIPELINE PROJECT
WEEKLY CONSTRUCTION STATUS REPORT
November 19 to November 25, 2009

Construction Activity

Enbridge continued construction of the Alberta Clipper Pipeline Project in North Dakota between November 19 and November 25, 2009. Construction continued with the installation of pipe sections at road, wetland, and waterbody crossings, which are then tied-in to the adjacent mainline pipe sections. The rough and final cleanup crews continue to make progress throughout North Dakota. Other activities included stormwater inspections, the installation and replacement of erosion and sediment controls, bridge cleaning, and dewatering of the trench prior to pipe installation. Rough and final clean up activities will continue to make progress by removing timber mats, replacing topsoil, and applying dormant seed mixes as required by agencies and landowners. Compaction alleviation of agricultural areas is being completed as a part of final restoration activities. In addition, crews are stabilizing the right-of-way in preparation for frozen conditions.

Additionally, the following work was also been completed to date:

- Clearing: 28.0 miles completed
- Grading: 28.0 miles completed
- Stringing: 28.0 miles completed
- Welding: 28.0 miles completed
- Trenching 28.0 miles completed
- Lowering-in 28.0 miles completed
- Backfill 28.0 miles completed
- Rough Cleanup 24.2 miles completed
- Final Cleanup 24.2 miles completed

Photographs of construction activities in North Dakota area attached.


Wetland Restoration



Decompaction of subsoil on right-of-way




Waterbody with erosion control devices in place and functioning

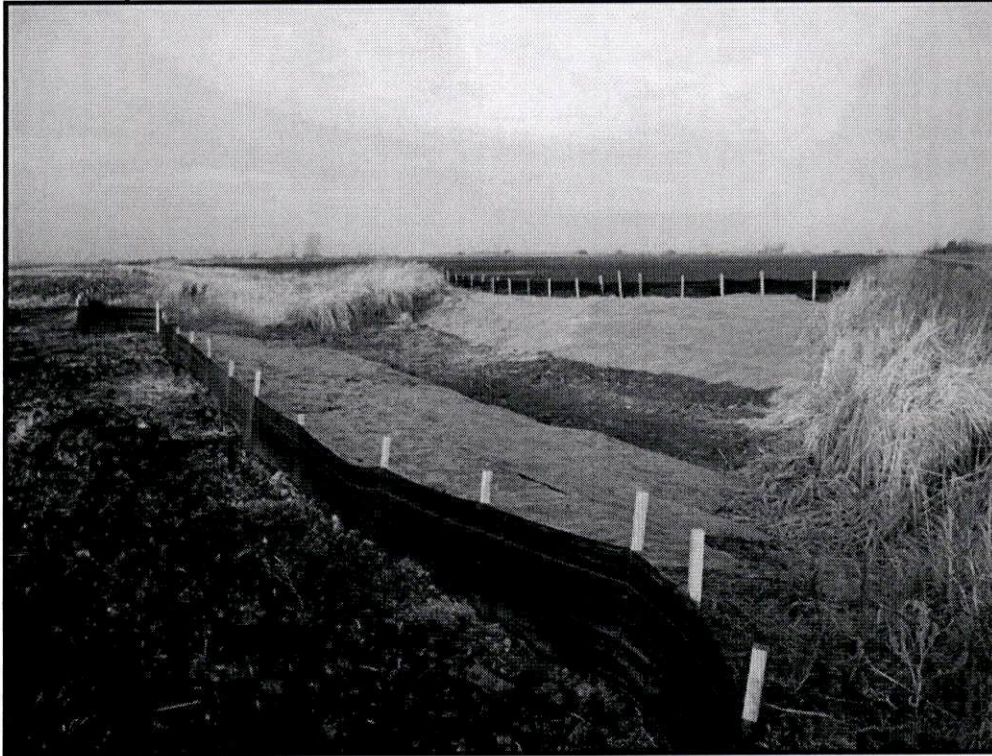

Restored right-of-way after decompaction and topsoil discing



Crews stabilizing ditch

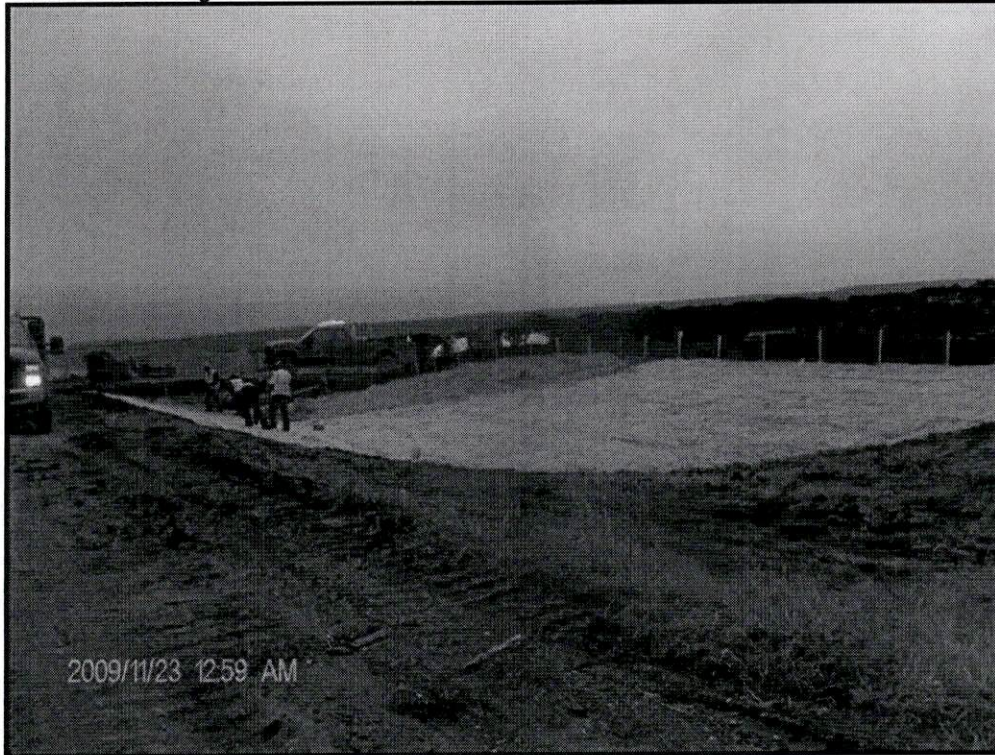


Stabilized waterbody



Tie-in location at road crossing



Bank Stabilization at Tongue River Cut-Off (s-783a)

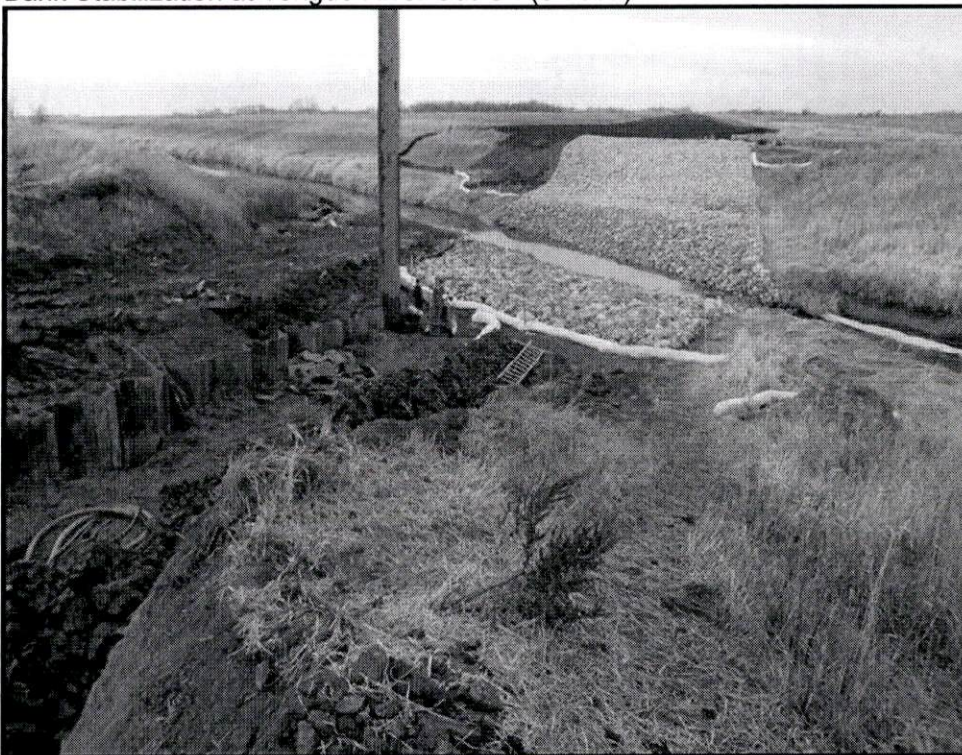

Agency Consultations

The North Dakota Department of Health will be updated on November 30, 2009 regarding pipeline construction related spills.

Upcoming Activities

The following activities are scheduled for the next reporting period:

- Continuation of road bore, wetland, and waterbody crossings;
- Continuation of stormwater inspections;
- Preparing the right-of-way for winter construction;
- Preparing and hydrostatically testing the mainline section;
- Continuation of rough and final clean-up activities; and
- Continuation of restoration activities.
