



Weekly Construction Progress Report

Case # **PU-12-40**

Project: Nelson to Ross

Week Ending: 7/9/2012

Report # 2

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	
Project Coordinator	Terry Wainwright	PPI	501-940-0672	
Contractor Spread	Ron Marsh	Pro-Pipe	406-239-0996	
Brief Description of Week's Activities				
Grading RoW, Building Fences, working on ECD's, Silt Fence, Waddles, Flume pipe. Stringing B-pipe				
Removed 9 Green Ash Tress @ stations 248+50, due to land owners request for equipment				
access from field to field & replanting will take place in a different location on his property at a ratio				
of 2 to 1.				
Project Completion Spread				
Description	Week Complete	% Week Complete	Total Complete	% Total Complete
Clear & Grade lft.	16,200'		25,200'	28%
ROW Finished lft.				
Stringing B/P	1,788'		1,788'	0.01.5
Welding	n/a			
Ditching	n/a			
Lowering In	n/a			
Backfill	n/a			
Clean-up	n/a			
Coating (Welds)	n/a			
ECDs Installed	n/a			
Silt Fence lft.	4,232'	n/a	4,232'	4,232'
Hay bales ea.	n/a	n/a		n/a
Mats ea.	64ea	n/a	93ea	93ea
Waddles ea.	72ea	n/a	72ea	72ea
Project construction / reclamation activities				
Description	Week Complete	% Week Complete	Total Complete	% Total Complete
Roadway / Bores ea.	n/a	n/a		n/a
Erosion / Sediment	n/a	n/a		n/a
Topsoil	n/a	n/a		n/a
Restoration/Cleanup	n/a	n/a		n/a
Roadway Restoration	n/a	n/a		n/a
Fence / Gate	n/a	n/a		n/a
Fertilizing / Seeding	n/a	n/a		n/a
Project Site Safety				
On Staff personal, we are acting as Safety, working together & good communication to head off any				
safety concerns				

Signature: _____

Date: _____

Terry Wainwright 7-9-2012



PLAINS
ALL AMERICAN
PIPELINE, L.P.

Weekly Construction Progress Report

Case # PU-12-40 Report # 2
Project: Nelson to Ross
Week Ending: 7/9/2012

Dates of construction	Startup	Shutdown
	6/15/2012	

Temperature high and low for week.	High	Low
	°86	°62

Landowner / Public Concerns	Addressing Individual	Phone
none		

Suspension of project activities (when, where, why ,how long)

On 06-26-2012/ Between 86th st & 87th st/ Due to Piping Plover Bird/Until we here from the USACE & USFWS/No Change

Identify Cultural Resources not previously identified.

n/a

Critical Habitat or Threatened or Endangered Species.


All proper authorities have been notified, & are waiting on response, all area's of concern has been taped off on count of Piping Plover, main areas of interest seems to be between 86th & 87th.

No Change.

Cathodic Protection Installed	When	Where
n/a		

Special Coordination	Who	When
n/a		

Pipeline in-service date	Date
n/a	

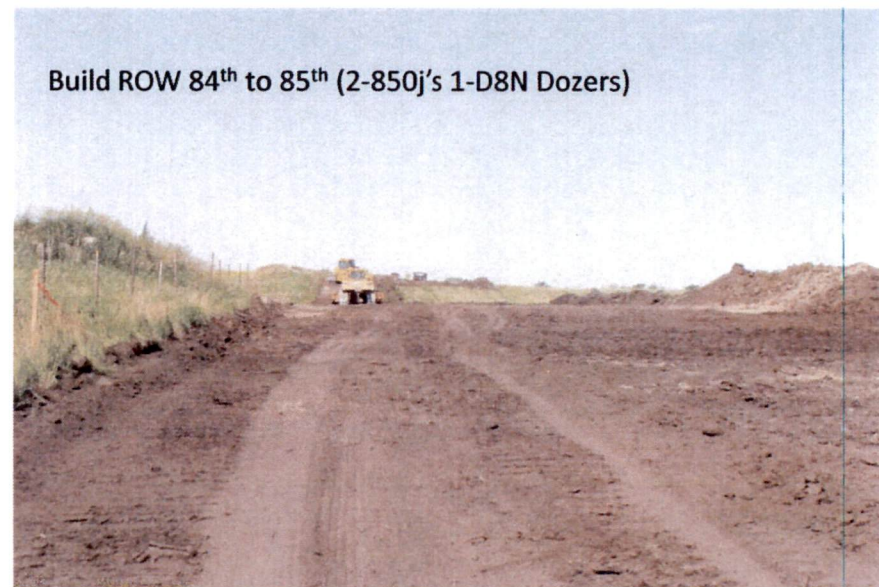

Date: 7-3-12
STA# 200+00
AFE# 15765



Contractor installed an additional 220 ft of silt fencing.
