



Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: Sunny



High: 73°F Low: 44°F

Winds: WSW 5-15 MPH

Precipitation: 20%chance

Monday, September 26th, 2005



97 Days to Completion

FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

♦Safety/Environmental:

- ♦ Next All Hands safety meeting Wednesday, September 28th, 2005 at 7:00 am.
- ♦ No injuries to date.

♦General:

- ♦ Electrical poles were due 9/23/05, are being tracked.
- ♦ Receiving substation and electrical materials, breaker due in today.

♦Road Construction

- ♦ Road construction from #3-#6 continues, and #13-#17 continues.
- ♦ 52nd St fabric and gravel continues.

♦ Foundation Construction:

- ♦ Setting inner can and backfill at #27.
- ♦ Pouring #28 started this morning.
- ♦ Pre Dig #4 and #5.

♦ Electrical Construction:

- ♦ Grounding crews right behind foundation crews.
- ♦ Capital Electric underground into laydown yard complete.
- ♦ Poured contaminate base, forming contaminate walls.

♦Tower Erection: Erection Days Lost for High Winds: 0

- ♦ Not Started

♦Mechanical Completion:

- ♦ Not Started

♦Commissioning:


- ♦ Not Started

♦WAPA Interconnect:

- ♦ Not started

RECEIVING			
	Today	Total Received	Remaining
Bases	0	0	33
Mids	0	0	33
Tops	0	0	33
Nacelles	0	0	33
Controllers	0	0	33
Blades	0	0	33
Transformers	0	0	33
Hubs	0	0	33
4/0 Cable	0	150,148	0
1000 MCM	0	7,245	0

General Information & Announcements

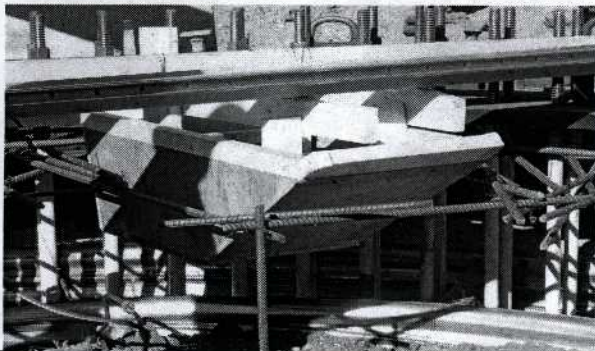

	Complete	Remaining	% complete
Roads Built	12,390	24,764	33.4%
Foundations completed & backfilled	1	32	3.0%
Tower Base sections installed	0	33	0.0%
Tower Mid sections installed	0	33	0.0%
Tower top sections installed	0	33	0.0%
Nacelles Installed	0	33	0.0%
Rotors installed	0	33	0.0%
Mechanically completed	0	33	0.0%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	0	49,291	0.0%
Trenching for 1000MCM cable (ft)	0	2,415	0.0%
Transformers Set/Terminated	0	33	0.0%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE.
