

Burleigh County Wind, LLC; Wilton, ND

Plan of the Day (POD)

Weather Forecast: Cloudy  High: 40°F Low: 28°F
 Winds: NNW 5-10 MPH Precipitation: 20%

Monday, November 21th, 2005



FPL Energy

41 Days to Completion

6 Days to SWPP Inspection


FPL Energy Par Golf Wanzek GE Aerial Contractors Ventus

Activities:

- ♦ **Safety/Environmental:**
 - ♦ Daily Safety meeting was held at Construction Trailer.
 - ♦ No injuries to date.
- ♦ **General:**
 - ♦ Next Management meeting Wednesday, November 30th, 2005 at 9:00 am.
- ♦ **Foundation Construction:**
 - ♦ Complete
- ♦ **Electrical Construction:**
 - ♦ Fiber Optic terminations/splices start today.
 - ♦ Installing substation fence.
 - ♦ Erecting substation buss, pulling and terminating control wiring.
 - ♦ OPGW installation is on hold for parts.
 - ♦ Pad Mount Xfmr terminations continues.
- ♦ **Tower Erection: Erection Days Lost for High Winds: 6**
 - ♦ Stack out #23 as winds allow, winds currently greater than 20 MPH.
 - ♦ Setting bases and mids as they arrive.
- ♦ **Mechanical Completion:**
 - ♦ Working #25 -#27 cable drops.
- ♦ **Commissioning:**
 - ♦ GE lead and one tech here on Monday.
- ♦ **WAPA Interconnect:**
 - ♦ Interconnect installation continues.

RECEIVING			
	Weekend	Total Received	Remaining
Bases	4	15	18
Mids	4	15	18
Tops	4	15	18
Nacelles	1	25	8
Controllers	0	33	0
Blades	3	18	15
Transformers	0	33	0
Hubs	2	31	2
4/0 Cable	0	147,874	0
1000 MCM	0	2,415	0

General Information & Announcements

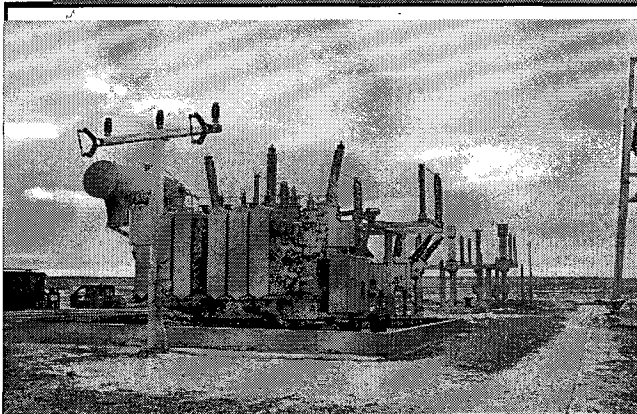

	Complete	Remaining	% complete
Roads Built	37,154	0	100.0%
Foundations completed & backfilled	33	0	100.0%
Tower Base sections installed	13	20	39.4%
Tower Mid sections installed	11	22	33.3%
Tower top sections installed	7	26	21.2%
Nacelles Installed	7	26	21.2%
Rotors installed	6	27	18.2%
Mechanically completed	2	31	6.1%
Pre-Commissioned	0	33	0.0%
Final Commissioned	0	33	0.0%
Trenching for 4/0 cable (ft)	49,291	0	100.0%
Trenching for 1000MCM cable (ft)	500	0	100.0%
Transformers Set/Terminated	29	4	87.9%

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLe.
