



**ENBRIDGE™**  
**ALBERTA CLIPPER PIPELINE PROJECT**  
**WEEKLY CONSTRUCTION STATUS REPORT**  
**October 29, 2009 to November 4, 2009**

### **Construction Activity**


Enbridge continued construction of the Alberta Clipper Pipeline Project in North Dakota between October 29 and November 4, 2009. Construction of the large pipe sections have been installed and backfilled in North Dakota. Construction continued with the installation of sections of pipe at road, wetland, and waterbody crossings, which are then tied-in to the adjacent mainline pipe sections. All horizontal directional drills have been completed in North Dakota, as the pipe section under the Red River of the North was completed during this time period. The rough and final cleanup crews continue to make significant progress throughout North Dakota. Other activities included the installation and replacement of erosion and sediment controls, bridge cleaning, and dewatering. Rough clean up will continue to make progress by removing timber mats, replacing topsoil, and applying dormant seed. Compaction alleviation of agricultural areas is being completed as a part of final restoration activities.

Additionally, the following work was also been completed to date:


- Clearing: 28.0 miles completed
- Grading: 28.0 miles completed
- Stringing: 28.0 miles completed
- Welding: 28.0 miles completed
- Trenching 28.0 miles completed
- Lowering-in 28.0 miles completed
- Backfill 28.0 miles completed
- Rough Cleanup 14.6 miles completed
- Final Cleanup 14.6 miles completed

Photographs of construction activities in North Dakota area attached.

Properly separated soils adjacent to a waterbody crossing

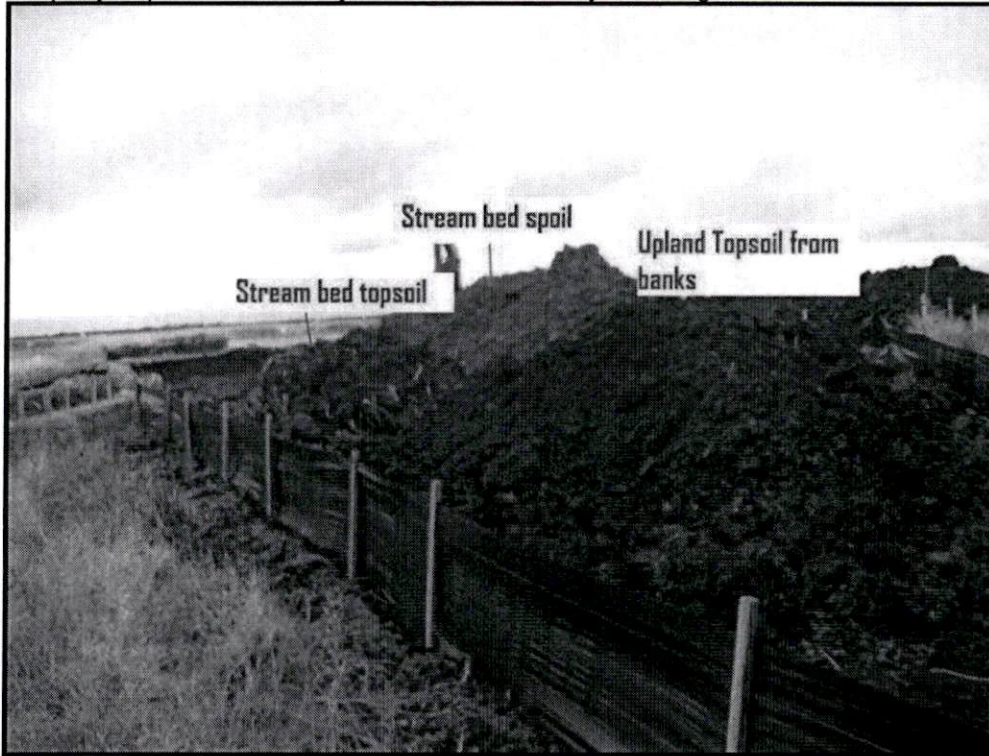

Bank stabilization following a waterbody crossing

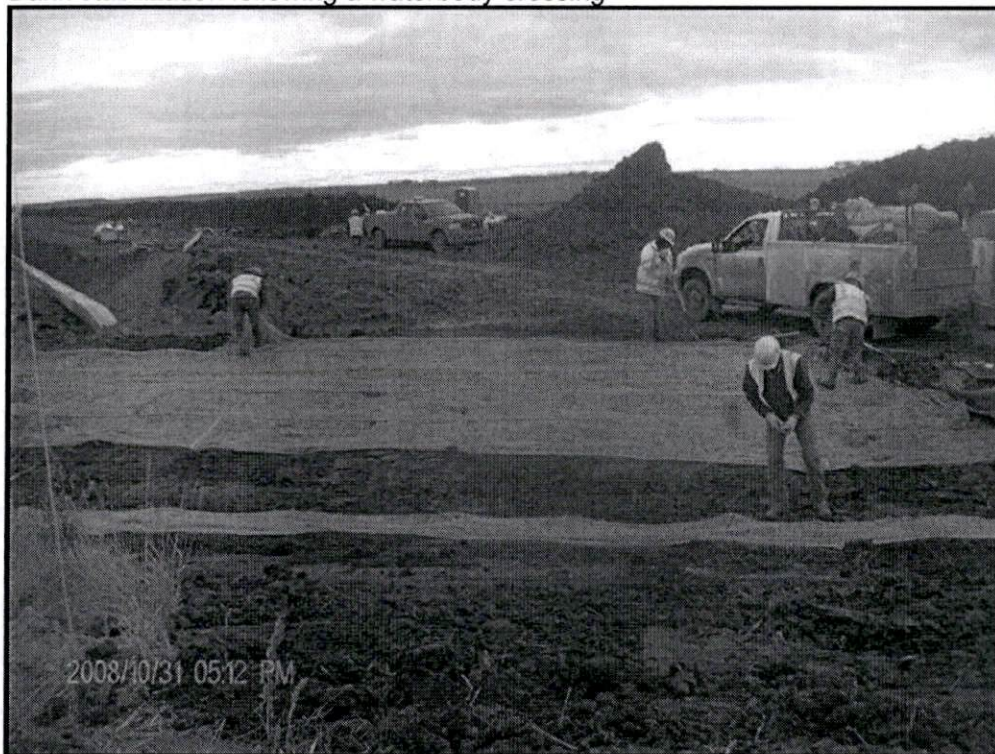

Tie-in crew installing at a waterbody crossing



Trench box removal following completion of road bore crossing



Timber mat removal during rough cleanup in wetland



Bridge over waterbody with ECDs in place and functioning properly



## **Agency Consultations**

The North Dakota Department of Health was updated on October 29, 2009 regarding pipeline construction related spills.

## **Upcoming Activities**

The following activities are scheduled for the next reporting period:

- Continue road bore, wetland, and waterbody crossings;
- Continuation of rough and final clean-up activities; and
- Continuation of restoration activities.
