




# NextEra™ Energy Resources Ashtabula Wind II

## Otter Tail

### Plan of the Day (POD)



**Date: Monday, 7/27/2009**  
**High: 82**  
**Precipitation Chances: 40%**

**COD: 10-15-09**  
**Low: 50**

**Days to COD: 81**  
**Winds: NW @ 10 mph**  
**Weather Forecast: Partly Sunny**

**NextEra™ Energy Resources      Otter Tail      Blattner Energy      GE**

**Safety/Environmental:**

- The corn stalk is beginning to impair vision, be cautious at intersections
- Make sure not to use any equipment if it is tagged out
- Keep your speed to a minimum
- SWPPP inspection every two weeks

**Civil/Erection:**

- Offload nacelle & blades

**Erection:**

- Erect base & mid at 136
- Assemble rotor at 136
- Erect top, nacelle & rotor at 133

**Collections:**

- Trench & cable install -500 the north home runs

**Electrical:**


- Grounding grid testing
- Controller termination at 145-148
- Install box pad at 147-154
- Low voltage cable termination install wire at 145 & 158

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	0	33
Grounding XFR	3	0	3
4/0 Cable	189,000	129,912	59,088
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	6	27
Controllers	33	8	25
Bases	33	5	28
Mids	33	5	28
Tops	33	5	28
Nacelles	33	6	27
Hubs	33	10	23
Blade Sets	33	5	28

**Negative Number Indicates Overage of Cable**

### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	29	33	87.9%
Crane Pads Completed	29	33	87.9%
Tower Base Sections Erected	4	33	12.1%
Tower Mid Sections Erected	4	33	12.1%
Tower Top Sections Erected	1	33	3.0%
Nacelles Installed	1	33	3.0%
Rotors Installed	0	33	0.0%
Tower Wiring Complete	0	33	0.0%
Mechanically Complete	0	33	0.0%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	35,455	189,000	18.8%
500 Cable Trenched	17,295	117,000	14.8%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set/Terminated	15	33	45.5%
(as of COB yesterday)			

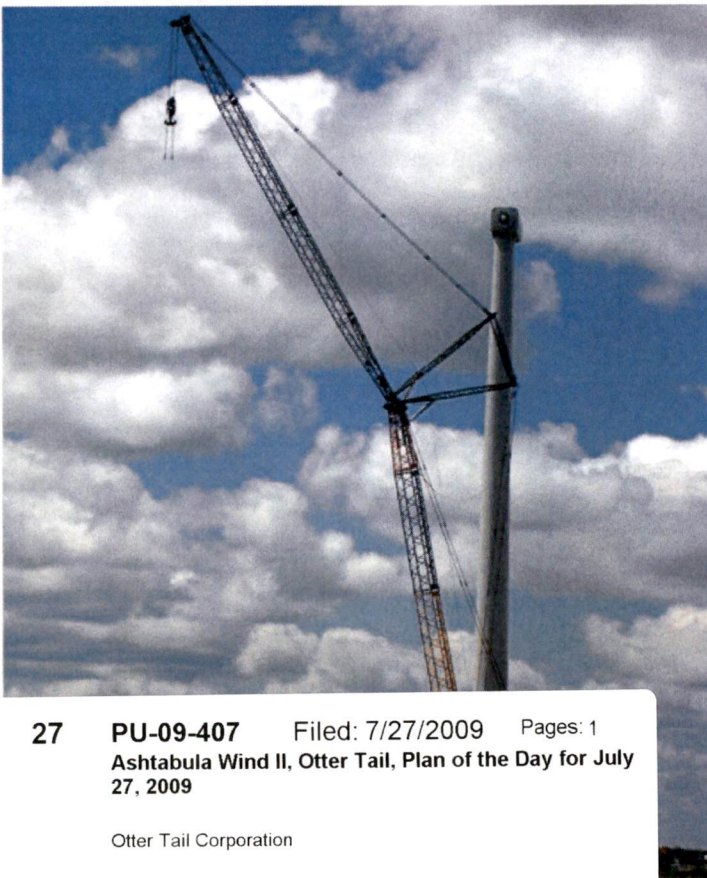

27 PU-09-407 Filed: 7/27/2009 Pages: 1  
 Ashtabula Wind II, Otter Tail, Plan of the Day for July 27, 2009

Otter Tail Corporation
