




NextEra™ Energy Resources Ashtabula Wind II

Otter Tail

Plan of the Day (POD)



Date: Tuesday, 7/28/2009
High: 76
Precipitation Chances: 0%

COD: 10-15-09
Low: 47

Days to COD: 80
Winds: WNW @ 7 mph
Weather Forecast: Mostly Sunny

NextEra™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- The corn stalk is beginning to impair vision, be cautious at intersections
- Make sure not to use any equipment if it is tagged out
- Keep your speed to a minimum
- SWPPP inspection every two weeks

Civil/Erection:

- Offload tower sections, nacelle, hubs & blades

Erection:

- Erect base & mid at 137
- Assemble rotor at 136 & 137
- Erect top, nacelle & rotor at 133

Collections:

- Trench & cable install -500 the north home runs

Electrical:


- Cable splicing 3-500
- High voltage cable termination at 143 & 159
- Low voltage cable termination at 139-141

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	0	33
Grounding XFR	3	0	3
4/0 Cable	189,000	129,912	59,088
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	6	27
Controllers	33	20	13
Bases	33	7	26
Mids	33	7	26
Tops	33	7	26
Nacelles	33	11	22
Hubs	33	12	21
Blade Sets	33	7	26

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	29	33	87.9%
Crane Pads Completed	29	33	87.9%
Tower Base Sections Erected	5	33	15.2%
Tower Mid Sections Erected	5	33	15.2%
Tower Top Sections Erected	2	33	6.1%
Nacelles Installed	1	33	3.0%
Rotors Installed	1	33	3.0%
Tower Wiring Complete	0	33	0.0%
Mechanically Complete	0	33	0.0%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	35,455	189,000	18.8%
500 Cable Trenched	21137	117,000	18.1%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set/Terminated	25	33	75.8%
(as of COB yesterday)			

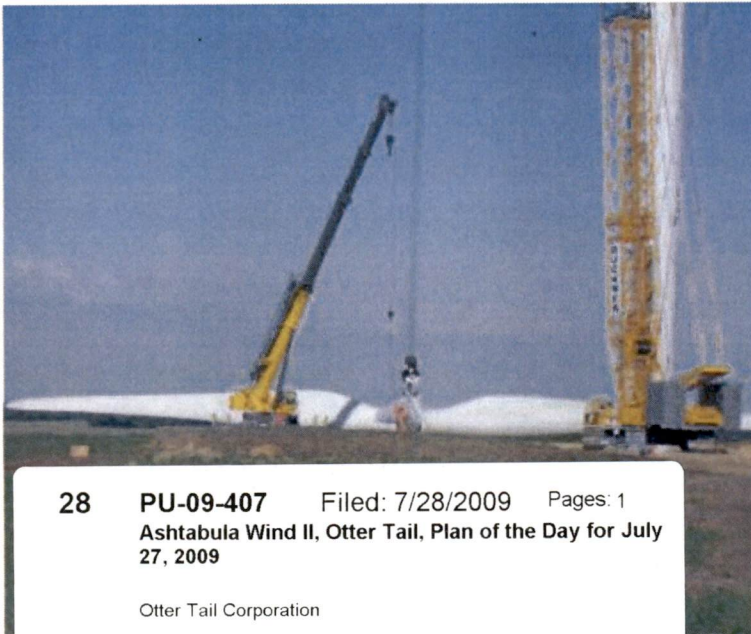

28 PU-09-407 Filed: 7/28/2009 Pages: 1
 Ashtabula Wind II, Otter Tail, Plan of the Day for July 27, 2009

Otter Tail Corporation
