




NextEra™ Energy Resources Ashtabula Wind II



Otter Tail

Plan of the Day (POD)

Date: Thursday, 7/30/2009
High: 71
Precipitation Chances: 45%

COD: 10-15-09
Low: 50

Days to COD: 78
Winds: NW @ 8 mph
Weather Forecast: Mostly Cloudy

NextEra™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Roads are wet today, watch speeds & be cautious of wildlife
- Make sure not to use any equipment if it is tagged out
- Keep your speed to a minimum
- SWPPP inspection every two weeks

Civil/Erection:

- Offload tower sections, nacelles, hubs & blades

Erection:

- Erect base & mid at 141
- Erect top, nacelle & rotor at 136 & 137

Collections:

- Trench & cable install -500 the north home runs

Electrical:


- Controller termination pulling cable at 159-161
- Low voltage cable termination at 139-141
- Mechanical completion pre-walk at 132 & 133

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	0	33
Grounding XFR	3	0	3
4/0 Cable	189,000	129,912	59,088
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	33	0
Controllers	33	20	13
Bases	33	13	20
Mids	33	13	20
Tops	33	13	20
Nacelles	33	13	20
Hubs	33	14	19
Blade Sets	33	11	22

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	29	33	87.9%
Crane Pads Completed	29	33	87.9%
Tower Base Sections Erected	8	33	24.2%
Tower Mid Sections Erected	8	33	24.2%
Tower Top Sections Erected	4	33	12.1%
Nacelles Installed	4	33	12.1%
Rotors Installed	4	33	12.1%
Tower Wiring Complete	0	33	0.0%
Mechanically Complete	0	33	0.0%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	35,455	189,000	18.8%
500 Cable Trenched	21137	117,000	18.1%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set	25	33	75.8%
(as of COB yesterday)			

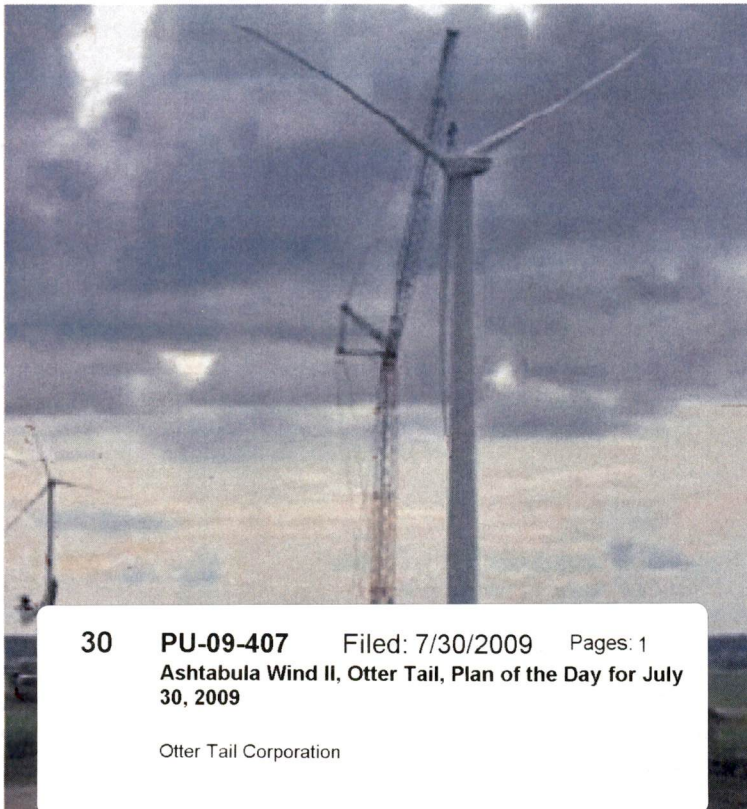

30 PU-09-407 Filed: 7/30/2009 Pages: 1
 Ashtabula Wind II, Otter Tail, Plan of the Day for July 30, 2009

Otter Tail Corporation
