




# NEXtera™ Energy Resources Ashtabula Wind II

## Otter Tail

### Plan of the Day (POD)



**Date:** Saturday, 8/8/2009  
**High:** 78  
**Precipitation Chances:** 55%

**COD:** 10-15-09  
**Low:** 57

**Days to COD:** 69  
**Winds:** NNE @ 3 mph  
**Weather Forecast:** Cloudy

**NEXtera™ Energy Resources    Otter Tail    Blattner Energy    GE**

**Safety/Environmental:**

- Drive cautiously, keep headlights must be on
- Keep your speed to a minimum
- Watch out for blind corners in areas where corn is growing
- SWPPP inspection every two weeks
- Crane walk paths

**Civil/Erection:**

**Erection:**

- Erect base & mid at 158
- Assemble rotor at 144 & 145
- Erect top nacelle & rotor at 144 & 145

**Collections:**

- Low voltage cable termination at 139, 141 & 142
- High voltage termination at substation

**Electrical:**


- Controller termination at 160-162

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	0	33
Grounding XFR	3	0	3
4/0 Cable	189,000	195,397	-6,397
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	33	0
Controllers	33	28	5
Bases	33	25	8
Mids	33	25	8
Tops	33	25	8
Nacelles	33	24	9
Hubs	33	25	8
Blade Sets	33	25	8

Negative Number Indicates Overage of Cable

### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	33	33	100.0%
Crane Pads Completed	33	33	100.0%
Tower Base Sections Erected	15	33	45.5%
Tower Mid Sections Erected	15	33	45.5%
Tower Top Sections Erected	12	33	36.4%
Nacelles Installed	12	33	36.4%
Rotors Installed	12	33	36.4%
Tower Wiring Complete	9	33	27.3%
Mechanically Complete	2	33	6.1%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	177,605	189,000	94.0%
500 Cable Trenched	100,122	117,000	85.6%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set	33	33	100.0%
(as of COB yesterday)			

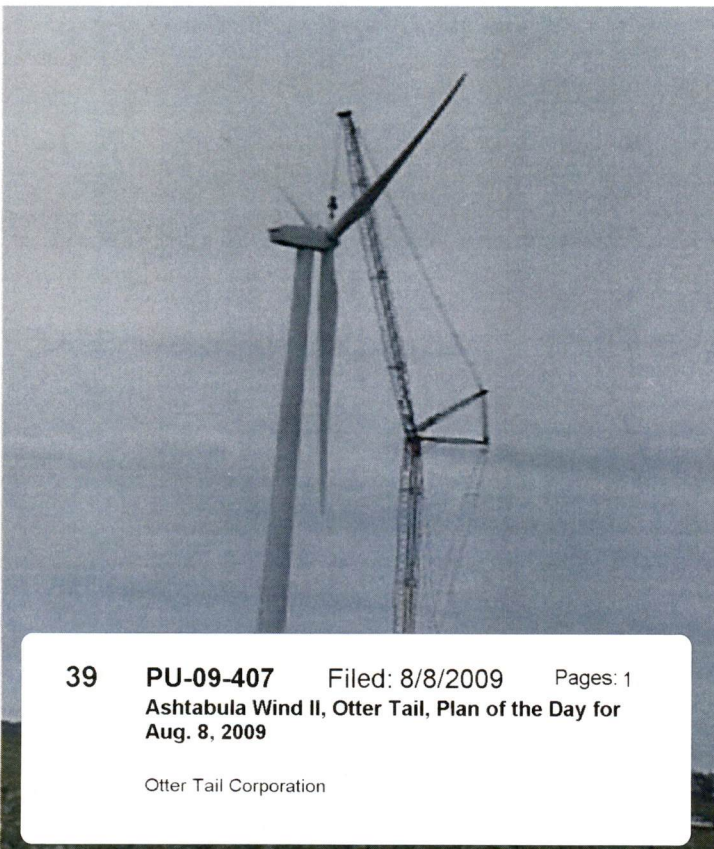

39    PU-09-407    Filed: 8/8/2009    Pages: 1  
 Ashtabula Wind II, Otter Tail, Plan of the Day for  
 Aug. 8, 2009

Otter Tail Corporation
