




# NEXtera™ Energy Resources Ashtabula Wind II



## Otter Tail

### Plan of the Day (POD)

**Date: Monday, 8/10/2009**  
**High: 83**  
**Precipitation Chances: 0%**

**COD: 10-15-09**  
**Low: 55**

**Days to COD: 67**  
**Winds: WSW @ 3 mph**  
**Weather Forecast: Sunny**

**NEXtera™ Energy Resources    Otter Tail    Blattner Energy    GE**

#### Safety/Environmental:

- Drive cautiously, keep headlights must be on
- Keep your speed to a minimum
- Watch out for blind corners in areas where corn is growing
- SWPPP inspection every two weeks
- Crane walk paths

#### Erection:

- Erect base & mid at 163-164
- Assemble rotor at 163-164
- Erect top nacelle & rotor at 145-146

#### Collections:

- Low voltage cable termination at 146, 162 & 163
- High voltage termination at 153-154

#### Electrical:


- Tower wiring at 143
- Mechanical completion Pre-walk at 137-138
- Mechanical completion walk down at 140 & 142
- Controller termination at 151-152

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	0	33
Grounding XFR	3	0	3
4/0 Cable	189,000	195,397	-6,397
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	33	0
Controllers	33	28	5
Bases	33	25	8
Mids	33	25	8
Tops	33	25	8
Nacelles	33	24	9
Hubs	33	25	8
Blade Sets	33	25	8

Negative Number Indicates Overage of Cable

#### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	33	33	100.0%
Crane Pads Completed	33	33	100.0%
Tower Base Sections Erected	16	33	48.5%
Tower Mid Sections Erected	16	33	48.5%
Tower Top Sections Erected	14	33	42.4%
Nacelles Installed	14	33	42.4%
Rotors Installed	13	33	39.4%
Tower Wiring Complete	9	33	27.3%
Mechanically Complete	2	33	6.1%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	177,605	189,000	94.0%
500 Cable Trenched	100,122	117,000	85.6%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set	33	33	100.0%
(as of COB yesterday)			

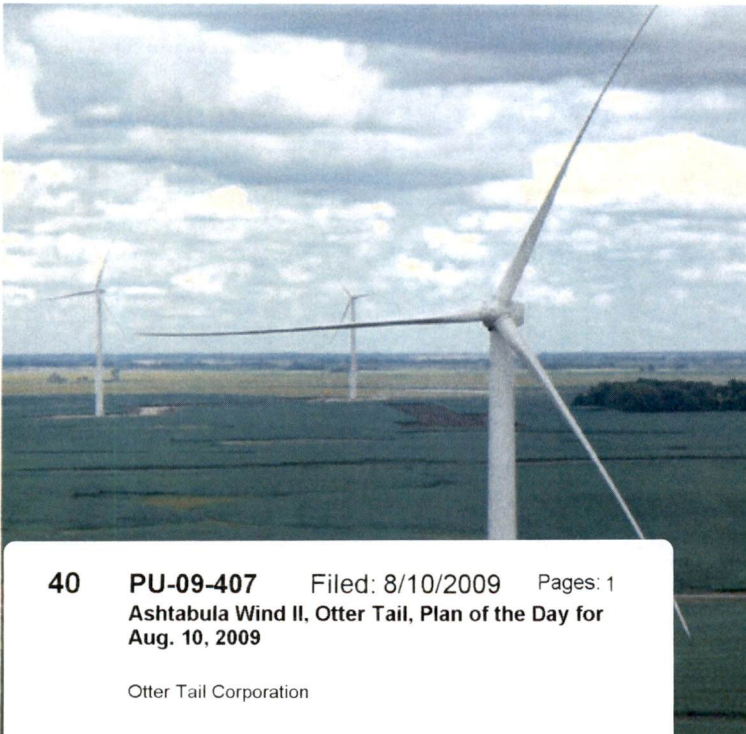

40    PU-09-407    Filed: 8/10/2009    Pages: 1  
 Ashtabula Wind II, Otter Tail, Plan of the Day for  
 Aug. 10, 2009

Otter Tail Corporation
