




# NEXTer<sup>TM</sup> Energy Resources Ashtabula Wind II



## Otter Tail

### Plan of the Day (POD)

**Date:** Tuesday, 8/11/2009  
**High:** 91  
**Precipitation Chances:** 0%

**COD:** 10-15-09  
**Low:** 57

**Days to COD:** 66  
**Winds:** S @ 3 mph  
**Weather Forecast:** Sunny

## NEXTer<sup>TM</sup> Energy Resources    Otter Tail    Blattner Energy    GE

#### Safety/Environmental:

- Keep hydrated
- Keep your speed to a minimum
- Watch out for blind corners in areas where corn is growing
- SWPPP inspection every two weeks

#### Erection:

- Offloading tower sections, nacelle, hub & blades
- Erect base & mid at 161-162
- Assemble rotor at 161-162
- Erect top nacelle & rotor – moving to 158

#### Collections:

- Low voltage cable termination at 159-161
- High voltage termination at 152-153

#### Electrical:

- Tower wiring at 144-145 & 196-197
- Mechanical completion walk down at 138 & 195
- Controller termination at 149-150


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	0	33
Grounding XFR	3	0	3
4/0 Cable	189,000	195,397	-6,397
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	33	0
Controllers	33	33	0
Bases	33	27	6
Mids	33	26	7
Tops	33	27	6
Nacelles	33	30	3
Hubs	33	30	3
Blade Sets	33	27	6

Negative Number Indicates Overage of Cable

### General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	33	33	100.0%
Crane Pads Completed	33	33	100.0%
Tower Base Sections Erected	18	33	54.5%
Tower Mid Sections Erected	18	33	54.5%
Tower Top Sections Erected	15	33	45.5%
Nacelles Installed	15	33	45.5%
Rotors Installed	15	33	45.5%
Tower Wiring Complete	12	33	36.4%
Mechanically Complete	4	33	12.1%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	179,188	189,000	94.8%
500 Cable Trenched	100,122	117,000	85.6%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set	33	33	100.0%

(as of COB yesterday)

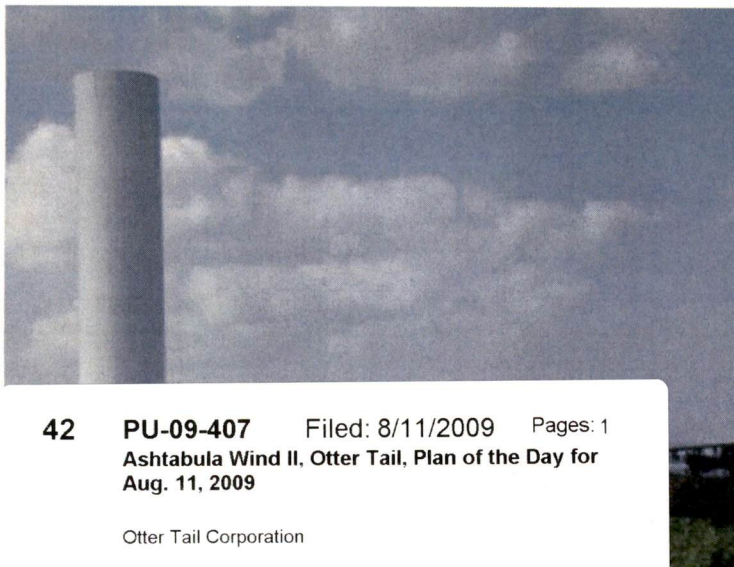

42    PU-09-407    Filed: 8/11/2009    Pages: 1  
 Ashtabula Wind II, Otter Tail, Plan of the Day for  
 Aug. 11, 2009

Otter Tail Corporation
