




NEXtera™ Energy Resources Ashtabula Wind II



Otter Tail

Plan of the Day (POD)

Date: **Wednesday, 8/12/2009**
 High: **95**
 Precipitation Chances: **0%**

COD: **10-15-09**
 Low: **59**

Days to COD: **65**
 Winds: **SSW @ 7 mph**
 Weather Forecast: **Sunny**

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- **Keep hydrated**
- **Keep your speed to a minimum**
- **Watch out for blind corners in areas where corn is growing**
- **SWPPP inspection every two weeks**

Erection:

- **Offloading tower sections, nacelle, hub & blades**
- **Erect base & mid at 159-160**
- **Assemble rotor at 159-160**
- **Erect top nacelle & rotor at 158**

Collections:

- **Low voltage cable termination at 159-161**
- **High voltage termination at 152-153**

Electrical:

- **Controller termination at 149-150**
- **Tower wiring at 145-146**
- **Mechanical completion walk down at 144-146**
- **IIP at 139**


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	0	33
Grounding XFR	3	0	3
4/0 Cable	189,000	195,397	-6,397
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	33	0
Controllers	33	33	0
Bases	33	27	6
Mids	33	26	7
Tops	33	27	6
Nacelles	33	30	3
Hubs	33	30	3
Blade Sets	33	27	6

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	33	33	100.0%
Crane Pads Completed	33	33	100.0%
Tower Base Sections Erected	20	33	60.6%
Tower Mid Sections Erected	20	33	60.6%
Tower Top Sections Erected	15	33	45.5%
Nacelles Installed	15	33	45.5%
Rotors Installed	15	33	45.5%
Tower Wiring Complete	13	33	39.4%
Mechanically Complete	4	33	12.1%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	179,188	189,000	94.8%
500 Cable Trenched	100,122	117,000	85.6%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set	33	33	100.0%

(as of COB yesterday)

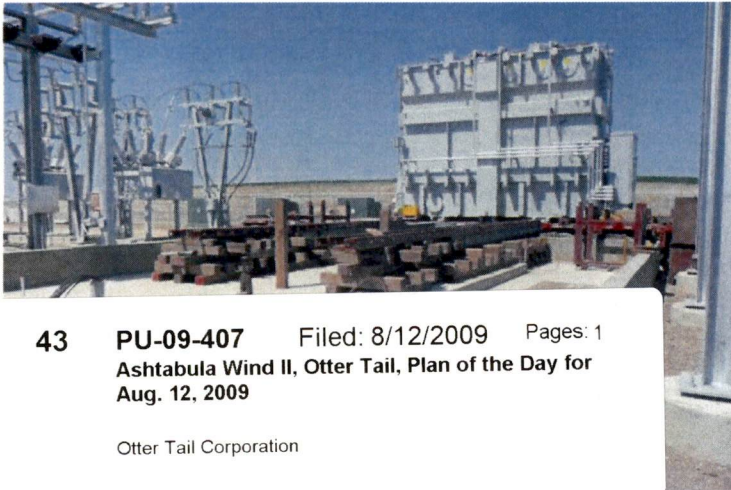

43 PU-09-407 Filed: 8/12/2009 Pages: 1
 Ashtabula Wind II, Otter Tail, Plan of the Day for
 Aug. 12, 2009

Otter Tail Corporation
