




**NEXtera™ Energy Resources  
Ashtabula Wind II**



**Otter Tail**

**Plan of the Day (POD)**

**Date: Thursday, 8/13/2009**  
**High: 92**  
**Precipitation Chances: 0%**

**COD: 10-15-09**  
**Low: 62**

**Days to COD: 64**  
**Winds: ENE @ 7 mph**  
**Weather Forecast: Sunny**

**NEXtera™ Energy Resources    Otter Tail    Blattner Energy    GE**

**Safety/Environmental:**

- **Keep hydrated**
- **Keep your speed to a minimum**
- **Watch out for blind corners in areas where corn is growing**
- **SWPPP inspection today**

**Erection:**

- **Offloading tower sections, nacelle & blades**
- **Erect base & mid at 153-154**
- **Assemble rotor at 153-154**
- **Erect top nacelle & rotor at 163-164**

**Collections:**

- **Low voltage cable termination at 159-161**
- **High voltage termination at 152-153**

**Electrical:**

- **Controller termination at 149-150**
- **Tower wiring at 158**
- **Mechanical completion walk down at 145-146**
- **IIP at 136 & 140**


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	4	29
Grounding XFR	3	3	0
4/0 Cable	189,000	195,397	-6,397
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	33	0
Controllers	33	33	0
Bases	33	31	2
Mids	33	31	2
Tops	33	31	2
Nacelles	33	32	1
Hubs	33	33	0
Blade Sets	33	31	2

**Negative Number Indicates Overage of Cable**

**General Construction Status**

	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	33	33	100.0%
Crane Pads Completed	33	33	100.0%
Tower Base Sections Erected	20	33	60.6%
Tower Mid Sections Erected	20	33	60.6%
Tower Top Sections Erected	15	33	45.5%
Nacelles Installed	15	33	45.5%
Rotors Installed	15	33	45.5%
Tower Wiring Complete	15	33	45.5%
Mechanically Complete	4	33	12.1%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	179,188	189,000	94.8%
500 Cable Trenched	100,122	117,000	85.6%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set	33	33	100.0%

(as of COB yesterday)

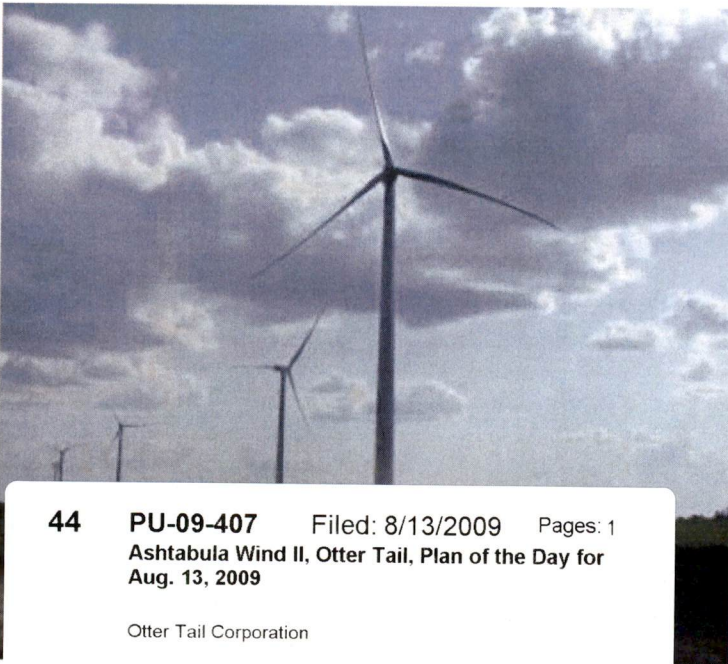

44    PU-09-407    Filed: 8/13/2009    Pages: 1  
 Ashtabula Wind II, Otter Tail, Plan of the Day for  
 Aug. 13, 2009

Otter Tail Corporation
