




NEXtera™ Energy Resources Ashtabula Wind II



Otter Tail

Plan of the Day (POD)

Date: Wednesday, 9/2/2009
High: 78
Precipitation Chances: 2%

COD: 10-15-09
Low: 52

Days to COD: 44
Winds: SE @ 7 mph
Weather Forecast: Partly Sunny

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- PPE is very important and must be worn on site at all times
- Keep focused when driving
- Keep your speed to a minimum
- Watch out for blind corners in areas where corn is growing
- SWPPP inspection every two weeks

Civil:

- Reclaim shoulders 132-pipeline & 133-135

Erection:

- Erect top & nacelle & rotor Complete

Collections:

Electrical:

- Tower wiring at 157
- IIP at 155-156
- GE Pre-Commissioning at 147-148 & 151

Substation:

- Circuit 3N Energization


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	33	0
Grounding XFR	3	3	0
4/0 Cable	189,000	195,397	-6,397
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	33	0
Controllers	33	33	0
Bases	33	33	0
Mids	33	33	0
Tops	33	33	0
Nacelles	33	33	0
Hubs	33	33	0
Blade Sets	33	33	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	33	33	100.0%
Crane Pads Completed	33	33	100.0%
Tower Base Sections Erected	33	33	100.0%
Tower Mid Sections Erected	33	33	100.0%
Tower Top Sections Erected	33	33	100.0%
Nacelles Installed	33	33	100.0%
Rotors Installed	33	33	100.0%
Tower Wiring Complete	33	33	100.0%
Mechanically Complete	29	33	87.9%
Pre-Commissioned	21	33	63.6%
Final Commissioned	18	33	54.5%
4/0 Cable Trenched	179,188	189,000	94.8%
500 Cable Trenched	100,122	117,000	85.6%
1000 Low Voltage Installed	12,750	12,750	100.0%
Fiber Optic 12 Fiber SM	97,000	97,000	100.0%
Transformers Set	33	33	100.0%

(as of COB yesterday)

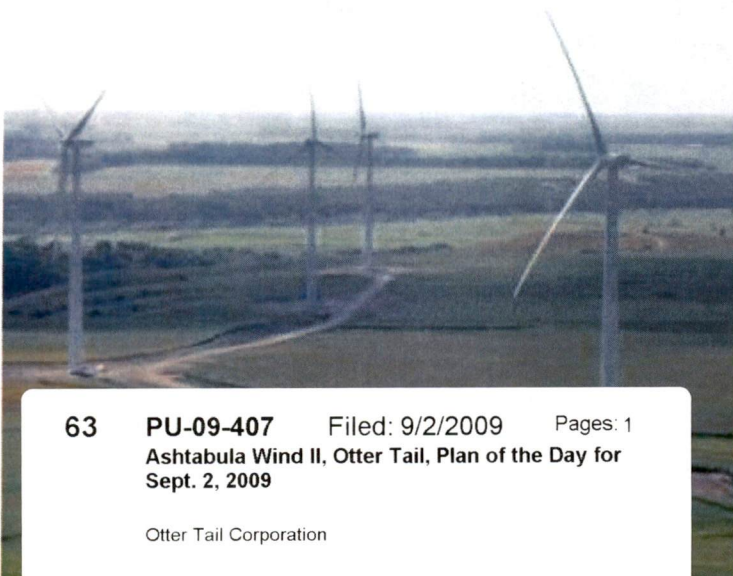

63 PU-09-407 Filed: 9/2/2009 Pages: 1
 Ashtabula Wind II, Otter Tail, Plan of the Day for
 Sept. 2, 2009

Otter Tail Corporation
