

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Thursday, 10-21-10
High: 63
Precipitation Chances: 0 %

COD: 11-30-10
Low: 33

Days to COD: 41
Winds: SSE @ 6 mph
Weather Forecast: Sunny

NextEra™ Energy Resources

Blattner Energy

Paradigm

GE

Safety/Environmental:

- SWPPP inspection 10-26-10
- Follow traffic signs

Civil/Erection:

- Reclaim at 31, 47-49 & 52
- Erect base at 11-12
- Erect mid at 11-12
- Assemble rotor at 9-10
- Erect top, nacelle & rotor at 27-29

Foundations: Complete

Collection:

- Underground fiber splicing at FS903, FS1003 & FS1103
- Turbine fiber splice at 11-15
- Fiber testing at F10

Electrical:

- Tower wiring at 30
- Mechanical completion pre-walk at 30
- IIP at 50-51
- GE Commissioning at 63-64

Substation:

- Control wire installation
- Wire Baldwin end of CT circuit


RECEIVING (As of COB yesterday)

	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	6	0
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	64	64	100.0%
Crane Pads Completed	64	64	100.0%
Tower Base Sections Erected	44	64	68.8%
Tower Mid Sections Erected	44	64	68.8%
Tower Top Sections Erected	35	64	54.7%
Nacelles Installed	35	64	54.7%
Rotors Installed	35	64	54.7%
Tower Wiring Complete	34	64	53.1%
Mechanically Complete	30	64	46.9%
Pre-Commissioned	24	64	37.5%
Commissioned	5	64	7.8%
4/0 Cable Trenched	149,724	149,724	100.0%
500 Cable Trenched	13,965	13,965	100.0%
1000 Cable Trenched	76,996	76,996	100.0%
Transformers Set/Terminated	64	64	100.0%
(as of COB yesterday)			

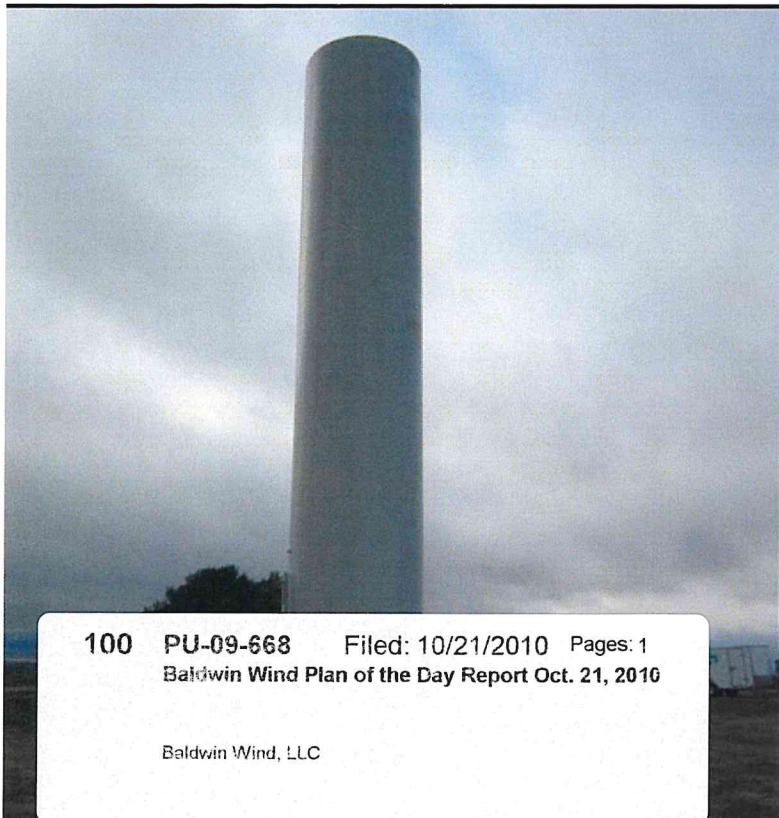

100 PU-09-668 Filed: 10/21/2010 Pages: 1
Baldwin Wind Plan of the Day Report Oct. 21, 2010

Baldwin Wind, LLC
