




NEXTerTM Energy Resources Ashtabula Wind III



NEXTer Energy Plan of the Day (POD)

Date: **Thursday, 9-23-10**
High: **58**
Precipitation Chances: **100%**

COD: **12-15-10**
Low: **41**

Days to COD: **84**
Winds: **N @ 17 mph**
Weather Forecast: **Rain**

NEXTerTM Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Be cautious of your speeds, obey traffic signs
- Wear proper PPE
- It is rainy and muddy so watch your footing

Civil/Erection:

- No work today due to rain

Foundations:

- Pour pedestal at 260-261

Collection:

Electrical:


Substation:

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	40	40	0
Grounding XFR	3	0	3
4/0 Cable	251,642	122,687	128,955
500 KCM	42,438	31,163	11,275
1000 KCM	265,584	147,175	118,409
1250 KCMIL	85,586	72,110	13,476
12 Fiber SM FOC	211,602	228,504	-16,902
XFR Box Pads	40	20	20
Controllers	39	39	0
Bases	39	39	0
Mids	39	39	0
Tops	39	39	0
Nacelles	39	39	0
Hubs	39	39	0
Blade Sets	39	39	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	42,500	68,421	62.1%
Roads Complete	25,128	68,421	36.7%
Silt Fence Installed	19,706	55,716	35.4%
Foundations Excavated	26	39	66.7%
Foundations Poured	12	39	30.8%
Foundations Backfilled	6	39	15.4%
Crane Pads Completed	0	39	0.0%
Tower Base Sections Erected	0	39	0.0%
Tower Mid Sections Erected	0	39	0.0%
Tower Top Sections Erected	0	39	0.0%
Nacelles Installed	0	39	0.0%
Rotors Installed	0	39	0.0%
Tower Wiring Complete	0	39	0.0%
Mechanically Complete	0	80	0.0%
Mechanically Complete	0	39	0.0%
Pre-Commissioned	0	39	0.0%
Final Commissioned	0	39	0.0%
4/0 Cable Trenched	20,695	251,642	8.2%
500 Cable Trenched	0	42,438	0.0%
1000 Cable Trenched	37,441	265,584	14.1%
1250 Cable Trenched	0	85,568	0.0%
Fiber Optic 12 Fiber SM	0	211,602	0.0%
Transformers Set/Terminated	0	39	0.0%
(as of COB yesterday)			

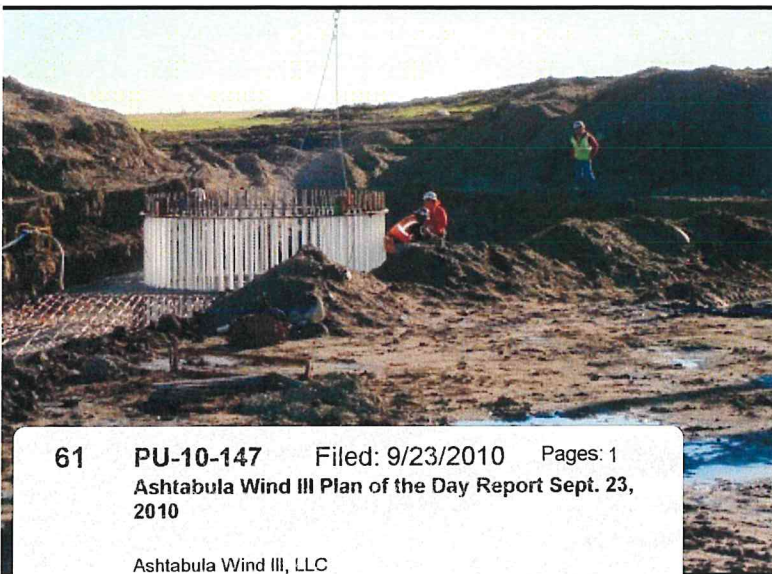

61 PU-10-147 Filed: 9/23/2010 Pages: 1
Ashtabula Wind III Plan of the Day Report Sept. 23, 2010

Ashtabula Wind III, LLC
