




NEXTerTM Energy Resources Ashtabula Wind II



Otter Tail

Plan of the Day (POD)

Date: Saturday, 8/1/2009
High: 74
Precipitation Chances: 5%

COD: 10-15-09
Low: 49

Days to COD: 78
Winds: WNW @ 7 mph
Weather Forecast: Partly Sunny

NEXTerTM Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Drive cautiously and keep speeds to a minimum
- Make sure not to use any equipment if it is tagged out
- Keep your speed to a minimum
- SWPPP inspection every two weeks

Civil/Erection:

Erection:

- Erect base & mid at 141
- Assemble rotor at 141
- Erect top, nacelle & rotor at 139

Collections:

- Trench & cable install -500 151-154

Electrical:


- Low voltage cable termination at 139-141
- High voltage cable termination at 138-139

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	0	33
Grounding XFR	3	0	3
4/0 Cable	189,000	129,912	59,088
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	33	0
Controllers	33	20	13
Bases	33	15	18
Mids	33	15	18
Tops	33	15	18
Nacelles	33	15	18
Hubs	33	15	18
Blade Sets	33	13	20

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	33	33	100.0%
Crane Pads Completed	33	33	100.0%
Tower Base Sections Erected	9	33	27.3%
Tower Mid Sections Erected	9	33	27.3%
Tower Top Sections Erected	7	33	21.2%
Nacelles Installed	7	33	21.2%
Rotors Installed	7	33	21.2%
Tower Wiring Complete	0	33	0.0%
Mechanically Complete	0	33	0.0%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	35,455	189,000	18.8%
500 Cable Trenched	21137	117,000	18.1%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set	25	33	75.8%
(as of COB yesterday)			

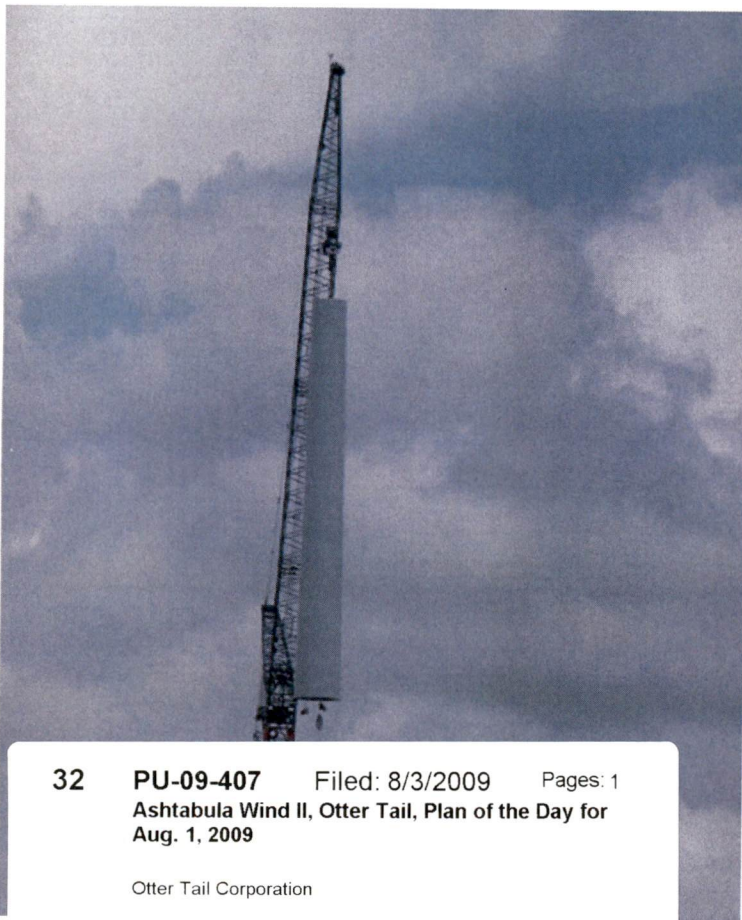

32 PU-09-407 Filed: 8/3/2009 Pages: 1
 Ashtabula Wind II, Otter Tail, Plan of the Day for
 Aug. 1, 2009

Otter Tail Corporation
