


NEXTerTM Energy Resources Ashtabula Wind II



Otter Tail

Plan of the Day (POD)

Date: Friday, 9/4/2009
High: 82
Precipitation Chances: 0%

COD: 10-15-09
Low: 52

Days to COD: 42
Winds: SE @ 4 mph
Weather Forecast: Sunny

NEXTerTM Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- PPE is very important and must be worn on site at all times
 - Keep focused when driving
 - Keep your speed to a minimum
 - Watch out for blind corners in areas where corn is growing
 - SWPPP inspection every two weeks
- Civil: No work today**

Erection:

Collections:

Electrical:

- GE Commissioning continuing


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	33	0
Grounding XFR	3	3	0
4/0 Cable	189,000	195,397	-6,397
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	12,700	50
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	33	0
Controllers	33	33	0
Bases	33	33	0
Mids	33	33	0
Tops	33	33	0
Nacelles	33	33	0
Hubs	33	33	0
Blade Sets	33	33	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	41,232	100.0%
Gravel Road (6")	41,232	41,232	100.0%
Roads Complete	41,232	41,232	100.0%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	33	33	100.0%
Foundations Backfilled	33	33	100.0%
Crane Pads Completed	33	33	100.0%
Tower Base Sections Erected	33	33	100.0%
Tower Mid Sections Erected	33	33	100.0%
Tower Top Sections Erected	33	33	100.0%
Nacelles Installed	33	33	100.0%
Rotors Installed	33	33	100.0%
Tower Wiring Complete	33	33	100.0%
Mechanically Complete	32	33	97.0%
Pre-Commissioned	21	33	63.6%
Final Commissioned	18	33	54.5%
4/0 Cable Trenched	179,188	189,000	94.8%
500 Cable Trenched	100,122	117,000	85.6%
1000 Low Voltage Installed	12,750	12,750	100.0%
Fiber Optic 12 Fiber SM	97,000	97,000	100.0%
Transformers Set	33	33	100.0%

(as of COB yesterday)

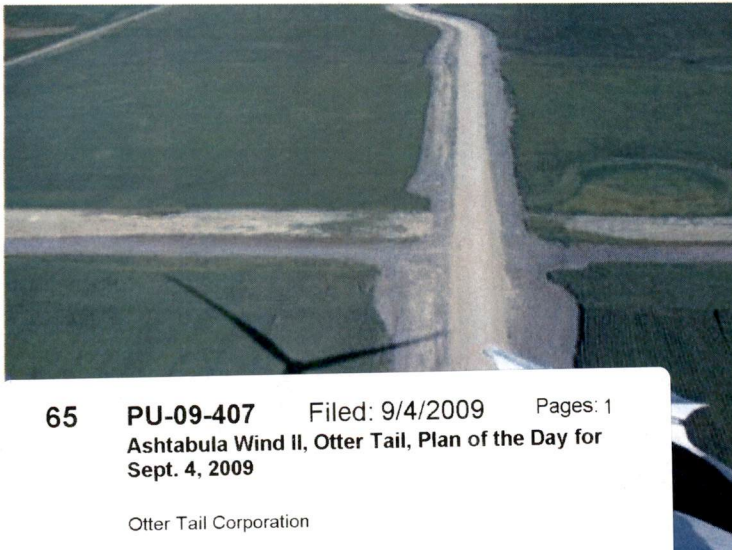

65 PU-09-407 Filed: 9/4/2009 Pages: 1
 Ashtabula Wind II, Otter Tail, Plan of the Day for
 Sept. 4, 2009

Otter Tail Corporation
