




**NEXtera™ Energy Resources  
Ashtabula Wind II**

**NEXtera Energy**

**Plan of the Day (POD)**



**Date: Saturday, 8/1/2009**  
**High: 74**  
**Precipitation Chances: 5%**

**COD: 10-31-09**  
**Low: 49**

**Days to COD: 92**  
**Winds: WNW @ 7 mph**  
**Weather Forecast: Partly Sunny**

**NEXtera™ Energy Resources    Otter Tail    Blattner Energy    GE**

**Safety/Environmental:**

- Drive cautiously
- Use correct procedure when offloading any material
- Keep your speed to a minimum
- SWPPP inspection every two weeks

**Civil/Erection:**

**Foundations:**

**Collection:**

• Boring at 179-191

**Electrical:**

- Cable termination at 195-196
- Box pad installation at 201
- PMT at 195-199


RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	381,214	59,786
500 KCM	36,000	37,036	-1,036
Copperdad	84,000	84,579	-579
1000 KCM	333,000	320,837	12,163
12 Fiber SM FOC	270,000	270,650	-650
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

**Negative Number Indicates Overage of Cable**

**General Construction Status**

	Complete	Total	% Complete
Roads Subgraded	47,876	117,188	40.9%
Gravel Roads (6")	42,532	117,188	36.3%
Roads Complete	38,327	117,188	32.7%
Silt Fence Installed	13,599	17,700	76.8%
Foundations Excavated	43	80	53.8%
Foundations Poured	26	80	32.5%
Foundations Backfilled	12	80	15.0%
Crane Pads Completed	11	80	13.8%
Tower Base Sections Erected	0	80	0.0%
Tower Mid Sections Erected	0	80	0.0%
Tower Top Sections Erected	0	80	0.0%
Nacelles Installed	0	80	0.0%
Rotors Installed	0	80	0.0%
Tower Wiring Complete	0	80	0.0%
Mechanically Complete	0	80	0.0%
Final Commissioned	0	80	0.0%
4/0 Cable Trenched	14,987	441,000	3.4%
500 Cable Trenched	2834	36,000	7.9%
1000 Cable Trenched	0	333,000	0.0%
Copperdad	0	84,000	0.0%
1000 Low Voltage Trenched	0	30,500	0.0%
Fiber Optic 12 Fiber SM	0	270,000	0.0%
Transformers Set/Terminated	0	80	0.0%

(as of COB yesterday)

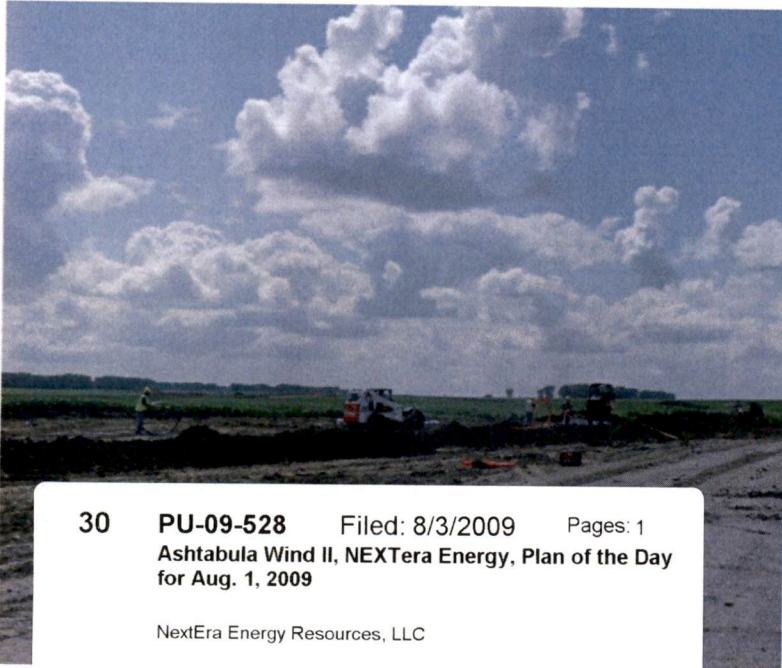

30    PU-09-528    Filed: 8/3/2009    Pages: 1  
 Ashtabula Wind II, NEXtera Energy, Plan of the Day  
 for Aug. 1, 2009

NextEra Energy Resources, LLC
