




NEXtera™ Energy Resources Ashtabula Wind II

NEXtera Energy

Plan of the Day (POD)



Date: Saturday, 8/8/2009
High: 78
Precipitation Chances: 55%

COD: 10-31-09
Low: 57

Days to COD: 85
Winds: NNE @ 3 mph
Weather Forecast: Cloudy

NEXtera™ Energy Resources Otter Tail Blattner Energy GE

Safety/Environmental:

- Drive cautiously, headlights must be on
- Keep your speed to a minimum
- Watch out for blind corners in areas where corn is growing
- SWPPP inspection every two weeks

Civil/Erection:

- Subgrade at 170-171 & 188
- Approach at 170

Foundations:

- Backfill at 209
- Build crane pads at 209

Erection:

- Erect base & mid at 187

Collection:

- Trench & cable install-1000kv at circuit 35 homerun

Electrical:


- Controller termination at 185 & 186

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	453,555	-12,555
500 KCM	36,000	37,036	-1,036
Copperclad	84,000	84,579	-579
1000 KCM	333,000	320,837	12,163
12 Fiber SM FOC	270,000	270,650	-650
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	60,786	117,188	51.9%
Gravel Roads (6")	53,211	117,188	45.4%
Roads Complete	50,311	117,188	42.9%
Silt Fence Installed	17,762	17,700	100.4%
Foundations Excavated	52	80	65.0%
Foundations Poured	39	80	48.8%
Foundations Backfilled	26	80	32.5%
Crane Pads Completed	25	80	31.3%
Tower Base Sections Erected	7	80	8.8%
Tower Mid Sections Erected	7	80	8.8%
Tower Top Sections Erected	4	80	5.0%
Nacelles Installed	4	80	5.0%
Rotors Installed	4	80	5.0%
Tower Wiring Complete	0	80	0.0%
Mechanically Complete	0	80	0.0%
Final Commissioned	0	80	0.0%
4/0 Cable Trenched	69,741	441,000	15.8%
500 Cable Trenched	9162	36,000	25.5%
1000 Cable Trenched	34,110	333,000	10.2%
Copperclad	0	84,000	0.0%
1000 Low Voltage Trenched	0	30,500	0.0%
Fiber Optic 12 Fiber SM	0	270,000	0.0%
Transformers Set/Terminated	8	80	10.0%
(as of COB yesterday)			

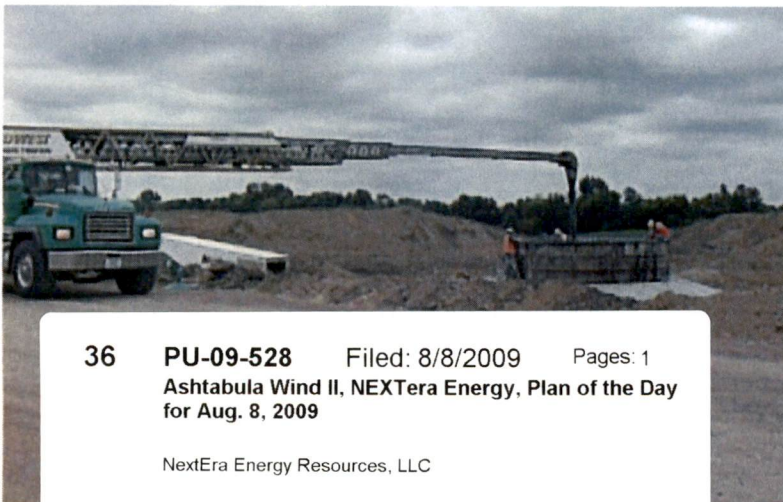

36 PU-09-528 Filed: 8/8/2009 Pages: 1
 Ashtabula Wind II, NEXtera Energy, Plan of the Day
 for Aug. 8, 2009

NextEra Energy Resources, LLC
