



**ENBRIDGE™**  
**ALBERTA CLIPPER PIPELINE PROJECT**  
**WEEKLY CONSTRUCTION STATUS REPORT**  
**November 26 to December 2, 2009**

### **Construction Activity**

Enbridge continued construction of the Alberta Clipper Pipeline Project in North Dakota between November 26 and December 2, 2009. Installation of the Alberta Clipper Pipeline has been completed with the exception of the North Dakota/Canada border crossing and the location of the hydrostatic testing at the Red River crossing. All wetland, waterbody and road crossings have been completed. The rough and final cleanup crews continued to make progress throughout North Dakota. Other activities included stormwater inspections and the installation and replacement of erosion and sediment controls. Rough and final clean up activities will continue to make progress by removing timber mats, replacing topsoil, and applying dormant seed mixes as required by agencies and landowners. Compaction alleviation of agricultural areas is being completed as a part of final restoration activities. In addition, crews are stabilizing the right-of-way in preparation for frozen conditions.

Additionally, the following work was also been completed to date:


- Clearing: 28.0 miles completed
- Grading: 28.0 miles completed
- Stringing: 28.0 miles completed
- Welding: 28.0 miles completed
- Trenching 28.0 miles completed
- Lowering-in 28.0 miles completed
- Backfill 28.0 miles completed
- Rough Cleanup 26.0 miles completed
- Final Cleanup 26.0 miles completed

Photographs of construction activities in North Dakota area attached.

Conservation Reserve Program parcel seeded and mulched



Restored waterbody slopes at Tongue River "Cutoff"

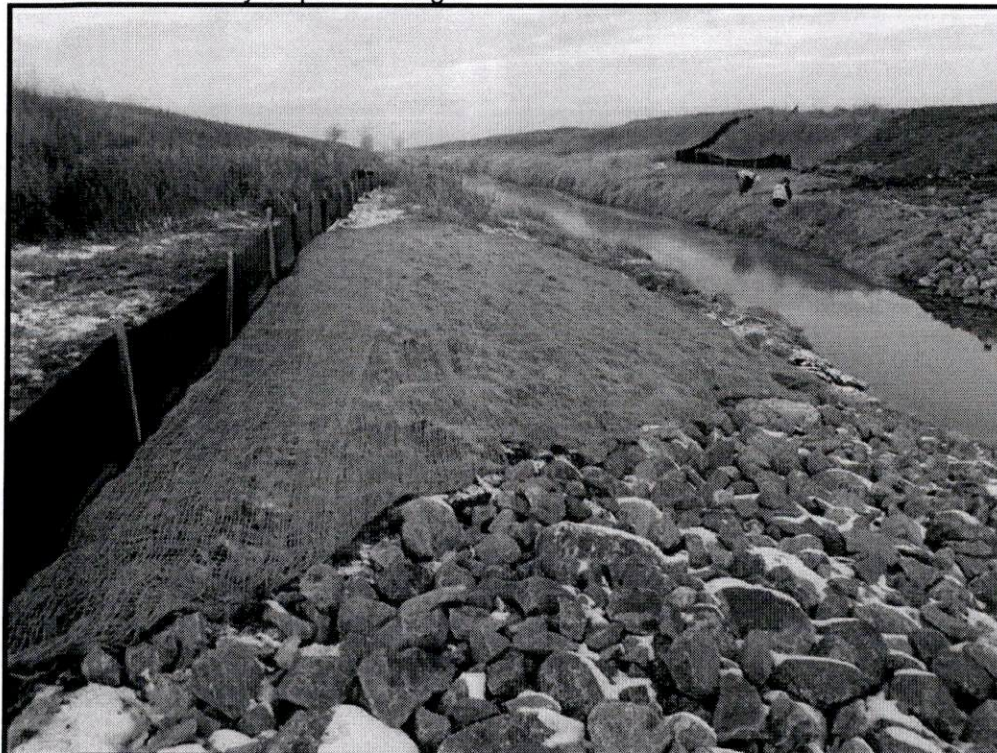

Erosion control devices in place and functioning




Trench Dewatering



Slope stabilization



Topsoil stabilization

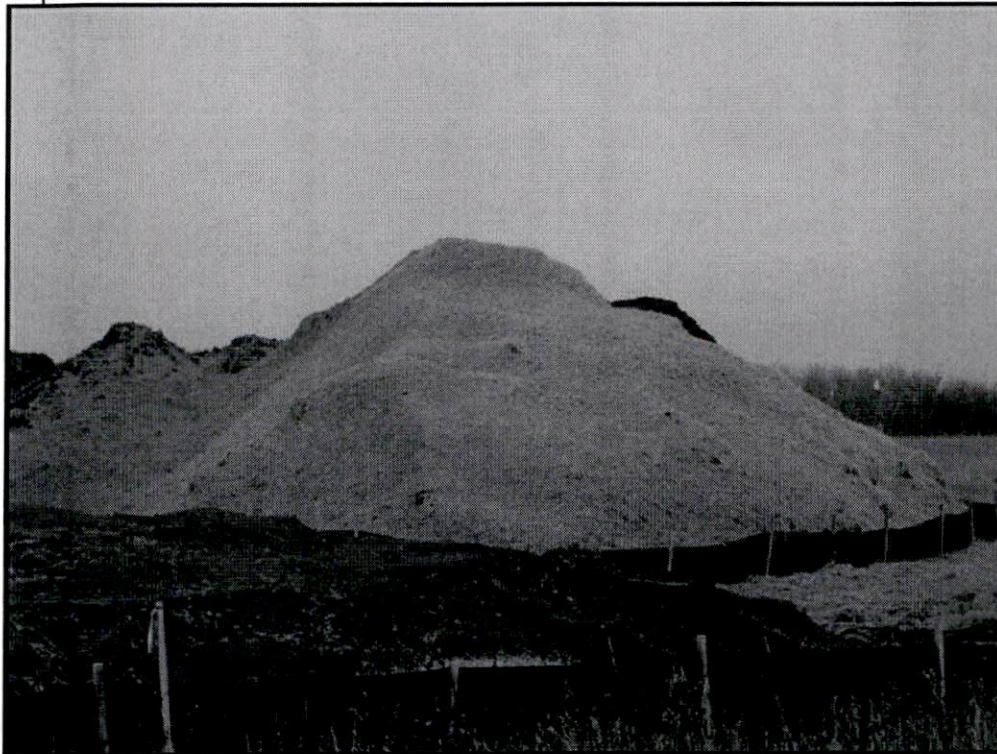

### Bank restoration



### Agency Consultations

The North Dakota Department of Health was updated on November 30, 2009 regarding pipeline construction related spills.

### Upcoming Activities

The following activities are scheduled for the next reporting period:

- Continuation of stormwater inspections;
- Stabilization of the right-of-way for winter;
- Preparing and hydrostatically testing the North Dakota pipeline section;
- Continuation of rough and final clean-up activities; and
- Continuation of restoration activities.
