

Exam Date:10/22/2018

Bowman Grain, Inc.

Page: 1

Examiner: 1, 2

Box 91

Bowman , ND

County:

Phone: 701-523-3173

CCC Number:

Location/Container Numbers/Comments	Section	Capacity
PART A - ADDITIONAL SPACE TO BE INCLUDED UNDER LICENSE		
114	M	4,821
115	M	4,821
116	M	4,821
117	M	4,821
107	E	3,966
108	E	3,966
	Total:	27,216
PART B - SPACE TO BE DELETED UNDER LICENSE		
<NO BINS DELETED>		
	Total:	0
PART C - ALL SPACE TO BE INCLUDED UNDER LICENSE		
	A	177,000
	C	15,000
	E	228,000
	M	20,000
	Total:	440,000
PART D - TOTAL CAPACITY BY FUNCTIONAL UNIT		
Bowman 231	A C E M	440,000
	Total:	440,000

Exam Date: 10/22/2018

Bowman Grain, Inc.

Page: 1

Examiner: 1, 2

Box 91

Bowman, ND

County:

Status	Section	Bin Number	Bin Type	Base Point	Diameter or Bu/Ft (irreg).		Side for wall	Add for Hopper	Ded. for Obst.	Effective Depth	Add for Peak Capac.	Depth for Foot	Bushels per Foot	Base Pack%	Bushel Capacity with Pack
					Length	Width									

Facility: Bowman

Section: A

A	001		Square	work floor	0.000	11.00	3.500	31.00	0.00	0.00	31.000	0.000	31.0		30.9	2.50	982
A	003		Square	work floor	0.000	11.00	7.800	47.00	0.00	0.00	47.000	0.000	47.0		69.0	5.20	3,412
A	004		Square	work floor	0.000	11.00	7.500	47.00	0.00	0.00	47.000	0.000	47.0		66.3	5.00	3,272
A	006		Square	work floor	0.000	11.00	7.500	47.00	0.00	0.00	47.000	0.000	47.0		66.3	5.00	3,272
A	007		Square	work floor	0.000	11.00	7.800	47.00	0.00	0.00	47.000	0.000	47.0		69.0	5.20	3,412
A	009		Square	work floor	0.000	10.00	5.000	33.00	0.00	0.00	33.000	0.000	33.0		40.2	3.00	1,367
A	010		Square	work floor	0.000	10.00	5.000	33.00	0.00	0.00	33.000	0.000	33.0		40.2	3.00	1,367
A	011		Square	work floor	0.000	10.00	5.000	33.00	0.00	0.00	33.000	0.000	33.0		40.2	3.00	1,367
A	012		Square	work floor	0.000	10.00	5.000	33.00	0.00	0.00	33.000	0.000	33.0		40.2	3.00	1,367
A	013		Square	work floor	0.000	11.00	7.800	47.00	0.00	0.00	47.000	0.000	47.0		69.0	5.20	3,412
A	014		Square	work floor	0.000	11.00	7.500	28.00	0.00	0.00	28.000	0.000	28.0		66.3	5.00	1,949
A	015		Square	work floor	0.000	11.00	6.500	28.00	0.00	0.00	28.000	0.000	28.0		57.5	4.80	1,687
A	017 T		Square	work floor	0.000	11.00	2.500	8.000	0.00	0.00	8.000	0.000	8.0		22.1	2.00	181
A	017 B		Square	work floor-top 8'	0.000	11.00	9.000	39.00	0.00	0.00	39.000	0.000	39.0		79.6	5.50	3,275
A	019		Square	work floor	0.000	11.00	6.500	8.000	0.00	0.00	8.000	0.000	8.0		57.5	4.80	482
A	021 T		Square	catwalk	0.000	15.50	10.00	36.00	0.00	0.00	36.000	0.000	36.0		124.6	6.50	4,778
A	021 B		Square	catwalk - top 36'	0.000	11.50	10.00	9.000	0.00	0.00	9.000	0.000	9.0		92.4	5.80	880
A	022		Square	catwalk	0.000	15.50	10.00	45.00	0.00	0.00	45.000	0.000	45.0		124.6	6.50	5,971
A	023 T		Square	catwalk	0.000	15.50	10.30	36.00	0.00	0.00	36.000	0.000	36.0		128.3	6.50	4,919
A	023 B		Square	catwalk - top 36'	0.000	11.50	10.30	9.000	0.00	0.00	9.000	0.000	9.0		95.2	6.00	908
A	024		Square	catwalk	0.000	15.50	10.30	45.00	0.00	0.00	45.000	0.000	45.0		128.3	6.50	6,149

Exam Date: 10/22/2018

Bowman Grain, Inc.

Examiner: 1, 2

Box 91
Bowman, ND

County:

Status	Section	Bin Number	Bin Type	Base Point	Diameter or Bu/Ft (Irreg.)	Length	Width	Side wall	Add for Hopper	Ded. for Obst.	Effective Depth	Add for Peak Capac.	Depth	Bushels per Foot	Base Pack%	Bushel Capacity with Pack
--------	---------	------------	----------	------------	----------------------------	--------	-------	-----------	----------------	----------------	-----------------	---------------------	-------	------------------	------------	---------------------------

Facility: Bowman

Section: A

A	025 T	Square	catwalk		0.000	15.50	10.00	36.00	0.00	0.00	36.000	0.000	36.0	124.6	6.50	4,778
A	025 B	Square	catwalk - top 36'		0.000	11.50	10.00	9.000	0.00	0.00	9.000	0.000	9.0	92.4	5.80	880
A	026	Square	catwalk		0.000	15.50	10.00	45.00	0.00	0.00	45.000	0.000	45.0	124.6	6.50	5,971
A	031 T	Square	catwalk		0.000	14.50	13.70	45.00	0.00	0.00	45.000	0.000	45.0	159.7	7.00	7,690
A	031 B	Square	catwalk - top 45'		0.000	13.50	11.80	3.500	0.00	0.00	3.500	0.000	3.5	128.1	6.50	477
A	032 T	Square	catwalk		0.000	14.50	13.70	45.00	0.00	0.00	45.000	0.000	45.0	159.7	7.00	7,690
A	032 B	Square	catwalk - top 45'		0.000	13.50	11.80	3.500	0.00	0.00	3.500	0.000	3.5	128.1	6.50	477
A	033 T	Square	catwalk		0.000	14.50	13.70	45.00	0.00	0.00	45.000	0.000	45.0	159.7	7.00	7,690
A	033 B	Square	catwalk-top 45'		0.000	13.50	11.80	3.500	0.00	0.00	3.500	0.000	3.5	128.1	6.50	477
A	034 T	Square	catwalk		0.000	14.50	13.70	45.00	0.00	0.00	45.000	0.000	45.0	159.7	7.00	7,690
A	034 B	Square	catwalk - top 45'		0.000	13.50	11.80	3.500	0.00	0.00	3.500	0.000	3.5	128.1	6.50	477
A	035 T	Square	catwalk -		0.000	14.50	13.70	45.00	0.00	0.00	45.000	0.000	45.0	159.7	7.00	7,690
A	035 B	Square	catwalk - top 45'		0.000	13.50	11.80	3.500	0.00	0.00	3.500	0.000	3.5	128.1	6.50	477
A	036 T	Square	catwalk		0.000	14.50	13.70	45.00	0.00	0.00	45.000	0.000	45.0	159.7	7.00	7,690
A	036 B	Square	catwalk - top 45'		0.000	13.50	11.80	3.500	0.00	0.00	3.500	0.000	3.5	128.1	6.50	477
A	037 T	Square	catwalk		0.000	14.50	13.70	45.00	0.00	0.00	45.000	0.000	45.0	159.7	7.00	7,690
A	037 B	Square	catwalk - top 45'		0.000	13.50	11.80	3.500	0.00	0.00	3.500	0.000	3.5	128.1	6.50	477
A	038 T	Square	catwalk		0.000	14.50	13.70	45.00	0.00	0.00	45.000	0.000	45.0	159.7	7.00	7,690
A	038 B	Square	catwalk - top 45'		0.000	13.50	11.80	3.500	0.00	0.00	3.500	0.000	3.5	128.1	6.50	477
A	039 T	Square	catwalk		0.000	14.50	13.70	45.00	0.00	0.00	45.000	0.000	45.0	159.7	7.00	7,690
A	039 B	Square	catwalk - top 45'		0.000	13.50	11.80	3.500	0.00	0.00	3.500	0.000	3.5	128.1	6.50	477

Exam Date: 10/22/2018

Bowman Grain, Inc.

Page: 3

Examiner: 1, 2

Box 91
Bowman, ND

County:

Status	Section	Bin Number	Bin Type	Base Point	Diameter or Bu/Ft (Irreg.)	Length	Width	Side wall	Add for Hopper	Det. for Obst.	Effective Depth	Add for Peak	Depth for Capac.	Bushels per Foot	Base Pack%	Bushel Capacity with Pack
--------	---------	------------	----------	------------	----------------------------	--------	-------	-----------	----------------	----------------	-----------------	--------------	------------------	------------------	------------	---------------------------

Facility: Bowman

Section: A

A	040 T		Square	catwalk	0.000	14.50	13.70	45.00	0.00	0.00	45.000	0.000	45.0	159.7	7.00	7,690
A	040 B		Square	catwalk- top 45"	0.000	13.50	11.80	3.500	0.00	0.00	3.500	0.000	3.5	128.1	6.50	477
A	103		Peaked	top of sidewall	13.500	0.000	0.000	15.00	2.25	0.00	17.250	0.800	18.1	115.1	5.20	2,191
A	104		Peaked	top of sidewall	13.500	0.000	0.000	15.00	2.25	0.00	17.250	0.800	18.1	115.1	5.20	2,191
A	105		Peaked	top of sidewall	13.500	0.000	0.000	15.00	2.25	0.00	17.250	0.800	18.1	115.1	5.20	2,191
A	106		Peaked	top of sidewall	13.500	0.000	0.000	15.00	2.25	0.00	17.250	0.800	18.1	115.1	5.20	2,191
A	107		Peaked	top of sidewall	16.000	0.000	0.000	20.00	2.40	0.00	22.400	1.000	23.4	161.6	5.80	4,000
A	108		Peaked	top of sidewall	16.000	0.000	0.000	20.00	2.40	0.00	22.400	1.000	23.4	161.6	5.80	4,000
A	109		Peaked	top of sidewall	16.000	0.000	0.000	20.00	2.40	0.00	22.400	1.000	23.4	161.6	5.80	4,000
A	110		Peaked	top of sidewall	16.000	0.000	0.000	20.00	2.40	0.00	22.400	1.000	23.4	161.6	5.80	4,000
A	111		Peaked	top of sidewall	16.000	0.000	0.000	20.00	2.40	0.00	22.400	1.000	23.4	161.6	5.80	4,000
Bin count: 53															Facility: Bowman Section: A Total:	176,472
															To Even:	177,000

Section: C

C	030		Peaked		30.000	0.000	0.000	22.00	0.00	0.00	22.000	1.800	23.8	568.2	9.00	14,740
Bin count: 1															Facility: Bowman Section: C Total:	14,740
															To Even:	15,000

Exam Date: 10/22/2018

Bowman Grain, Inc.

Page: 4

Examiner: 1, 2

Box 91
Bowman, ND

County:

Status	Section	Bin Number	Bin Type	Base Point	Diameter or Bu/Ft (Irreg.)	Length	Width	Side wall	Add for Hopper	Ded. for Obs.	Effective Depth	Add for Peak Capac.	Depth for Foot	Bushels per Foot	Base Pack%	Bushel Capacity with Pack
--------	---------	------------	----------	------------	----------------------------	--------	-------	-----------	----------------	---------------	-----------------	---------------------	----------------	------------------	------------	---------------------------

Facility: Bowman

Section: E

E	001	Square	work floor		0.000	9.200	4.200	47.00	0.00	0.00	47.000	0.000	47.0	31.1	2.50	1,499
E	002 T	Square	work floor		0.000	8.700	6.300	54.00	0.00	0.00	54.000	0.000	54.0	44.1	3.50	2,464
E	002 B	Square	work floor - top 54'		0.000	9.700	7.700	17.00	0.00	0.00	17.000	0.000	17.0	60.0	4.80	1,069
E	004	Square	work floor		0.000	9.800	6.800	52.00	0.00	0.00	52.000	0.000	52.0	53.6	4.50	2,912
E	005	Square	work floor		0.000	11.40	5.000	52.00	0.00	0.00	52.000	0.000	52.0	45.8	4.00	2,477
E	006	Square	work floor		0.000	11.40	5.000	52.00	0.00	0.00	52.000	0.000	52.0	45.8	4.00	2,477
E	007 T	Square	work floor		0.000	8.700	6.300	54.00	0.00	0.00	54.000	0.000	54.0	44.1	3.50	2,464
E	007 B	Square	work floor - top 54'		0.000	9.700	7.700	17.00	0.00	0.00	17.000	0.000	17.0	60.0	4.80	1,069
E	009 T	Square	work floor		0.000	6.800	1.500	14.00	0.00	0.00	14.000	0.000	14.0	8.2	2.00	117
E	009 B	Square	work floor - top 14'		0.000	7.700	6.800	38.00	0.00	0.00	38.000	0.000	38.0	42.1	3.50	1,656
E	012	Square	work floor		0.000	7.700	6.800	52.00	0.00	0.00	52.000	0.000	52.0	42.1	3.50	2,266
E	013	Square	work floor		0.000	9.800	6.800	52.00	0.00	0.00	52.000	0.000	52.0	53.6	4.50	2,912
E	014 T	Square	work floor		0.000	13.50	10.40	64.00	0.00	0.00	64.000	0.000	64.0	112.9	6.20	7,674
E	014 B	Square	work floor - top 64'		0.000	11.10	10.40	7.000	0.00	0.00	7.000	0.000	7.0	92.8	5.80	688
E	015 T	Square	work floor		0.000	10.40	4.200	47.00	0.00	0.00	47.000	0.000	47.0	35.1	3.00	1,700
E	015 M	Square	work floor - top 47'		0.000	13.50	10.40	17.00	0.00	0.00	17.000	0.000	17.0	112.9	6.20	2,038
E	015B	Square	work floor - top & middle 64'		0.000	11.10	10.40	7.000	0.00	0.00	7.000	0.000	7.0	92.8	5.80	688
E	017	Square	work floor		0.000	9.000	5.000	47.00	0.00	0.00	47.000	0.000	47.0	36.2	3.00	1,752
E	018	Square	work floor		0.000	9.000	5.000	47.00	0.00	0.00	47.000	0.000	47.0	36.2	3.00	1,752
E	021 T	Square	work floor -		0.000	11.60	4.200	54.00	0.00	0.00	54.000	0.000	54.0	39.2	3.00	2,181
E	021 M	Square	work floor - top 54'		0.000	13.50	11.60	10.00	0.00	0.00	10.000	0.000	10.0	125.9	6.50	1,341

Exam Date: 10/22/2018

Bowman Grain, Inc.

Page: 5

Examiner: 1, 2

Box 91
Bowman, ND

County:

Status	Section	Bin Number	Bin Type	Base Point	Diameter or Bu/Ft (irreg.)	Length	Width	Side wall	Add for Hopper	Det. for Obst.	Effective Depth	Add for Peak Capac.	Depth	Bushels per Foot	Base Pack%	Bushel Capacity with Pack
--------	---------	------------	----------	------------	-------------------------------	--------	-------	--------------	----------------------	----------------------	--------------------	------------------------------	-------	------------------------	---------------	------------------------------

Facility: Bowman

Section: E

E	021B		Square	work floor - top & middle 64'	0.000	11.60	11.10	7.000	0.00	0.00	7.000	0.000	7.0	103.5		6.00	769
E	022		Square	work floor	0.000	9.000	5.700	47.00	0.00	0.00	47.000	0.000	47.0	41.2		3.50	2,004
E	023 T		Square	work floor	0.000	13.50	11.60	64.00	0.00	0.00	64.000	0.000	64.0	125.9		6.50	8,582
E	023 B		Square	work floor - top 64'	0.000	11.60	11.10	7.000	0.00	0.00	7.000	0.000	7.0	103.5		6.00	769
E	024		Square	work floor	0.000	9.000	5.700	47.00	0.00	0.00	47.000	0.000	47.0	41.2		3.50	2,004
E	025 T		Square	work floor	0.000	13.50	11.60	64.00	0.00	0.00	64.000	0.000	64.0	125.9		6.50	8,582
E	025 B		Square	work floor - top 64'	0.000	11.60	11.10	7.000	0.00	0.00	7.000	0.000	7.0	103.5		6.00	769
E	026 T		Square	work floor	0.000	13.50	11.60	64.00	0.00	0.00	64.000	0.000	64.0	125.9		6.50	8,582
E	026 B		Square	work floor - top 64'	0.000	11.60	11.10	7.000	0.00	0.00	7.000	0.000	7.0	103.5		6.00	769
E	027 T		Square	work floor	0.000	13.50	11.60	64.00	0.00	0.00	64.000	0.000	64.0	125.9		6.50	8,582
E	027 B		Square	work floor-top 64'	0.000	11.60	11.10	7.000	0.00	0.00	7.000	0.000	7.0	103.5		6.00	769
E	028 T		Square	work floor	0.000	13.50	11.60	64.00	0.00	0.00	64.000	0.000	64.0	125.9		6.50	8,582
E	028 B		Square	work floor-top 64'	0.000	11.60	11.10	7.000	0.00	0.00	7.000	0.000	7.0	103.5		6.00	769
E	029 T		Square	work floor	0.000	13.50	11.60	64.00	0.00	0.00	64.000	0.000	64.0	125.9		6.50	8,582
E	029 B		Square	work floor - top 64'	0.000	11.60	11.10	7.000	0.00	0.00	7.000	0.000	7.0	103.5		6.00	769
E	030 T		Square	work floor	0.000	13.50	11.60	64.00	0.00	0.00	64.000	0.000	64.0	125.9		6.50	8,582
E	030 B		Square	work floor-top 64'	0.000	11.60	11.10	7.000	0.00	0.00	7.000	0.000	7.0	103.5		6.00	769
E	031 T		Square	work floor	0.000	13.50	11.30	64.00	0.00	0.00	64.000	0.000	64.0	122.6		6.50	8,356
E	031 B		Square	work floor - top 64'	0.000	11.30	11.10	7.000	0.00	0.00	7.000	0.000	7.0	100.8		6.00	748
E	032 T		Square	work floor	0.000	13.50	11.30	64.00	0.00	0.00	64.000	0.000	64.0	122.6		6.50	8,356
E	032 B		Square	work floor - top 64'	0.000	11.30	11.10	7.000	0.00	0.00	7.000	0.000	7.0	100.8		6.00	748

Exam Date: 10/22/2018
 Examiner: 1, 2

Bowman Grain, Inc.
 Box 91
 Bowman, ND
 County:

Status	Section	Bin Number	Bin Type	Base Point	Diameter or Bu/Ft (Irreg.)	Length	Width	Side wall	Add for Hopper	Det. for Obst.	Effective Depth	Add for Peak	Depth for Capac.	Bushels per Foot	Base Pack%	Bushel Capacity with Pack
--------	---------	------------	----------	------------	----------------------------	--------	-------	-----------	----------------	----------------	-----------------	--------------	------------------	------------------	------------	---------------------------

Facility: Bowman

Section: E

E	101		Irregular	work floor -12.3x9.5 +	99.400	0.000	0.000	62.00	0.00	0.00	62.000	0.000	62.0	99.4	6.00	6,533
E	102 T		Square	work floor	0.000	12.30	8.600	62.00	0.00	0.00	62.000	0.000	62.0	85.0	5.80	5,576
E	102 B		Square	work floor - top 62'	0.000	11.80	10.50	8.000	0.00	0.00	8.000	0.000	8.0	99.6	6.00	845
E	103 T		Square	work floor	0.000	12.30	8.600	62.00	0.00	0.00	62.000	0.000	62.0	85.0	5.80	5,576
E	103 B		Square	work floor -top 62'	0.000	11.80	10.50	8.000	0.00	0.00	8.000	0.000	8.0	99.6	6.00	845
E	105 T		Square	work floor	0.000	11.30	10.80	62.00	0.00	0.00	62.000	0.000	62.0	98.1	6.00	6,447
E	105 B		Square	work floor -top 62'	0.000	10.50	10.20	8.000	0.00	0.00	8.000	0.000	8.0	86.1	5.80	729
E	106 T		Square	work floor	0.000	10.70	8.600	62.00	0.00	0.00	62.000	0.000	62.0	74.0	5.50	4,840
E	106 B		Square	work floor - top 62'	0.000	10.50	10.30	8.000	0.00	0.00	8.000	0.000	8.0	86.9	5.80	735
Added	E 107		Peaked	top of sidewall Steel bin	16.000	0.000	0.000	20.00	2.20	0.00	22.200	1.000	23.2	161.6	5.80	3,966
E	107 T		Square	work floor	0.000	11.30	10.80	62.00	0.00	0.00	62.000	0.000	62.0	98.1	6.00	6,447
E	107 B		Square	work floor -TOP 62'	0.000	10.50	10.20	8.000	0.00	0.00	8.000	0.000	8.0	86.1	5.80	729
Added	E 108		Peaked	top of sidewall Steel bin	16.000	0.000	0.000	20.00	2.20	0.00	22.200	1.000	23.2	161.6	5.80	3,966
E	108 T		Square	work floor	0.000	10.70	8.600	62.00	0.00	0.00	62.000	0.000	62.0	74.0	5.50	4,840
E	108 B		Square	work floor -top 62'	0.000	10.50	10.30	8.000	0.00	0.00	8.000	0.000	8.0	86.9	5.80	735
E	110 T		Square	work floor	0.000	10.70	8.600	62.00	0.00	0.00	62.000	0.000	62.0	74.0	5.50	4,840
E	110 B		Square	work floor - top 62'	0.000	10.50	10.30	8.000	0.00	0.00	8.000	0.000	8.0	86.9	5.80	735
E	111 T		Square	work floor	0.000	10.70	8.600	62.00	0.00	0.00	62.000	0.000	62.0	74.0	5.50	4,840
E	111 B		Square	work floor - top 62'	0.000	10.50	10.30	8.000	0.00	0.00	8.000	0.000	8.0	86.9	5.80	735
E	112		Square	work floor	0.000	10.70	9.500	62.00	0.00	0.00	62.000	0.000	62.0	81.7	5.50	5,344
E	113		Square	work floor	0.000	13.50	9.500	62.00	0.00	0.00	62.000	0.000	62.0	103.1	6.00	6,776

Exam Date: 10/22/2018
 Examiner: 1, 2

Bowman Grain, Inc.
 Box 91
 Bowman, ND
 County:

Status	Section	Bin Number	Bin Type	Base Point	Diameter or Bu/Ft (Irreg.)	Length	Width	Side wall	Add for Hopper	Ded. for Obs.	Effective Depth	Add for Peak	Depth for Capac.	Bushels per Foot	Base Pack%	Bushel Capacity with Pack
--------	---------	------------	----------	------------	----------------------------	--------	-------	-----------	----------------	---------------	-----------------	--------------	------------------	------------------	------------	---------------------------

Facility: Bowman

Section: E

E		114	Irregular	work floor 10.7x9.5 + 2.5x4	89.800	0.000	0.000	62.00	0.00	0.00	62.000	0.000	62.0	89.8	5.80	5,891
E		115 T	Square	work floor	0.000	13.50	8.600	62.00	0.00	0.00	62.000	0.000	62.0	93.3	5.80	6,121
E		115 B	Square	work floor - top 62'	0.000	12.90	10.50	8.000	0.00	0.00	8.000	0.000	8.0	108.9	6.20	925
E		116 T	Square	work floor	0.000	13.50	8.600	62.00	0.00	0.00	62.000	0.000	62.0	93.3	5.80	6,121
E		116 B	Square	work floor - top 62'	0.000	12.90	10.50	8.000	0.00	0.00	8.000	0.000	8.0	108.9	6.20	925
															Bin count: 68	Facility: Bowman Section: E Total: 227,700
															To Even: 228,000	

Section: M


Added	M	114	Peaked	top of sidewall	16.000	0.000	0.000	25.00	2.20	0.00	27.200	1.000	28.2	161.6	5.80	4,821
Added	M	115	Peaked	top of sidewall	16.000	0.000	0.000	25.00	2.20	0.00	27.200	1.000	28.2	161.6	5.80	4,821
Added	M	116	Peaked	top of sidewall	16.000	0.000	0.000	25.00	2.20	0.00	27.200	1.000	28.2	161.6	5.80	4,821
Added	M	117	Peaked	top of sidewall	16.000	0.000	0.000	25.00	2.20	0.00	27.200	1.000	28.2	161.6	5.80	4,821
															Bin count: 4	Facility: Bowman Section: M Total: 19,284
															To Even: 20,000	

Overall Licensed Bin Capacity for:
 Bowman Grain, Inc.
 Bin count: 126


Licensed Capacity: (includes pack) **438,196 Bu.**

Licensed Capacity (to even): (includes pack and section totals are rounded up to next highest 1000) **440,000 Bu.**


Bowman Grain Inc
 Bowman, ND
 Section A
 Corp #115
 10/22/18 PH

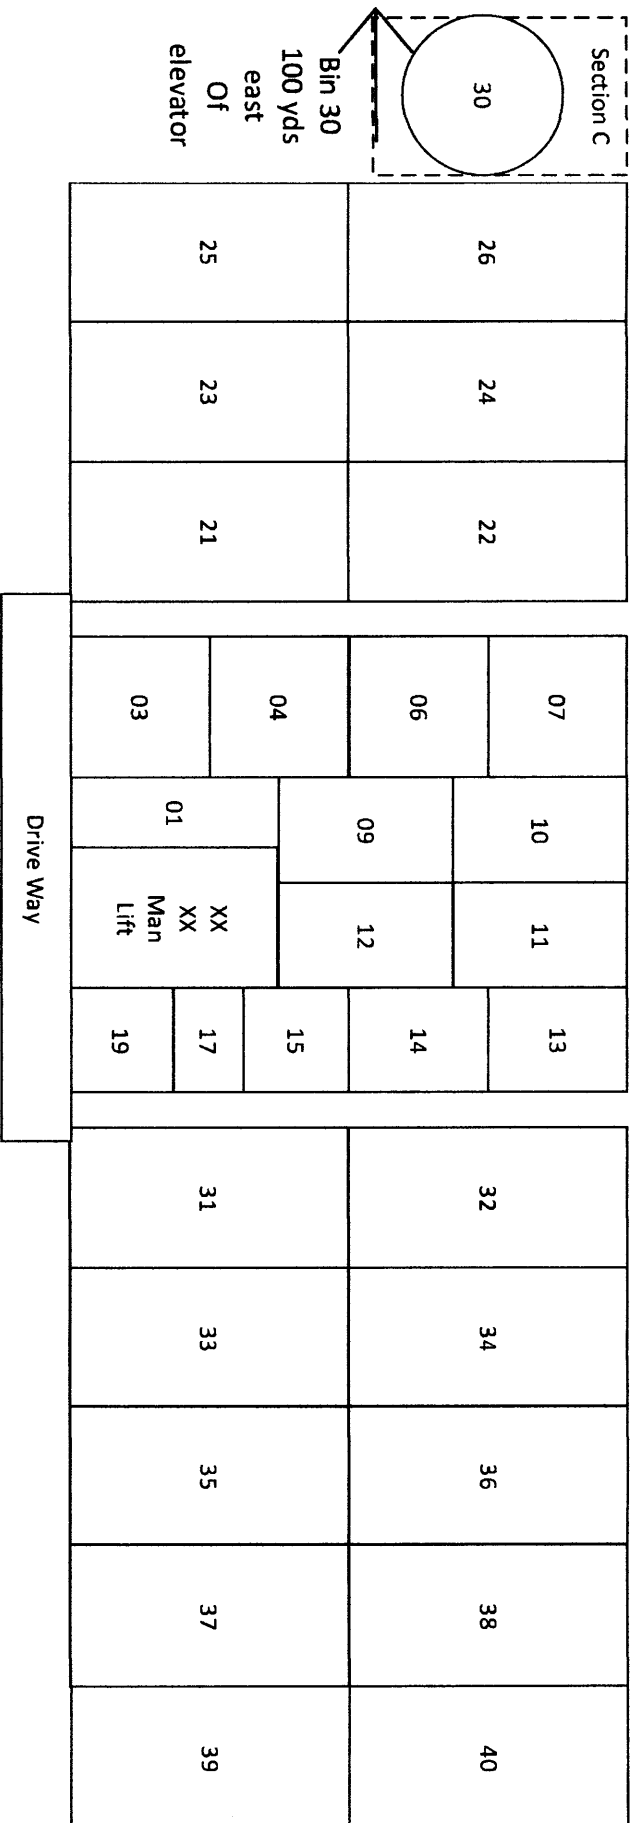


Bin 30
 100 yds
 east
 Of
 elevator



Section C






Section M



Bins 107-111 200 yds west of elevator

Bowman Grain Inc
 Bowman, ND
 Section E
 Corp #115
 10/22/18 PH



31	29	27	25
	30	28	26

23	14	12	09	07	13	04	05	06
21	15							
24	22	17	18		X X	01	02	
					ML X X			

102	107	106	110	115
101	X X	114	112	113
	X X			
103	105	108	111	116

