



NDPSC FIELD CHECKLIST

OBSERVER: Steven Strack

Project	NuStar Pipeline	Project No.	6077-024
Date	8/23/2016	SITE VISIT	1

NOTES:

*From my conversation with Dale and observations this morning, it seems like there is an efficient topsoil separation method being used. See attached diagram for details.

*Contractor using a dozer to clear and grub and another dozer stripping and stockpiling topsoil.

*Existing topsoil depth ranging from 8-12".

OBSERVERS'S SIGNATURE: Steven Strack




TO Page 3 of 3

DATE 8/23/16

SUBJECT Topsoil Stripping

BY Steven Strack

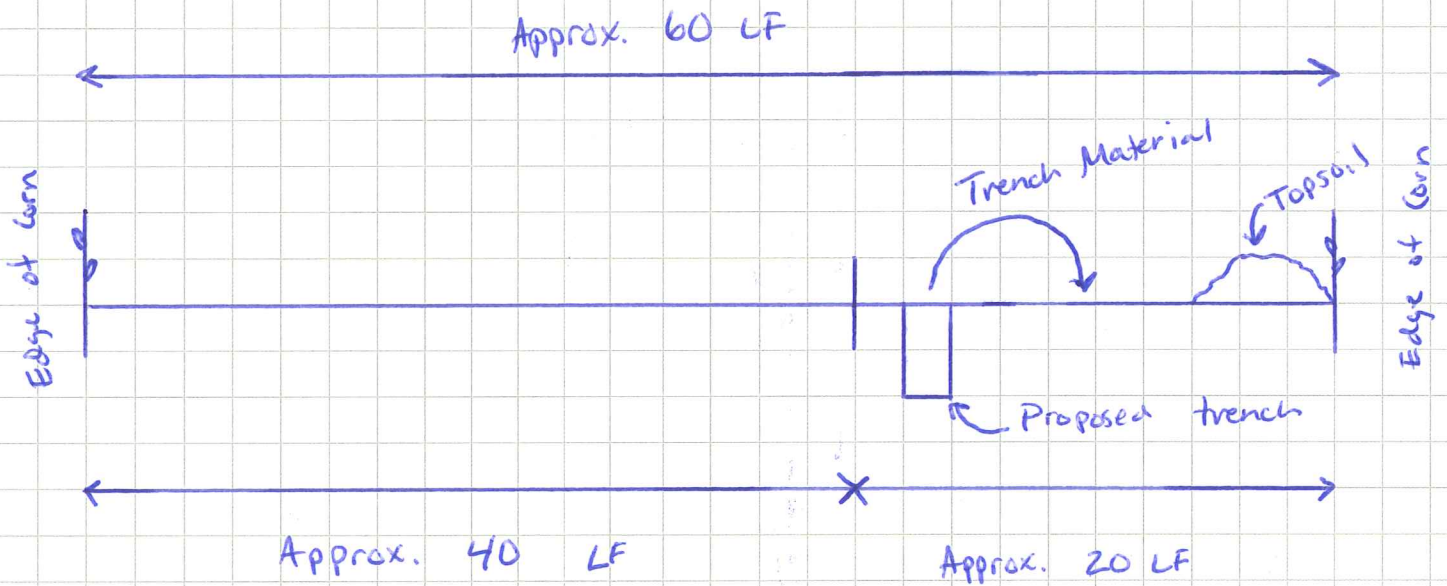

Clearing + grubbing only

Topsoil Stripping + Stockpiling

Area to be used for laying out pipe, construction vehicles, etc.
