

DAILY REPORT

RPR: Travis Johnson, P.E.

Project: Emmons Logan Energy Storage	Project No.: PU-25-209
Date: 5/5/2026 and 5/6/2026	Day: Tuesday, Wednesday
<u>Contractor:</u> Michels Construction	<u>Weather:</u> Mostly cloudy, Windy
<u>Hours Worked:</u> 8am to 6pm +/-	<u>Temp:</u> AM: 30s and 40s, PM 50s

Contractor Job Safety Meetings/Briefing: Tailgate safety briefing conducted by Rob Ewing the morning of 5/5/26 as a project kickoff prior to beginning work.

Job Site Hazards/Concerns and Actions Taken:

General safety notices given, stated that first aid, eye wash, fire extinguishers, and EPC's located in vehicles, information for nearest medical facility. Noted need for PPE to include closed toed footwear, hardhat, high visibility vest. Noted adjacent active power substation and active large equipment.

Engineering Staff:

Travis Johnson, Houston Engineering, Inc.

Work in Progress:

Mobilizing. Installed silt fence, Begin topsoil stripping.

Contractor's Labor Force

Labor Type	Labor Name	Labor Number
Laborer 2		
Operator 3		
Foreman 1		

Contractor's Equipment Summary

Equipment Type	Equipment Model	Equipment Number
Excavator 1		
Loader 0		
Skid Steer 2		
Compactor 2		
Backhoe on Tractor 0		

Date: 5/6/2026

Communications/Observations:

The intent of this report is to document the inspection of the initial topsoil stripping for the project. As the project began startup and had the initial project onsite kickoff meeting on 5/5/26, there was not sufficient progress on the topsoil stripping to give a proper reporting of the work. A follow up visit was conducted on 5/6/26 to inspect the topsoil stripping and give feedback to the site superintendent and equipment operators on the stripping. Four sites were being stripped in preparation for the site grading and construction of the infrastructure for the energy storage facility.

Noted topsoil stripping depth at Site 1 was exceeding the depth necessary and getting into underlying soils. Informed the operator that we did not want to mix subsoils with the topsoil and to exercise care not to get too deep.

Discussed stripping depth with onsite Superintendent and the intent to strip to one foot depth or the full cultivated depth, whichever is greater. Reviewed stripping depth at all four sites with Superintendent to ensure compliance with Certification Relating to Order Provisions. Pointed out over depth stripping at site 1 and recommended exercising care to not strip too deeply.

Site 1 Looking South



Site 1 Looking East



Site 2 Looking North



Site 2 Looking South



Date: 5/6/2026

Site 3 Looking South



Site 3 Looking North




Site 4 Looking North



Site 4 Looking East



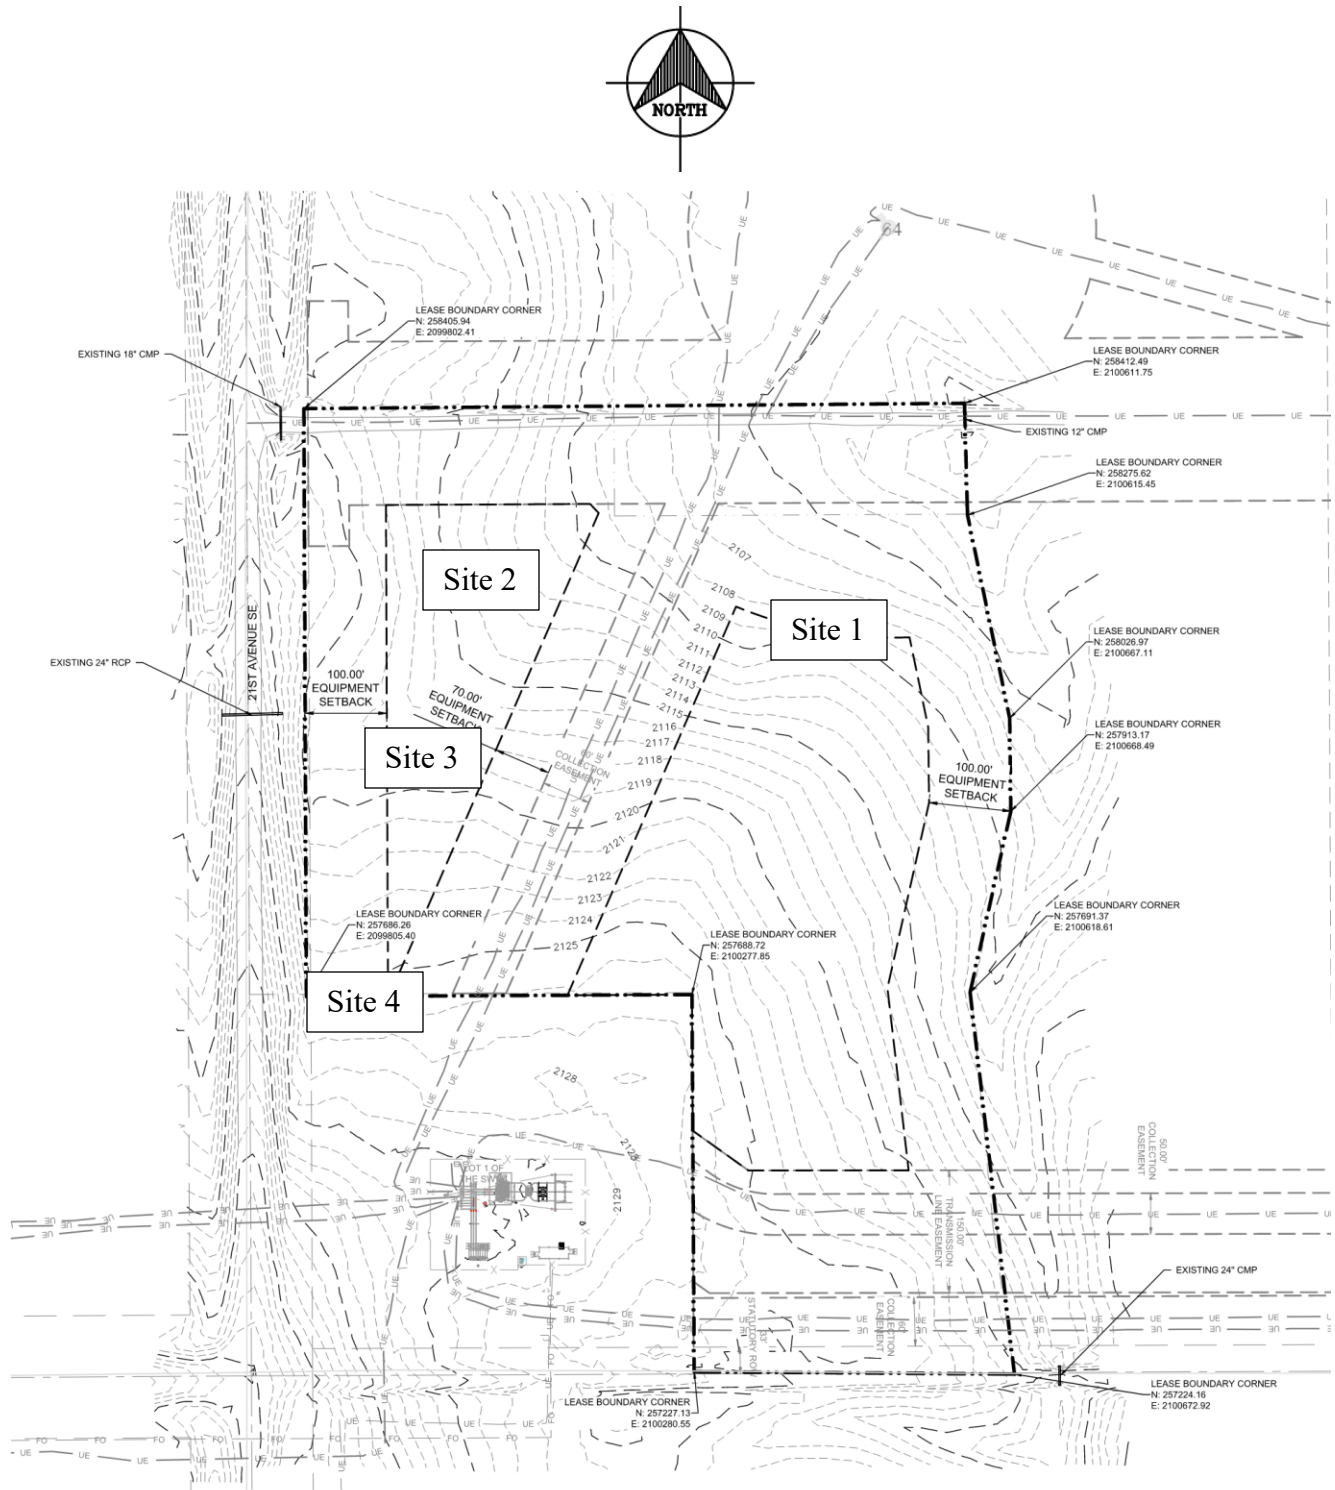

Emmons Logan Energy Storage Existing Conditions Sitemap
