

Exam Date:09/04/2018

Klindworth Seed & Bean Company Inc
2139 Highway 30
Fessenden, ND
County:

Page: 1

Examiner: 1

Status	Section	Bin Number	Bin Type	Base Point	Diameter or Bu/Ft (Irreg.)	Length	Width	Side wall	Add for Hopper	Ded. for Obst.	Effective Depth	Add for Peak	Depth for Capac.	Bushels per Foot	Base Pack%	Bushel Capacity with Pack
--------	---------	------------	----------	------------	-------------------------------	--------	-------	--------------	----------------------	----------------------	--------------------	--------------------	------------------------	------------------------	---------------	------------------------------

Facility: Fessenden

Section: A

A	001	Square	floor over bins		0.000	8.200	8.200	24.50	1.30	0.00	25.800	0.000	25.8	54.1	4.50	1,459
A	005	Square	floor over bins		0.000	8.200	8.200	24.50	1.30	0.00	25.800	0.000	25.8	54.1	4.50	1,459
A	007	Square	floor over bins		0.000	8.200	8.200	24.50	1.30	0.00	25.800	0.000	25.8	54.1	4.50	1,459
A	008	Square	floor over bins		0.000	8.200	8.200	24.50	1.30	0.00	25.800	0.000	25.8	54.1	4.50	1,459
A	009	Square	floor over bins		0.000	8.200	8.200	24.50	1.30	0.00	25.800	0.000	25.8	54.1	4.50	1,459
A	011	Square	floor over bins		0.000	8.200	8.200	24.50	1.30	0.00	25.800	0.000	25.8	54.1	4.50	1,459
A	012	Square	floor over bins		0.000	4.100	8.200	24.50	1.30	0.00	25.800	0.000	25.8	27.0	2.50	714
A	013	Square	floor over bins		0.000	4.100	8.200	24.50	1.30	0.00	25.800	0.000	25.8	27.0	2.50	714
A	014	Square	floor over bins		0.000	8.200	8.200	24.50	1.30	0.00	25.800	0.000	25.8	54.1	4.50	1,459
A	015	Square	floor over bins		0.000	8.200	8.200	24.50	1.30	0.00	25.800	0.000	25.8	54.1	4.50	1,459
A	016	Square	floor over bins		0.000	8.200	4.100	24.50	1.30	0.00	25.800	0.000	25.8	27.0	2.50	714
A	017	Square	floor over bins		0.000	8.200	4.100	24.50	1.30	0.00	25.800	0.000	25.8	27.0	2.50	714
A	018	Square	floor over bins		0.000	8.200	8.200	24.50	1.30	0.00	25.800	0.000	25.8	54.1	4.50	1,459
A	019	Square	floor over bins		0.000	8.200	8.200	24.50	1.30	0.00	25.800	0.000	25.8	54.1	4.50	1,459
A	020	Square	floor over bins		0.000	8.200	4.100	24.50	1.30	0.00	25.800	0.000	25.8	27.0	2.50	714
A	021	Square	floor over bins		0.000	8.200	4.100	24.50	1.30	0.00	25.800	0.000	25.8	27.0	2.50	714
A	022	Square	floor over bins		0.000	8.200	8.200	24.50	1.30	0.00	25.800	0.000	25.8	54.1	4.50	1,459
A	023	Flat	get dimensions		0.000	60.00	30.00	6.000	0.00	0.00	6.000	0.000	6.0	1446.9	10.0	9,549
A	191	Peaked	eave at sidewall		18.000	0.000	0.000	37.00	2.70	0.00	39.700	1.100	40.8	204.6	6.00	8,849
A	192	Peaked	eave at sidewall		18.000	0.000	0.000	37.00	2.70	0.00	39.700	1.100	40.8	204.6	6.00	8,849
A	B1	Peaked	eave at sidewall		16.000	0.000	0.000	17.00	2.30	0.00	19.300	1.000	20.3	161.6	5.80	3,470
A	B2	Peaked	eave at sidewall		16.000	0.000	0.000	17.00	2.30	0.00	19.300	1.000	20.3	161.6	5.80	3,470

Exam Date:09/04/2018

Klindworth Seed & Bean Company Inc
2139 Highway 30
Fessenden, ND
County:

Page: 2

Examiner: 1

Status	Section	Bin Number	Bin Type	Base Point	Diameter or Bu/Ft (Irreg). Length	Width	Side wall	Add for Hopper	Ded. for Obst.	Effective Depth	Add for Peak	Depth for Capac.	Bushels per Foot	Base Pack%	Bushel Capacity with Pack
--------	---------	------------	----------	------------	---	-------	--------------	----------------------	----------------------	--------------------	--------------------	------------------------	------------------------	---------------	------------------------------

Facility: Fessenden

Section: A

A	H1	Peaked	eave at sidewall		16.000	0.000	0.000	17.00	2.30	0.00	19.300	1.000	20.3	161.6	5.80	3,470
A	H2	Peaked	eave at sidewall		16.000	0.000	0.000	17.00	2.30	0.00	19.300	1.000	20.3	161.6	5.80	3,470
A	H3	Peaked	eave at sidewall		16.000	0.000	0.000	17.00	2.30	0.00	19.300	1.000	20.3	161.6	5.80	3,470
A	H31	Peaked	eave at sidewall		21.000	0.000	0.000	34.50	3.20	0.00	37.700	1.300	39.0	278.4	6.80	11,596
A	H32	Peaked	eave at sidewall		21.000	0.000	0.000	34.50	3.20	0.00	37.700	1.300	39.0	278.4	6.80	11,596
A	H33	Peaked	eave at sidewall		16.000	0.000	0.000	20.00	2.40	0.00	22.400	1.000	23.4	161.6	5.80	4,000
A	H34	Peaked	eave at sidewall		16.000	0.000	0.000	20.00	2.40	0.00	22.400	1.000	23.4	161.6	5.80	4,000
A	H4	Peaked	eave at sidewall		16.000	0.000	0.000	17.00	2.30	0.00	19.300	1.000	20.3	161.6	5.80	3,470
A	H5	Peaked	eave at sidewall		16.000	0.000	0.000	17.00	2.30	0.00	19.300	1.000	20.3	161.6	5.80	3,470

Bin count: 31

Facility: Fessenden Section: A Total: 103,062

To Even: 104,000

Section: B

B	301	Flat	straight wall warehouse		0.000	101.0	49.20	8.000	0.00	0.00	8.000	0.000	8.0	3994.5	10.0	35,152
B	303	Flat	flat storage south of plant		0.000	118.5	68.50	7.000	0.00	0.00	7.000	0.000	7.0	6525.1	10.0	50,244

Bin count: 2

Facility: Fessenden Section: B Total: 85,396

To Even: 86,000

Overall Licensed Bin Capacity for:

Klindworth Seed & Bean Company Inc

Bin count: 33

Licensed Capacity:
(includes pack)

188,458 Bu.




Licensed Capacity (to even):
(includes pack and section totals are
rounded up to next highest 1000)

190,000 Bu.

Klindworth Seed & Bean Co. Inc.
 Fessenden ND
 Corp.# 894
 Updated 9-13-18 A.S.

N
 W + E
 S

Section B
 Straight wall warehouse #301
 Located South of the plant
 49.2'W x101.0'L
 Grain wall ht. 4.0'
 Bottom center rafter to floor 15.5'
 Sidwall beams & rafters 25' on center

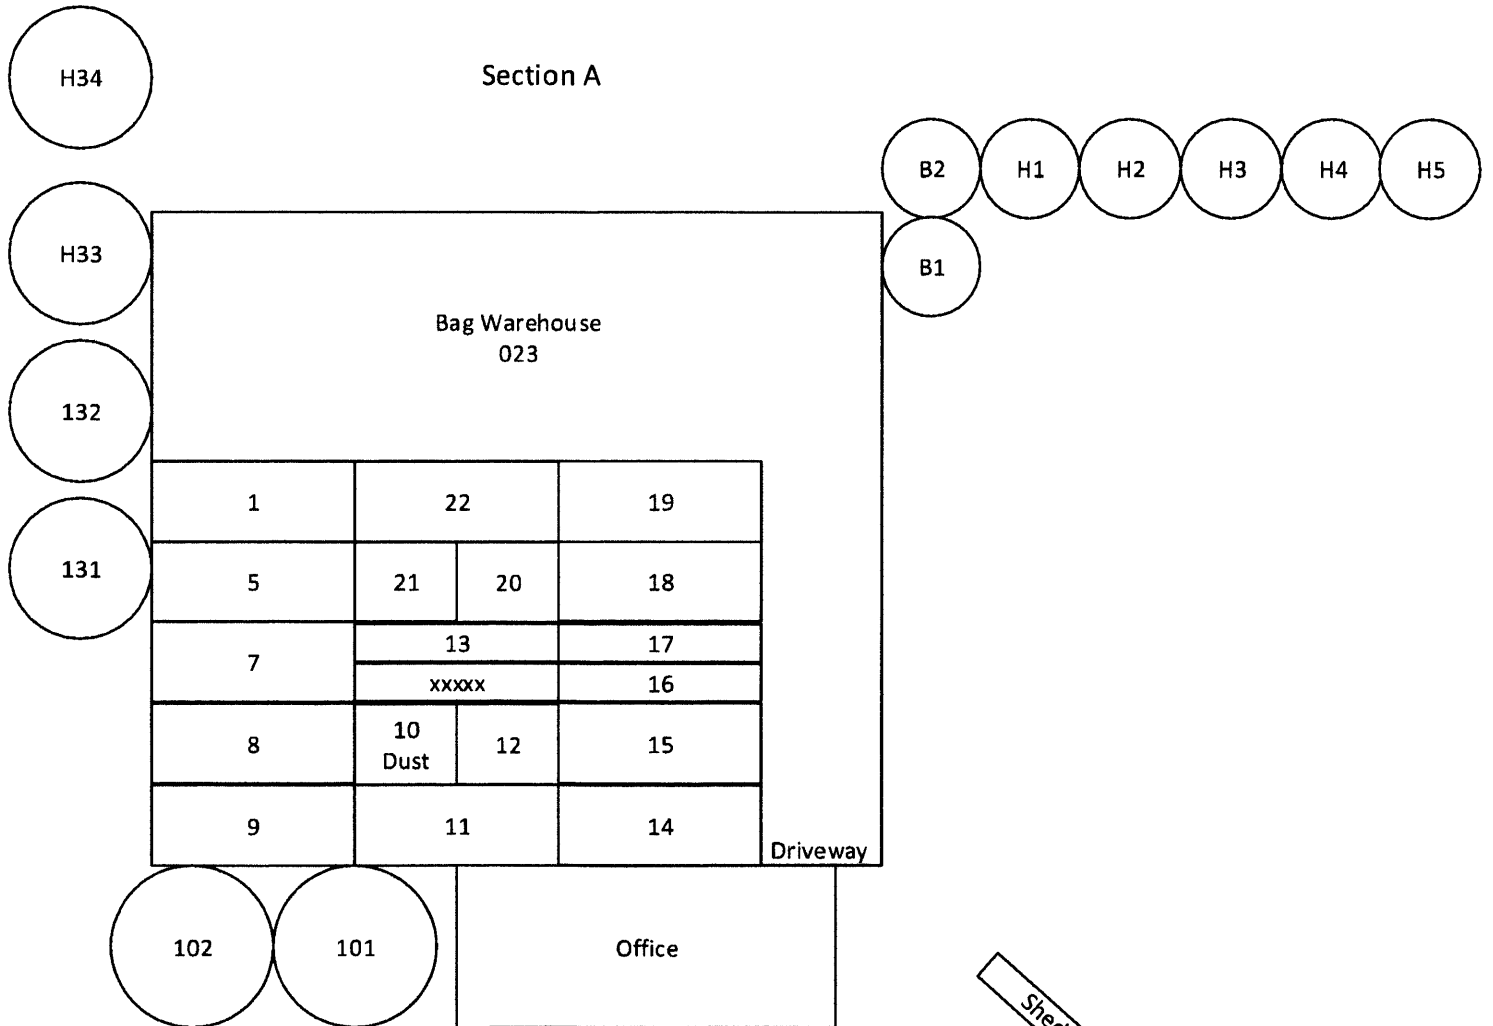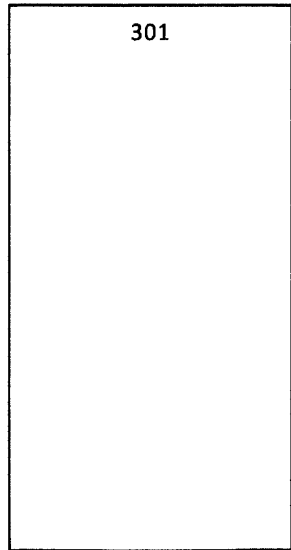

Clindworth Seed & Bean Co. Inc.
Fessenden ND
Corp.# 894
Updated 9-13-18 A.S.

Section B #303

Basic Dimensions

Outside dimensions 120'L x 70'W

Inside dimensions 118.5'L x 68.5'W

Grain wall ht. 7.5'

Bottom center rafter to floor 21.5'

Main beams & rafters 24.0' on center

