**BASIN ELECTRIC POWER COOPERATIIVE**
**Project: Williston to Tioga T-line Contract**
**Contractor: Great Southwestern**

**Weekly Progress Report**

Progress for the week ending : 07/31/2010

Manpower = 30

Note:
Completion the past week
Completion to date
X - indicates a foundation location
Str.#1 @ Williston and Str #406 @ Tioga

| | Weekly total | Weekly % | Cumulative total | Cumulative % |
|---|---|---|---|---|
| R/W Prep | 0 | 0.0 | 392 | 96.6 |
| Foundation Inst'l. (54) | 6 | 11.1 | 47 | 87.0 |
| Structure hauling | 69 | 17.0 | 382 | 94.1 |
| Structure assembly | 2 | 0.5 | 193 | 47.5 |
| Structure erection | 23 | 5.7 | 68 | 16.7 |
| Conductor/OPGW installation | | 0.0 | | 0.0 |
| R/W cleanup | | 0.0 | | 0.0 |
| R/W restoration | | 0.0 | | 0.0 |
| | | | | |

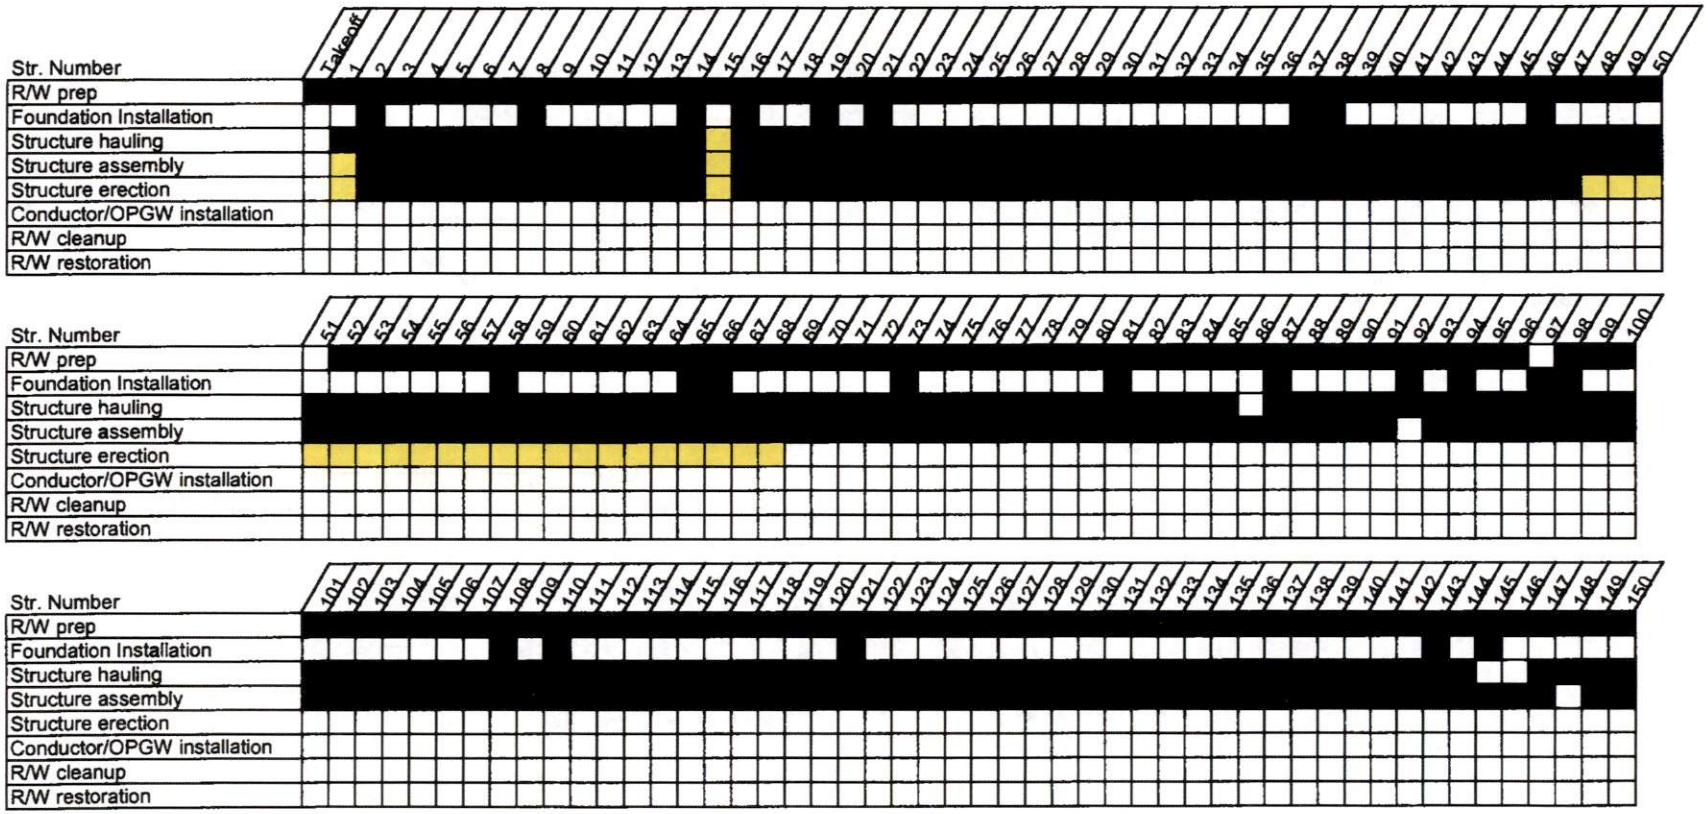




67 PU-07-671 Filed: 8/2/2010 Pages: 4
Williston to Tioga Basin Electric T-line Progress report week ending 7-31-2010
Basin Electric Power Cooperative

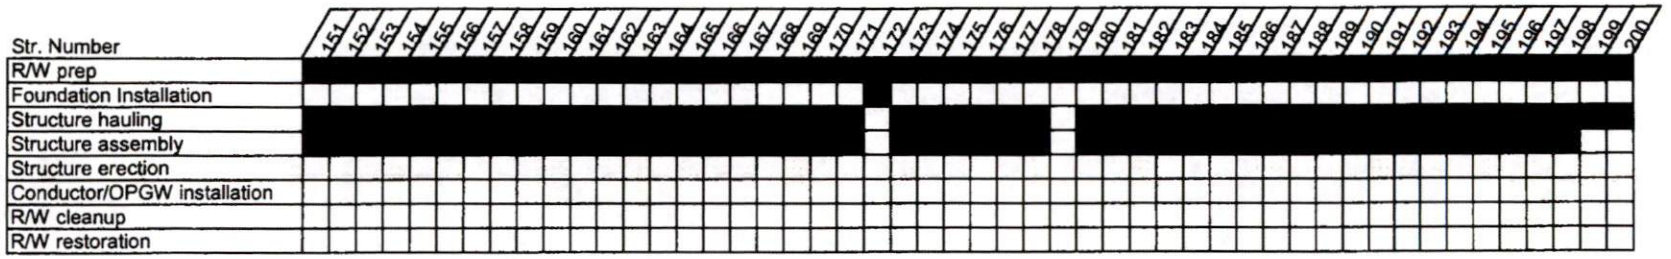
Str. Number
151 152 153 154 155 156 157 158 159 160 161 162 163 164 165 166 167 168 169 170 171 172 173 174 175 176 177 178 179 180 181 182 183 184 185 186 187 188 189 190 191 192 193 194 195 196 197 198 199 200
R/W prep
Foundation Installation
Structure hauling
Structure assembly
Structure erection
Conductor/OPGW installation
R/W cleanup
R/W restoration

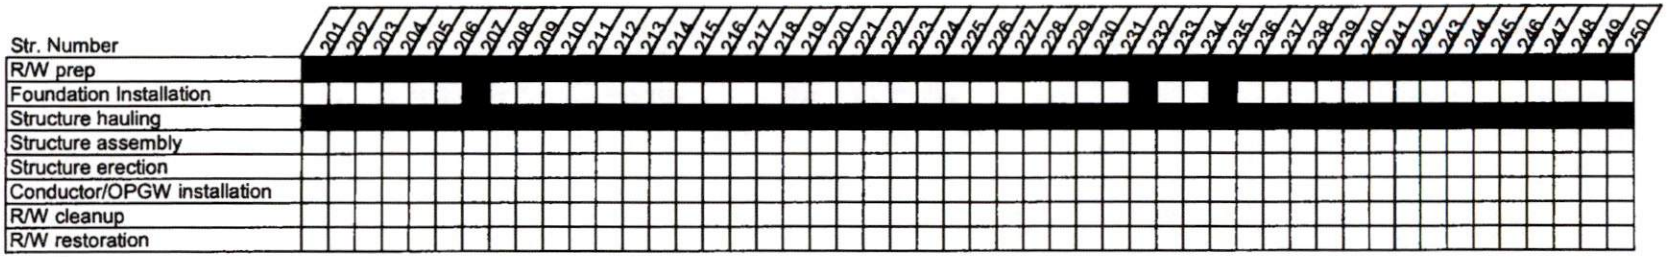
Str. Number
201 202 203 204 205 206 207 208 209 210 211 212 213 214 215 216 217 218 219 220 221 222 223 224 225 226 227 228 229 230 231 232 233 234 235 236 237 238 239 240 241 242 243 244 245 246 247 248 249 250
R/W prep
Foundation Installation
Structure hauling
Structure assembly
Structure erection
Conductor/OPGW installation
R/W cleanup
R/W restoration

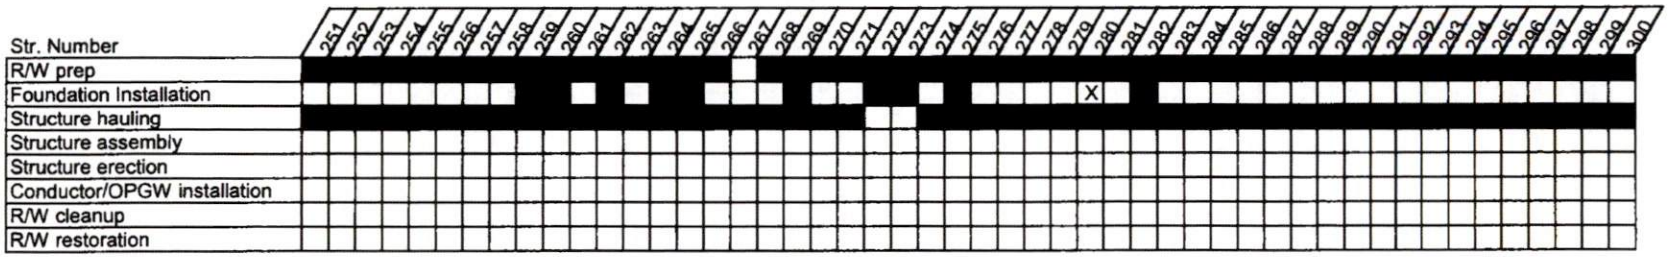
Str. Number
251 252 253 254 255 256 257 258 259 260 261 262 263 264 265 266 267 268 269 270 271 272 273 274 275 276 277 278 279 280 281 282 283 284 285 286 287 288 289 290 291 292 293 294 295 296 297 298 299 300
R/W prep
Foundation Installation
X
Structure hauling
Structure assembly
Structure erection
Conductor/OPGW installation
R/W cleanup
R/W restoration

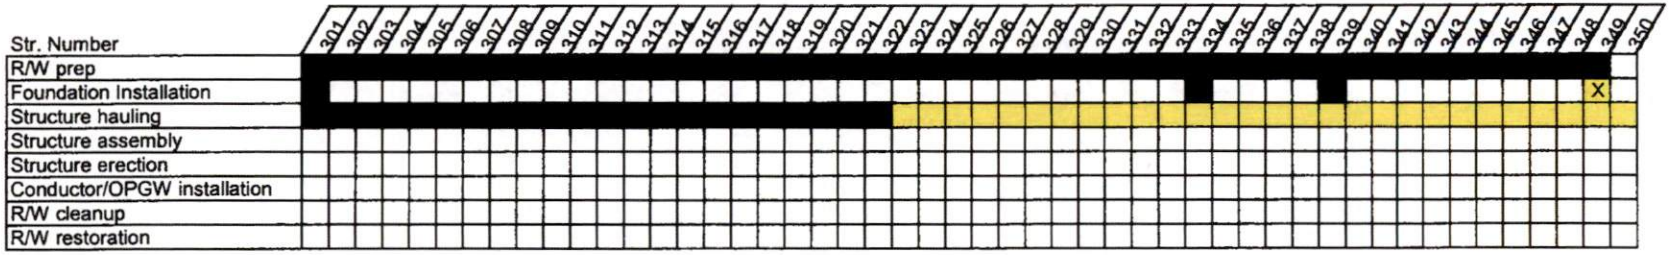
Str. Number
301 302 303 304 305 306 307 308 309 310 311 312 313 314 315 316 317 318 319 320 321 322 323 324 325 326 327 328 329 330 331 332 333 334 335 336 337 338 339 340 341 342 343 344 345 346 347 348 349 350
R/W prep
Foundation Installation
X
Structure hauling
Structure assembly
Structure erection
Conductor/OPGW installation
R/W cleanup
R/W restoration

| Str. Number | 351 | 352 | 353 | 354 | 355 | 356 | 357 | 358 | 359 | 360 | 361 | 362 | 363 | 364 | 365 | 366 | 367 | 368 | 369 | 370 | 371 | 372 | 373 | 374 | 375 | 376 | 377 | 378 | 379 | 380 | 381 | 382 | 383 | 384 | 385 | 386 | 387 | 388 | 389 | 390 | 391 | 392 | 393 | 394 | 395 | 396 | 397 | 398 | 399 | 400 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| R/W prep | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Foundation Installation | | | | | | | | | | | | | | | X | X | | | X | | | | | X | | | | | | | | | | | | X | | | | | | | X | | X | | | X | X |
| Structure hauling | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Structure assembly | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Structure erection | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Conductor/OPGW installation | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| R/W cleanup | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| R/W restoration | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

| Str. Number | 401 | 402 | 403 | 404 | 405 | 406 | Takeoff |
|---|---|---|---|---|---|---|---|
| R/W prep | | | | | | | |
| Foundation Installation | | | X | | X | | |
| Structure hauling | | | | | | | |
| Structure assembly | | | | | | | |
| Structure erection | | | | | | | |
| Conductor/OPGW installation | | | | | | | |
| R/W cleanup | | | | | | | |
| R/W restoration | | | | | | | |

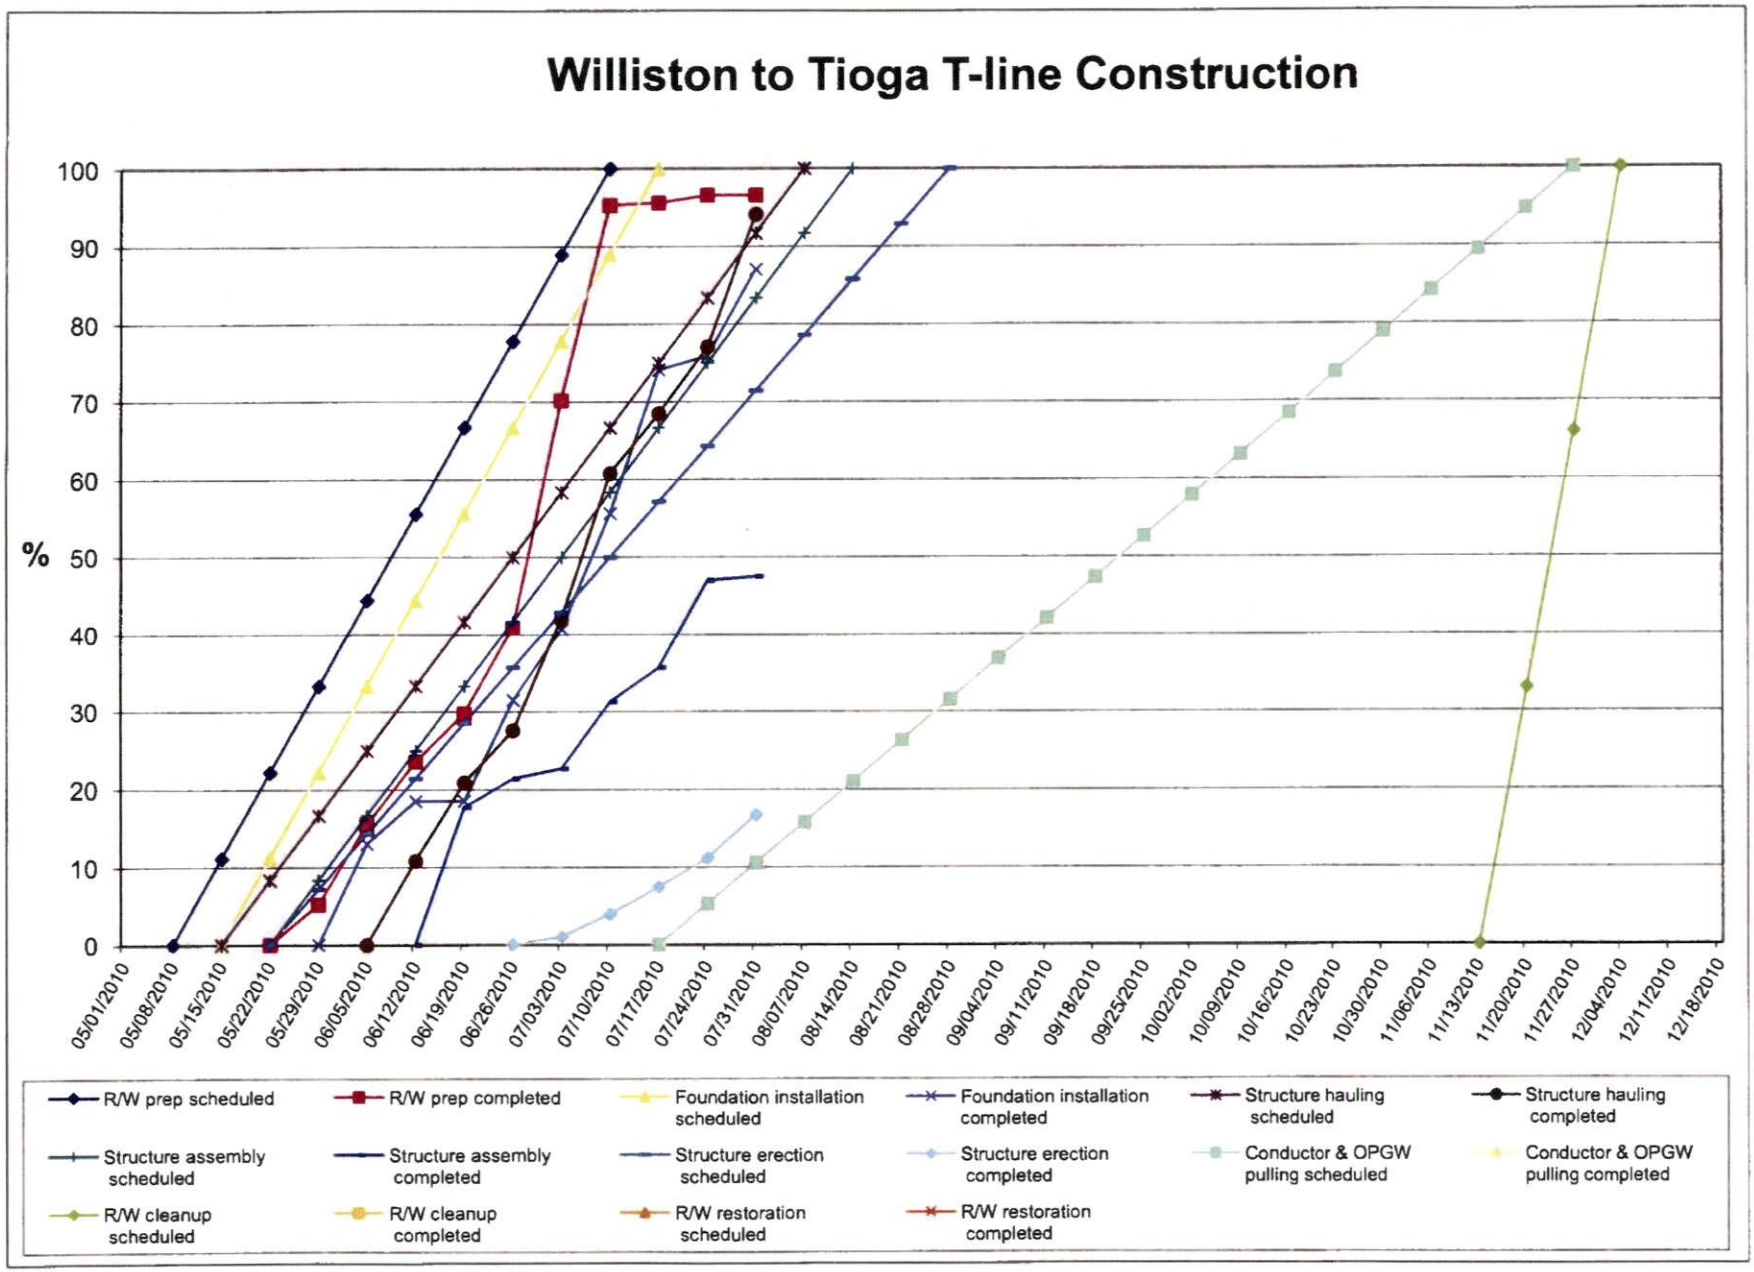
Williston to Tioga T-line Construction
%
100
90
80
70
60
50
40
30
20
10
0
05/01/2010
05/08/2010
05/15/2010
05/22/2010
05/29/2010
06/05/2010
06/12/2010
06/19/2010
06/26/2010
07/03/2010
07/10/2010
07/17/2010
07/24/2010
07/31/2010
08/07/2010
08/14/2010
08/21/2010
08/28/2010
09/04/2010
09/11/2010
09/18/2010
09/25/2010
10/02/2010
10/09/2010
10/16/2010
10/23/2010
10/30/2010
11/06/2010
11/13/2010
11/20/2010
11/27/2010
12/04/2010
12/11/2010
12/18/2010
R/W prep scheduled
R/W prep completed
Foundation installation scheduled
Foundation installation completed
Structure hauling scheduled
Structure hauling completed
Structure assembly scheduled
Structure assembly completed
Structure erection scheduled
Structure erection completed
Conductor & OPGW pulling scheduled
Conductor & OPGW pulling completed
R/W cleanup scheduled
R/W cleanup completed
R/W restoration scheduled
R/W restoration completed
