BASIN ELECTRIC POWER COOPERATIIVE
Project: Williston to Tioga T-line Contract
Contractor: Great Southwestern

Weekly Progress Report

Progress for the week ending : 10/16/2010

Manpower = 27

Note:
Completion the past week
Completion to date
X - indicates a foundation location
Str.#1 @ Williston and Str #406 @ Tioga

	Weekly total	Weekly %	Cumulative total	Cumulative %
R/W Prep	0	0.0	406	100.0
Foundation Inst'l. (54)	0	0.0	54	100.0
Structure hauling	0	0.0	406	100.0
Structure assembly	0	0.0	359	88.4
Structure erection	42	10.3	357	87.9
Conductor/OPGW installation	44	10.8	235	57.9
R/W cleanup	31	7.6	174	42.9
R/W restoration		0.0		0.0

81 PU-07-671 Filed: 10/18/2010 Pages: 4
Williston to Tioga Basin Electric T-line Progress
report week ending 10-16-2010
Basin Electric Power Cooperative

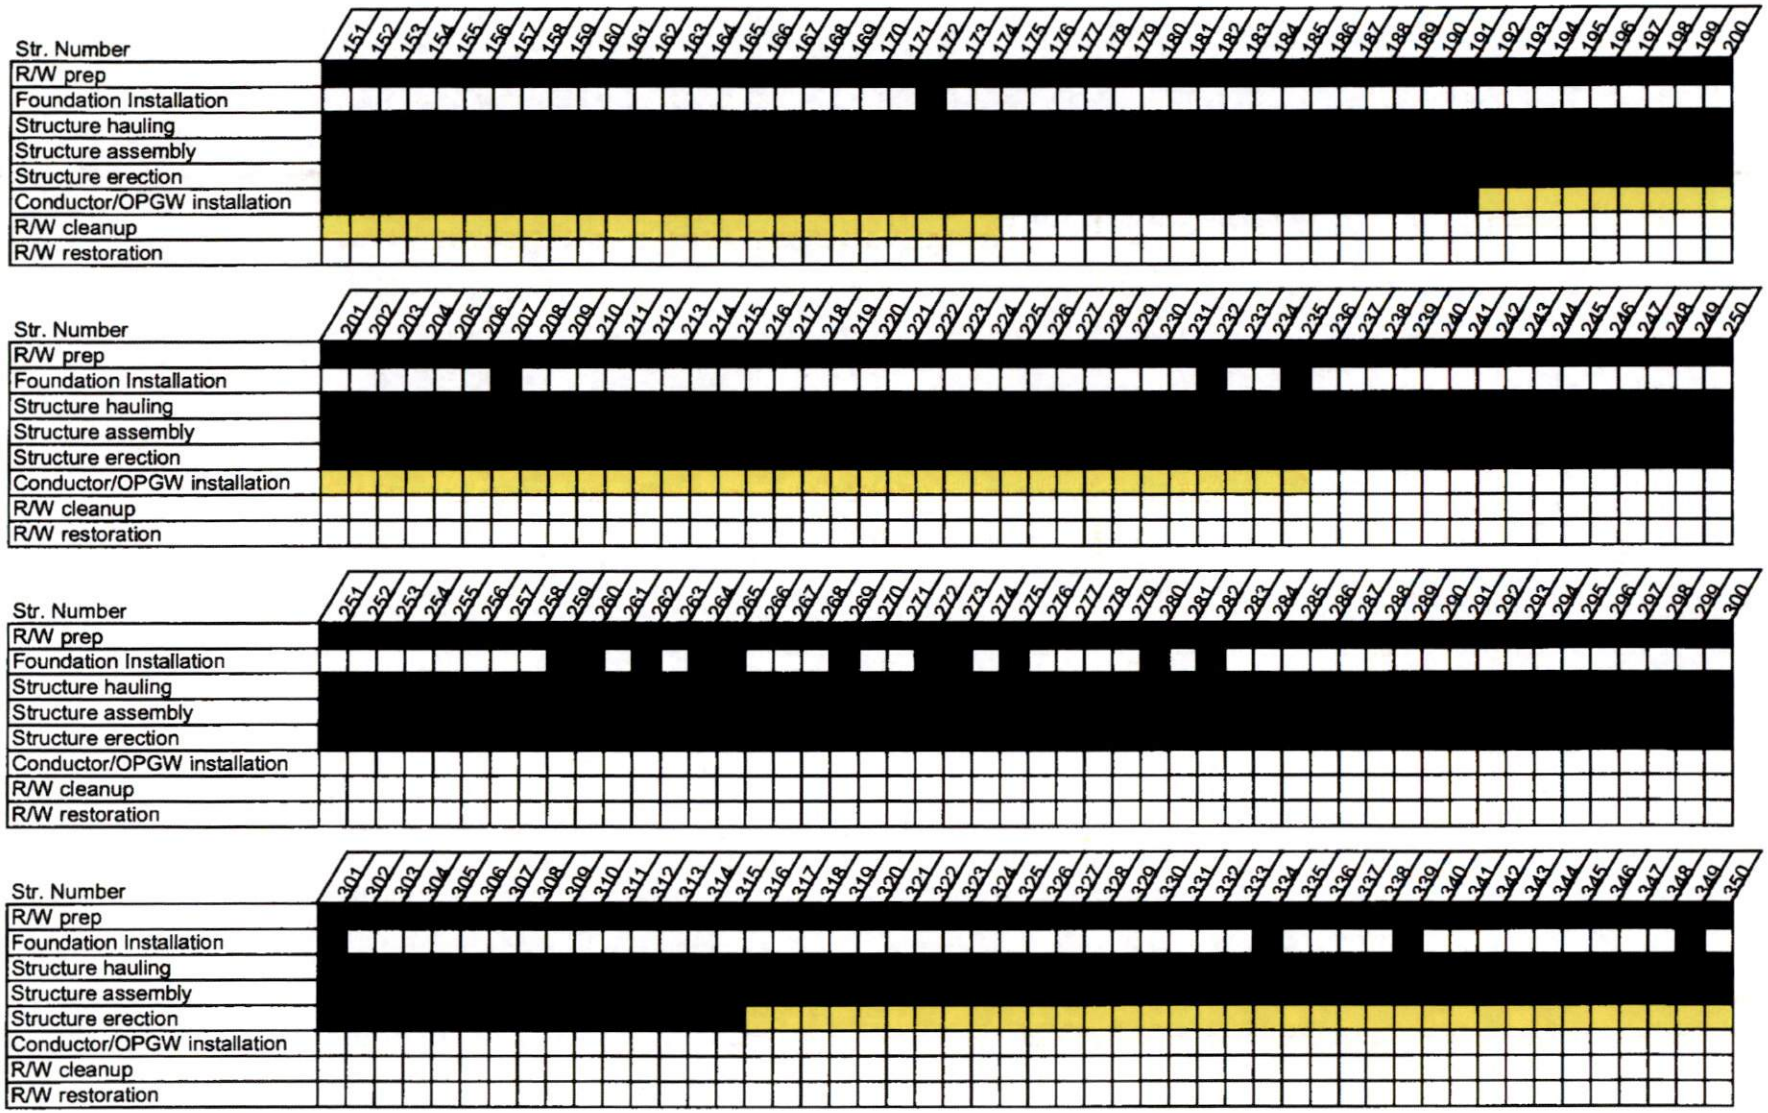
Str. Number
R/W prep
Foundation Installation
Structure hauling
Structure assembly
Structure erection
Conductor/OPGW installation
R/W cleanup
R/W restoration

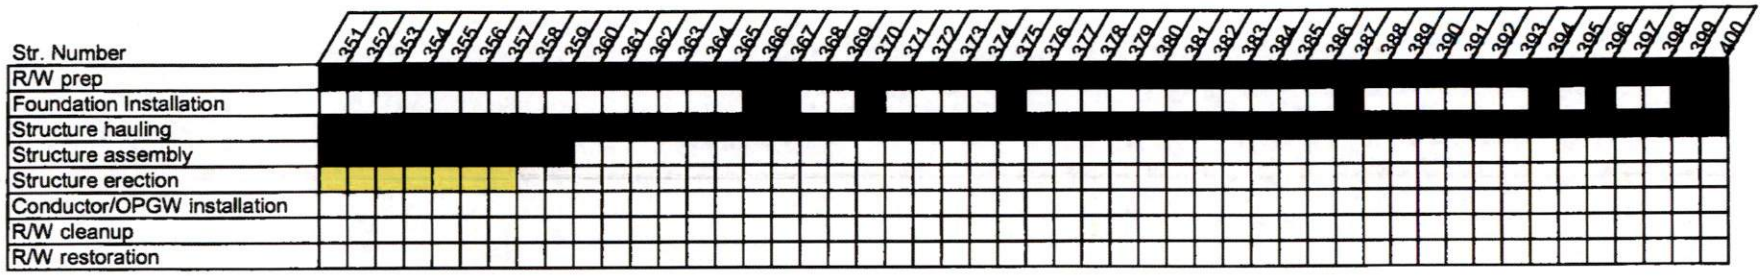
Str. Number
351 352 353 354 355 356 357 358 359 360 361 362 363 364 365 366 367 368 369 370 371 372 373 374 375 376 377 378 379 380 381 382 383 384 385 386 387 388 389 390 391 392 393 394 395 396 397 398 399 400
R/W prep
Foundation Installation
Structure hauling
Structure assembly
Structure erection
Conductor/OPGW installation
R/W cleanup
R/W restoration

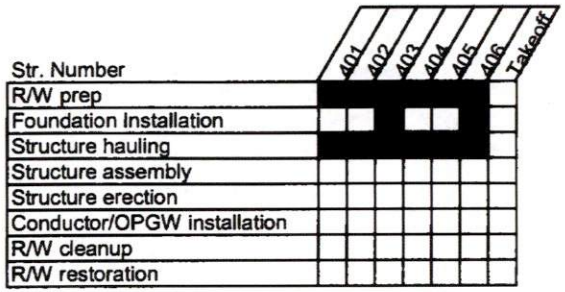
Str. Number
401 402 403 404 405 406 Takeoff
R/W prep
Foundation Installation
Structure hauling
Structure assembly
Structure erection
Conductor/OPGW installation
R/W cleanup
R/W restoration
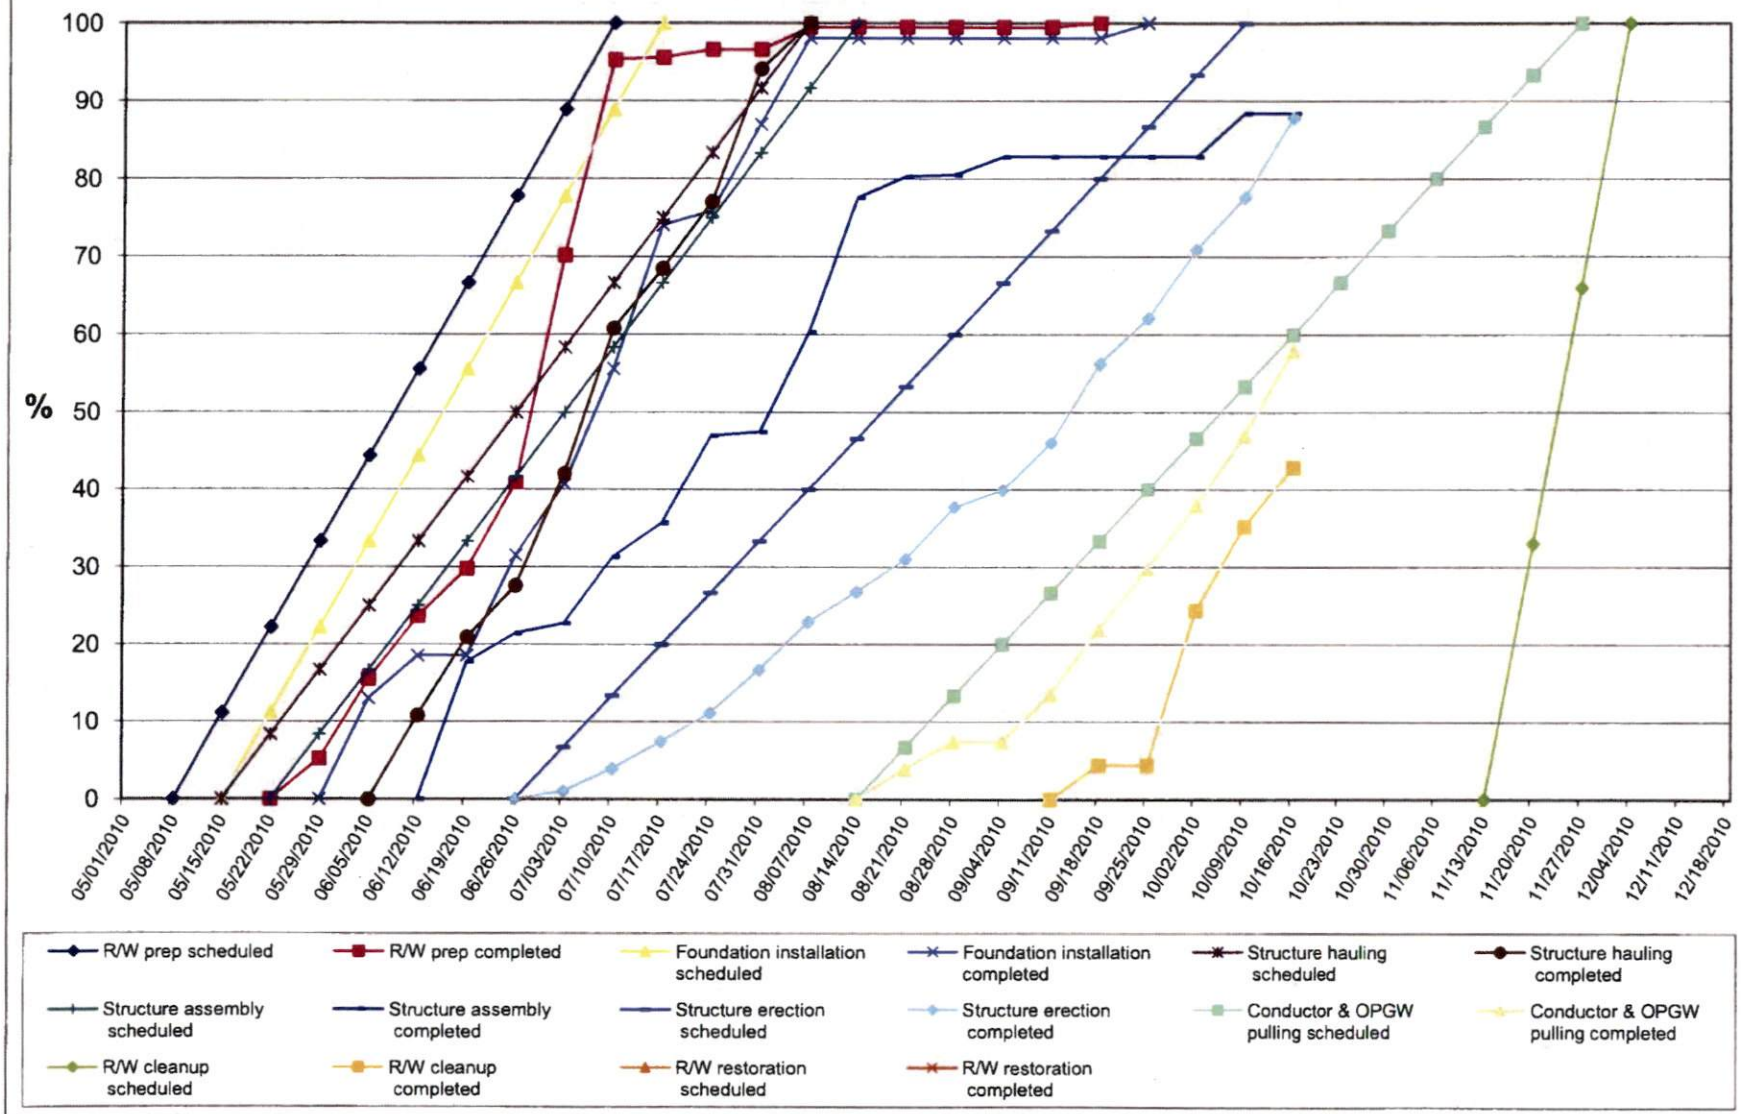
Williston to Tioga T-line Construction (Rev. 1)
