**BASIN ELECTRIC POWER COOPERATIIVE**
**Project: Williston to Tioga T-line Contract**
**Contractor: Great Southwestern**

**Weekly Progress Report**

Progress for the week ending : 06/18/2011

Manpower = 0

Note:
Completion the past week

Completion to date

X - indicates a foundation location

Str.#1 @ Williston and Str #406 @ Tioga

| | Weekly total | Weekly % | Cumulative total | Cumulative % |
|---|---|---|---|---|
| R/W Prep | | 0.0 | 406 | 100.0 |
| Foundation Inst'l. (54) | | 0.0 | 54 | 100.0 |
| Structure hauling | | 0.0 | 406 | 100.0 |
| Structure assembly | | 0.0 | 406 | 100.0 |
| Structure erection | | 0.0 | 406 | 100.0 |
| Conductor/OPGW installation | | 0.0 | 406 | 100.0 |
| R/W cleanup | | 0.0 | 406 | 100.0 |
| R/W restoration | 0 | 0.0 | 185 | 45.6 |
| | | | | |

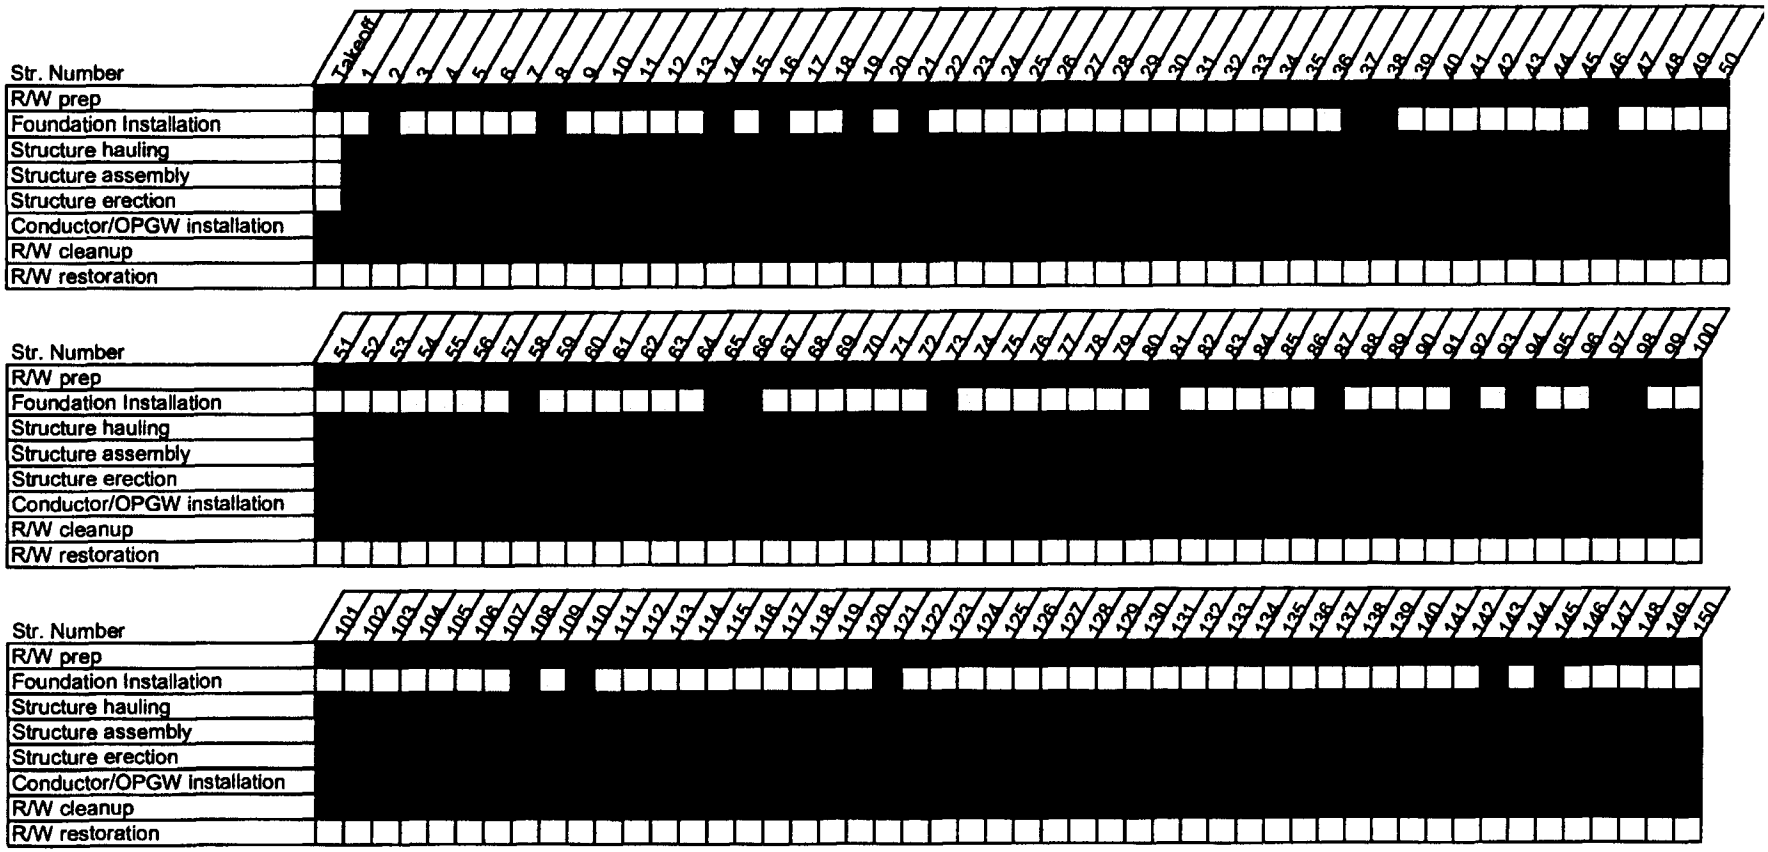


95 PU-07-671 Filed: 6/20/2011 Pages: 4
Williston to Tioga Basin Electric T-line Progress report week ending 6-18-2011
Basin Electric Power Cooperative

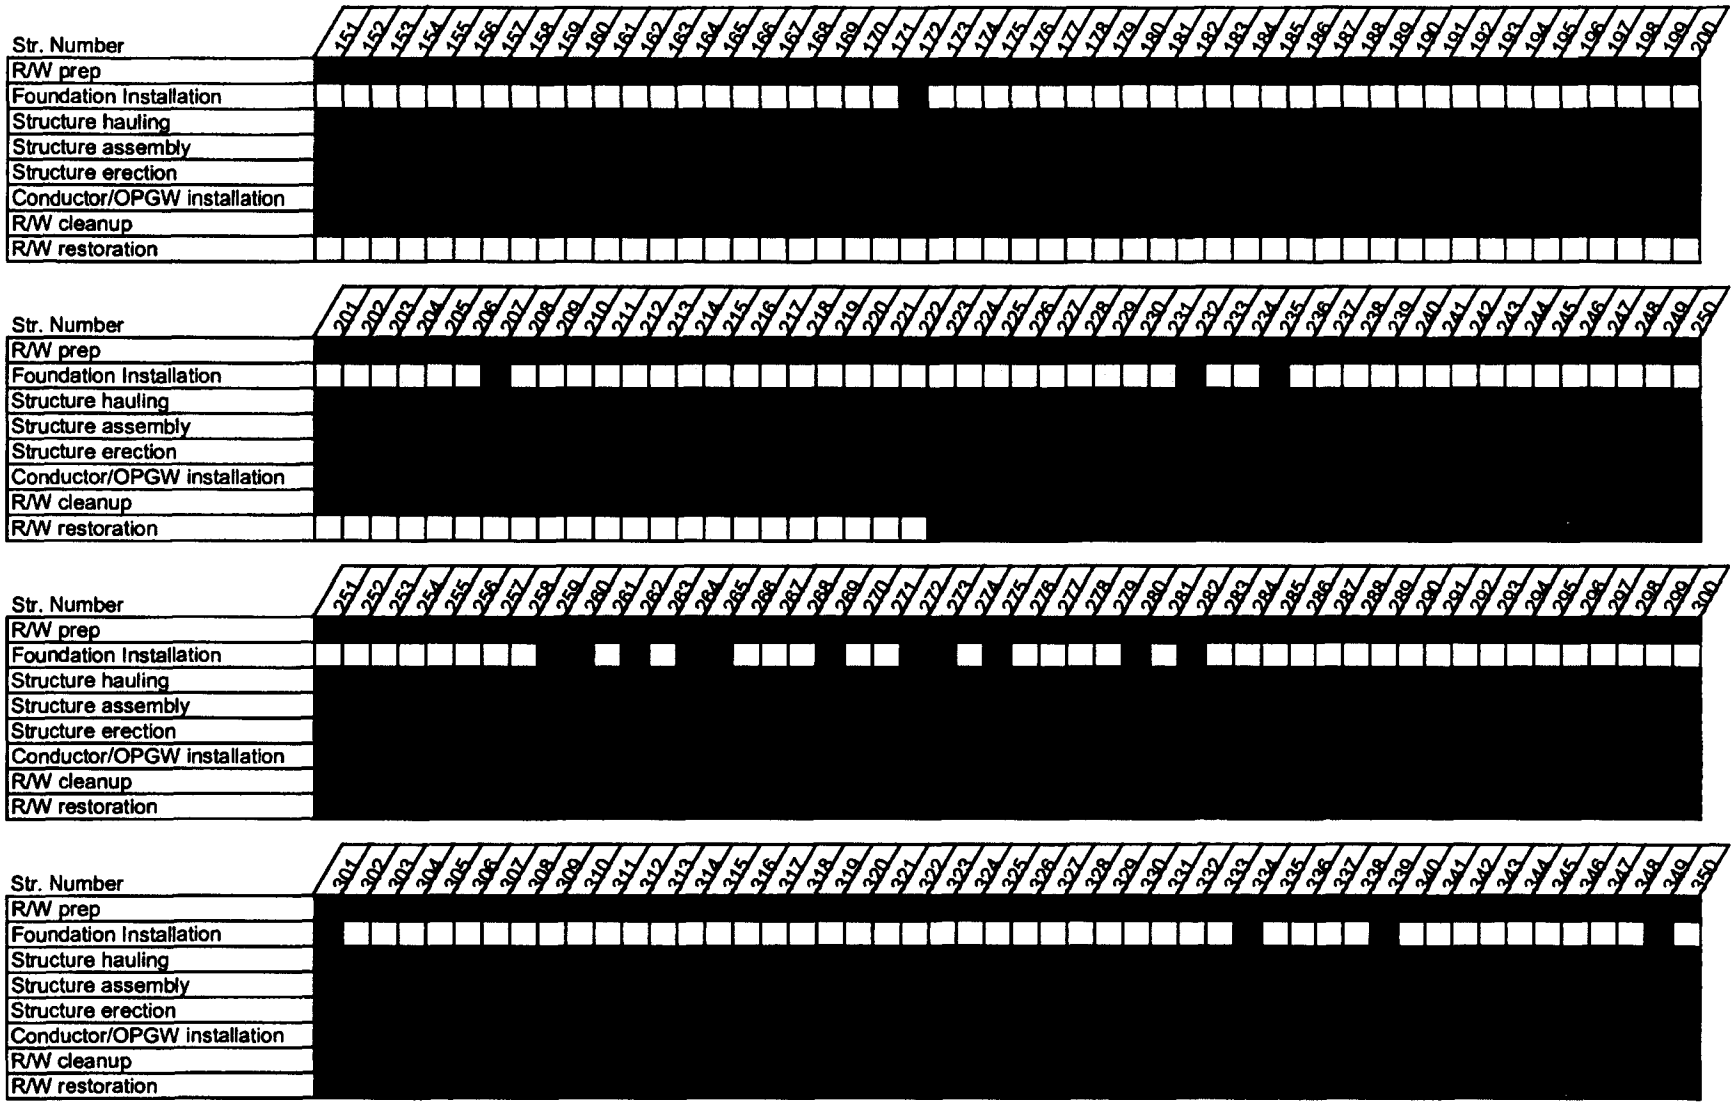
Str. Number
R/W prep
Foundation Installation
Structure hauling
Structure assembly
Structure erection
Conductor/OPGW installation
R/W cleanup
R/W restoration

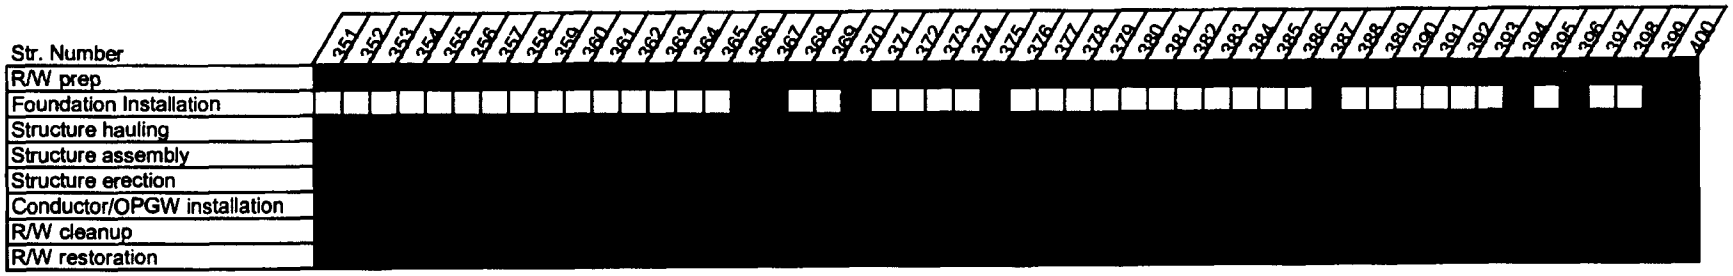
Str. Number
351
352
353
354
355
356
357
358
359
360
361
362
363
364
365
366
367
368
369
370
371
372
373
374
375
376
377
378
379
380
381
382
383
384
385
386
387
388
389
390
391
392
393
394
395
396
397
398
399
400
R/W prep
Foundation Installation
Structure hauling
Structure assembly
Structure erection
Conductor/OPGW installation
R/W cleanup
R/W restoration

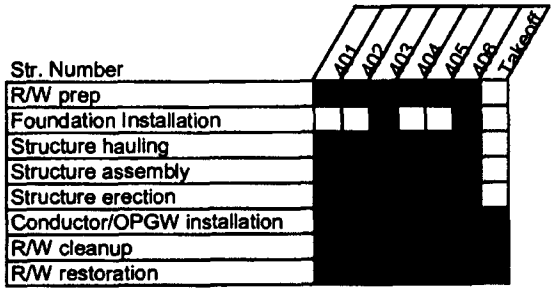
Str. Number
401
402
403
404
405
406
Takeoff
R/W prep
Foundation Installation
Structure hauling
Structure assembly
Structure erection
Conductor/OPGW installation
R/W cleanup
R/W restoration
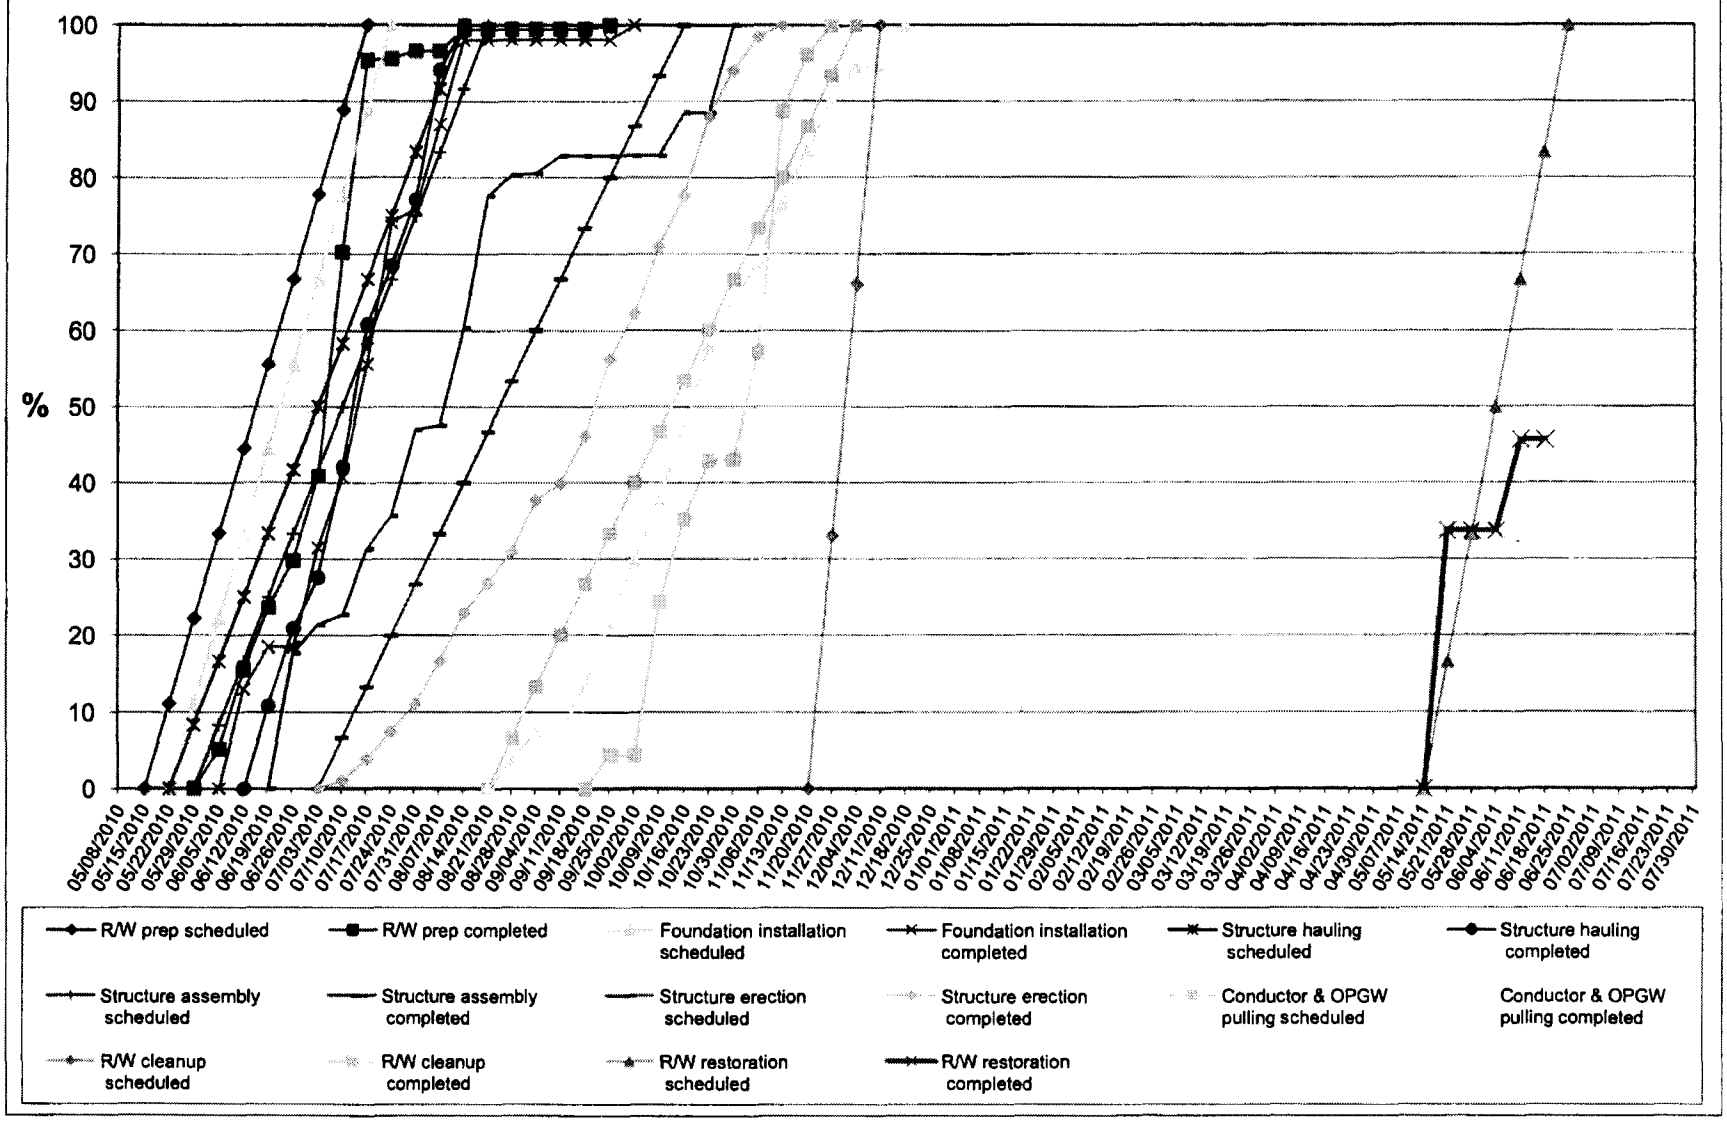
# Williston to Tioga T-line Construction (Rev. 1)
