FPL ENERGY LANGDON WIND II, LLC
LANGDON, NORTH DAKOTA

Plan of the Day (POD)

Weather Forecast: Partly Sunny
High: 80°F **Low:** 54°F
Winds: NNW @ 5 mph
Precipitation Chances: 44 %

Thursday, July 31, 2008 **COD - 09/26/08** **58 Days to COD**

FPL Energy | Wanzek | GEWE

Safety/Environmental:
- Site wide safety meeting every Tuesday at 7:00 a.m.
- SWPPP inspection scheduled for August 6th
- Hydration
- Adhere to speed limits
- Be aware of gravel trucks & heavy equipment in area

Civil:
- Foundations & Pedestals complete
- Foundation backfill at L2-6, L2-8 & L2-9
- Crane pad at L2-10 – L2-12

Erection:
- Grout Base L2-22 & L2-23
- Erect Base tower section L2-22 & L2-23
- Erect Mid tower section L2-22 & L2-23
- Assemble Rotor at L2-24 & L2-25
- Offloading DTA's, tower sections, blades & nacelle

Electrical:
- Installing Transformer box pads at L2-1– L2-3 & L2-10-L2-12
- Backfilling box pad
- Foundation grounding at L2-8 & L2-9
- Prep towers before erection

Collection:
- Collection cable from J Box to L2-22 & L2-23 & West to substation

Substation:
- NASS crew is prepping HICO transformer

Monthly Management Meeting Today

Receiving (As of COB yesterday)			
	Total	Rec'd	Balance
PMT XFR	28	28	0
Grounding XFR	2	2	0
4/0 Cable	315,000	300,692	14,308
1000KM	49,038	54,982	-5,944
500KM	54,000	56,020	-2,020
12 Fiber SM	134,000	140,798	-6,798
1000 KCM (LVC)	12,500	12,140	360
Grounding XFR boxp	2	2	0
XFR Box Pads	28	28	0
Junction Boxes	9	9	0
Bases	27	12	15
Mids	27	13	14
Tops	27	13	14
Machine Heads	27	10	17
Contollers (DTA's)	27	24	3
Blade Sets	27	13	14
Hubs	27	14	13

General Construction Status

76 PU-07-722 Filed 07/31/2008 Pages: 1
Langdon Wind Plan of the Day, July 31, 2008
Langdon Wind, LLC

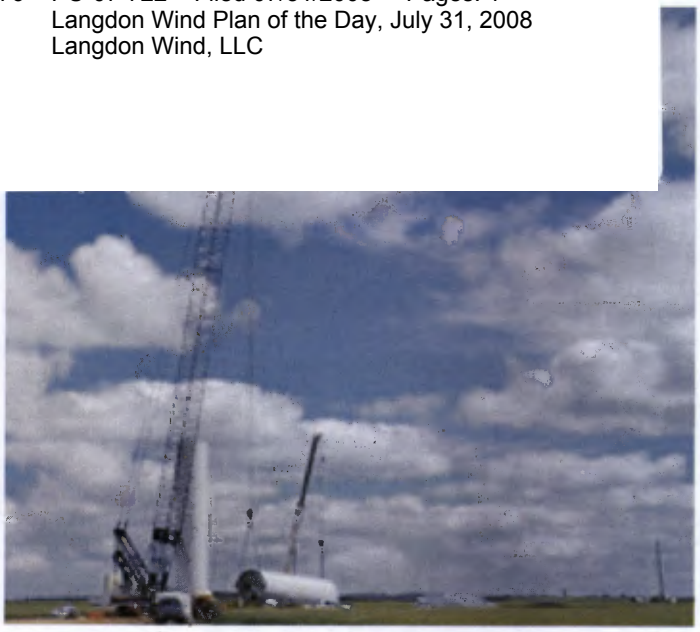

	Complete	Total	% Complete
Roads Subgraded	43,080	43,080	100.0%
Roads Complete	43,080	43,080	100.0%
Foundations Excavated	27	27	100.0%
Foundations Poured	27	27	100.0%
Foundations Backfilled	24	27	88.9%
Crane Pads Complete	15	27	55.6%
Tower Base Sections Erected	7	27	25.9%
Tower Mid Sections Erected	7	27	25.9%
Tower Top Sections Erected	0	27	0.0%
Machine Heads Installed	0	27	0.0%
Rotors Flown	0	27	0.0%
Mechanically Completed	0	27	0.0%
Pre-Commissioned	0	27	0.0%
Final Commissioned	0	27	0.0%
Cable Installed 4/0	24,188	315,000	7.7%
Cable Installed 1000 KM	5,084	45,000	11.3%
Cable Installed 500 KM	6,596	54,000	12.2%
Fiber-Optic 12 Fiber SM	34,690	134,000	25.9%
Transformers Set	13	28	46.4%
Transformers Terminated	0	28	0.0%
(as of COB yesterday)			

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE
