FPL ENERGY LANGDON WIND II, LLC
LANGDON, NORTH DAKOTA

Plan of the Day (POD)

Weather Forecast: Sunny
High: 83 F **Low:** 48 F
Winds: SSE @ 14 mph
Precipitation Chances: 1 %

Tuesday, August 26, 2008 **COD - 09/26/08** **32 Days to COD**

FPL Energy **Wanzek** **GEWE**

Safety/Environmental:
- Site wide safety meeting every Tuesday at 7:00 a.m.
- SWPPP inspection scheduled for September 3rd
- Climbing safety
- Crane safety awareness
- Hydration
- Road Construction Awareness

Erection:
- Offloading base tower section
- Erect mid at L2-6
- Mobilizing 2500 Demag to L2-10 - L2-12

Electrical:
- Terminating DTA's
- Tower wiring & bus bar terminating

Collection:
- Fiber Splicing
- Testing ground grid

Substation:
- Construction at 85% complete
- Installing Fence

Monthly Management Meeting is scheduled for Thursday September 4, 2008

Receiving (As of COB yesterday)			
	Total	Rec'd	Balance
PMT XFR	28	28	0
Grounding XFR	2	2	0
4/0 Cable	315,000	300,692	14,308
1000KM	49,038	54,982	-5,944
500KM	54,000	56,020	-2,020
12 Fiber SM	134,000	140,798	-6,798
1000 KCM (LVC)	12,500	12,140	360
Grounding XFR boxp	2	2	0
XFR Box Pads	28	28	0
Junction Boxes	9	9	0
Bases	27	26	1
Mids	27	27	0
Tops	27	27	0
Machine Heads	27	27	0
Contollers (DTA's)	27	27	0
Blade Sets	27	27	0
Hubs	27	27	0

General Construction Status

96 PU-07-722 Filed 08/26/2008 Pages: 1
Langdon Wind Plan of the Day, Aug. 26, 2008
Langdon Wind, LLC

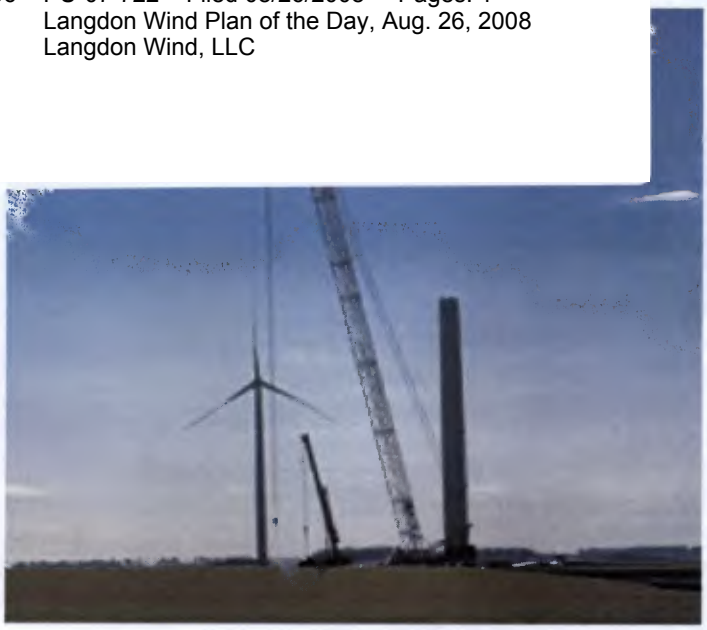

	Complete	Total	% Complete
Roads Subgraded	43,080	43,080	100.0%
Roads Complete	43,080	43,080	100.0%
Foundations Excavated	27	27	100.0%
Foundations Poured	27	27	100.0%
Foundations Backfilled	27	27	100.0%
Crane Pads Complete	27	27	100.0%
Tower Base Sections Erected	24	27	88.9%
Tower Mid Sections Erected	23	27	85.2%
Tower Top Sections Erected	15	27	55.6%
Machine Heads Installed	15	27	55.6%
Rotors Flown	15	27	55.6%
Mechanically Completed	1	27	3.7%
Pre-Commissioned	0	27	0.0%
Final Commissioned	0	27	0.0%
Cable Installed 4/0	83,902	83,370	100.6%
Cable Installed 1000 KM	15,481	14,665	105.6%
Cable Installed 500 KM	16,642	16,890	98.5%
Fiber-Optic 12 Fiber SM	123,690	119,175	103.8%
Transformers Set	28	28	100.0%
Transformers Terminated	13	28	46.4%
(as of COB yesterday)			

Plan of the Day contents shall not be forwarded or distributed without prior written consent of FPLE
