Progress Report for Week Ending

Date: 10/17/09

PU-08-75

BASIN ELECTRIC POWER COOPERATIVE
A Touchstone Energy® Cooperative

PrairieWinds 1 Project

	Units Complete	% Complete	08/01/2009	08/08/2009	08/15/2009	08/22/2009	08/29/2009	09/05/2009	09/12/2009	09/19/2009	09/26/2009	10/03/2009	10/10/2009	10/17/2009	10/24/2009	10/31/2009	11/07/2009	11/14/2009	11/21/2009	11/28/2009	12/05/2009	12/12/2009	12/19/2009	12/26/2009	01/02/2010	01/09/2010	01/16/2010	01/23/2010	01/30/2010	02/06/2010	02/13/2010	02/20/2010	02/27/2010	03/06/2010	
			End of Week Units Complete																																
Access Roads	43	56%	0	0	0	2	3	4	2	5	4	9	11	3																					43
Crane Pads	27	35%	0	0	0	0	0	0	0	4	3	10	5	5																					27
Deliver Padmount	77	100%	0	0	0	0	18	29	17	13																									77
Install Padmount	21	27%	0	0	0	0	0	0	0	0	0	0	5	16																					21
Foundation Construction	51	66%	0	0	0	0	0	2	2	6	15	13	8	5																					51
Delivery Turbine Components	24	31%	0	0	0	0	0	0	0	0	0	2	14	8																					24
Set Base & Mid Tower Sections	7	9%	0	0	0	0	0	0	0	0	0	1	1	5																					7
Grout & Bolt Tensioning	2	3%	0	0	0	0	0	0	0	0	0	0	0	2																					2
Set Tower Top, Nacelle, Rotor	1	1%	0	0	0	0	0	0	0	0	0	0	0	1																					1
Tower Wiring & Mech. Completion	0	0%	0	0	0	0	0	0	0	0	0	0	0	0																					0

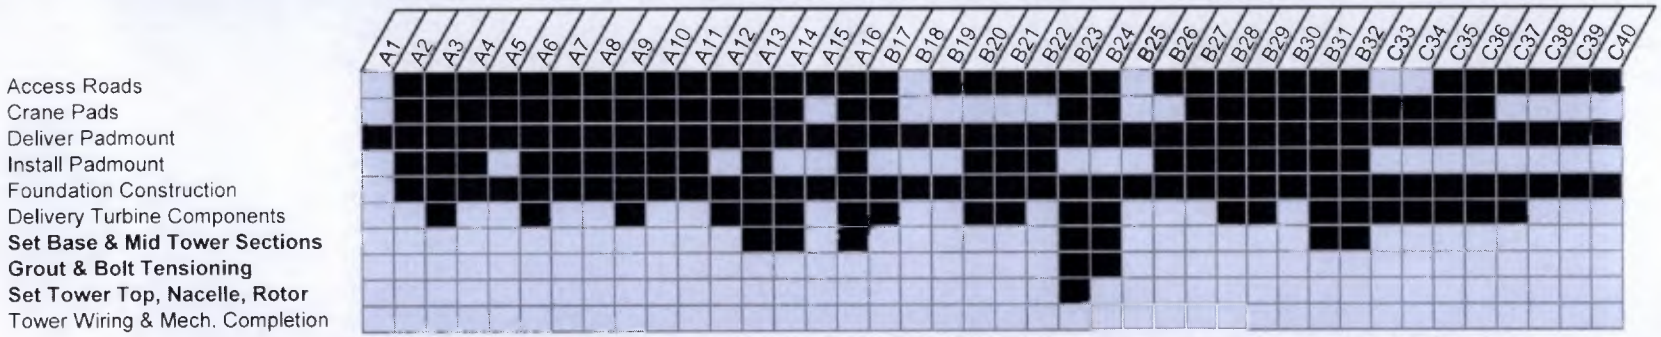

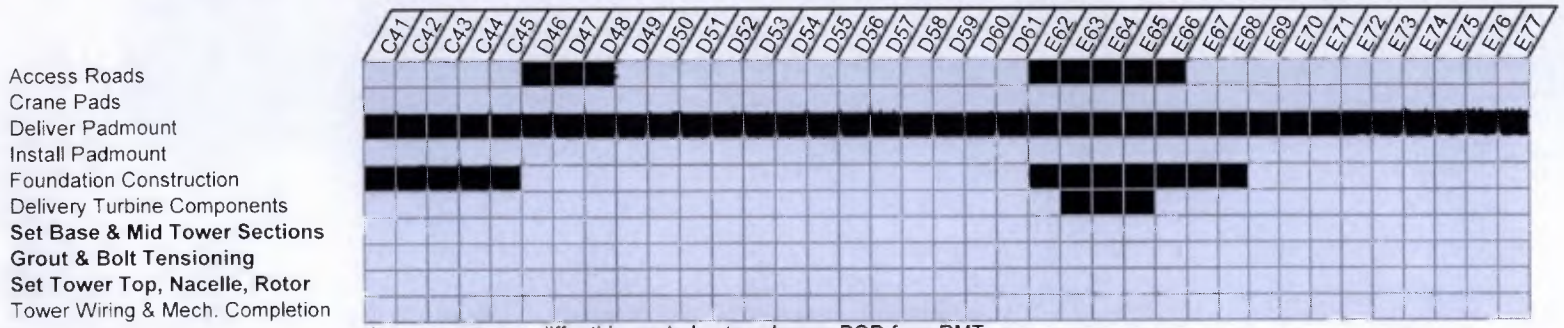

* man power may differ this week due to unknown POD from RMT

Wind Connect Staffing	130	Subcontractor Staffing	47
Management	8	Building Dimensions Inc.	10
Safety	3	L & H Utility Contractors Inc.	11
Civil	101	World Wind Services Inc.	4
Electrical	12	TimberLine	12
Logistics / QA	6	Great Western Erectors (rebar)	7
		Brundage Bone Concrete Pumping	3

Complete Unit ----------> ■

57 PU-08-75 Filed: 10/16/2009 Pages: 1
Prairie Winds 1 Project Progress Report for Week Ending 10-17-2009

Basin Electric Power Cooperative
