Progress Report for Week Ending

Date: 11/21/09

PU-08-75

BASIN ELECTRIC POWER COOPERATIVE
A Touchstone Energy Cooperative

PrairieWinds 1 Project

End of Week Units Complete

	Units Complete	% Complete	08/01/2009	08/08/2009	08/15/2009	08/22/2009	08/29/2009	09/05/2009	09/12/2009	09/19/2009	09/26/2009	10/03/2009	10/10/2009	10/17/2009	10/24/2009	10/31/2009	11/07/2009	11/14/2009	11/21/2009	11/28/2009	12/05/2009	12/12/2009	12/19/2009	12/26/2009	01/02/2010	01/09/2010	01/16/2010	01/23/2010	01/30/2010	02/06/2010	02/13/2010	02/20/2010	02/27/2010	03/06/2010	
Access Roads	76	99%	0	0	0	2	3	4	2	5	4	9	11	3	9	10	5	9	0																76
Crane Pads	72	94%	0	0	0	0	0	0	0	4	3	10	5	5	8	7	6	17	7																72
Deliver Padmount	77	100%	0	0	0	0	18	29	17	13																									77
Install Padmount	75	97%	0	0	0	0	0	0	0	0	0	0	5	16	5	6	16	16	11																75
Foundation Construction	77	100%	0	0	0	0	0	2	2	6	15	13	8	5	7	19																			77
Delivery Turbine Components	76	99%	0	0	0	0	0	0	0	0	0	2	14	8	13	9	11	10	9																76
Set Base & Mid Tower Sections	77	100%	0	0	0	0	0	0	0	0	0	1	1	5	4	16	23	17	5																72
Grout & Bolt Tensioning	70	91%	0	0	0	0	0	0	0	0	0	0	0	2	1	13	9	29	16																70
Set Tower Top, Nacelle, Rotor	49	64%	0	0	0	0	0	0	0	0	0	0	0	1	1	9	10	20	8																49
Tower Wiring & Mech. Completion	12	16%	0	0	0	0	0	0	0	0	0	0	0	0	0	0	3	9	0																12

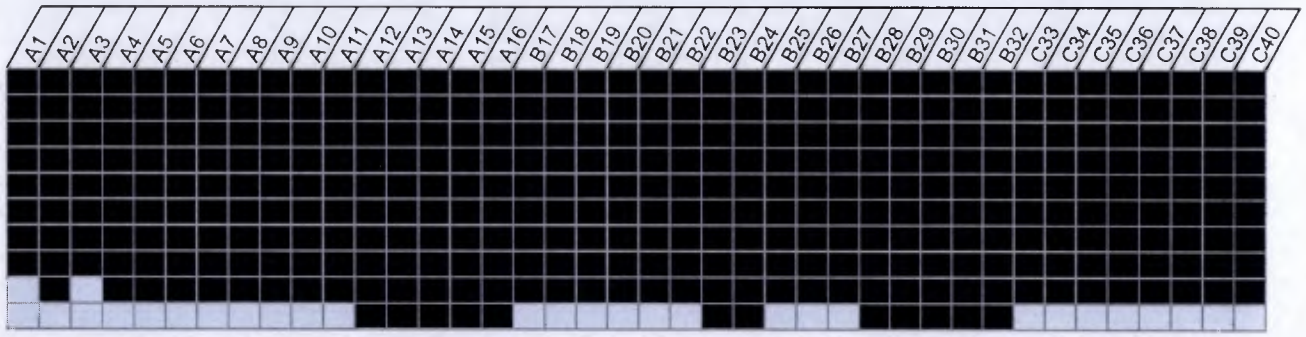

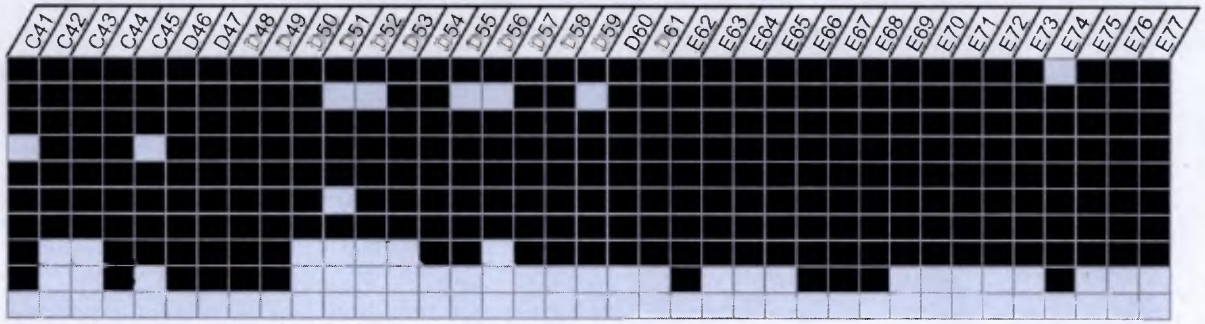

*Access roads to turbines recognised in this report are not final product, as this just reflects access for construction.

Wind Connect Staffing	214	Subcontractor Staffing	57
Management	9	Building Dimensions Inc.	4
Safety	3	L & H Utility Contractors Inc.	17
Civil	179	World Wind Services Inc.	26
Electrical	13	TimberLine	3
Logistics / QA	10	Great Western Erectors (rebar)	4
		Brundage Bone Concrete Pumping	3

Complete Unit ----------> ■

Staffing not accurate due to lack of POD's

65 **PU-08-75** Filed: 11/24/2009 Pages: 1
Prairie Winds 1 Project Progress Report for Week Ending 11-21-2009

Basin Electric Power Cooperative
