Progress Report for Week Ending

Date: 11/28/09

PU-08-75

BASIN ELECTRIC POWER COOPERATIVE
A Touchstone Energy Cooperative

PrairieWinds 1 Project

	Units Complete	% Complete	End of Week Units Complete																																					
			08/01/2009	08/08/2009	08/15/2009	08/22/2009	08/29/2009	09/05/2009	09/12/2009	09/19/2009	09/26/2009	10/03/2009	10/10/2009	10/17/2009	10/24/2009	10/31/2009	11/07/2009	11/14/2009	11/21/2009	11/28/2009	12/05/2009	12/12/2009	12/19/2009	12/26/2009	01/02/2010	01/09/2010	01/16/2010	01/23/2010	01/30/2010	02/06/2010	02/13/2010	02/20/2010	02/27/2010	03/06/2010		
Access Roads	76	99%	0	0	0	2	3	4	2	5	4	9	11	3	9	10	5	9	0	0																			76	
Crane Pads	77	100%	0	0	0	0	0	0	0	4	3	10	5	5	8	7	6	17	7	5																			77	
Deliver Padmount	77	100%	0	0	0	0	18	29	17	13																													77	
Install Padmount	77	100%	0	0	0	0	0	0	0	0	0	0	5	16	5	6	16	16	11	2																			77	
Foundation Construction	77	100%	0	0	0	0	0	2	2	6	15	13	8	5	7	19																							77	
Delivery Turbine Components	77	100%	0	0	0	0	0	0	0	0	0	2	14	8	13	9	11	10	9	1																			77	
Set Base & Mid Tower Sections	77	100%	0	0	0	0	0	0	0	0	0	1	1	5	4	16	23	17	5	5																			77	
Grout & Bolt Tensioning	77	100%	0	0	0	0	0	0	0	0	0	0	0	2	1	13	9	29	16	7																			77	
Set Tower Top, Nacelle, Rotor	66	86%	0	0	0	0	0	0	0	0	0	0	0	1	1	9	10	20	8	17																			66	
Tower Wiring & Mech. Completion	12	16%	0	0	0	0	0	0	0	0	0	0	0	0	0	0	3	9	0	0																			12	

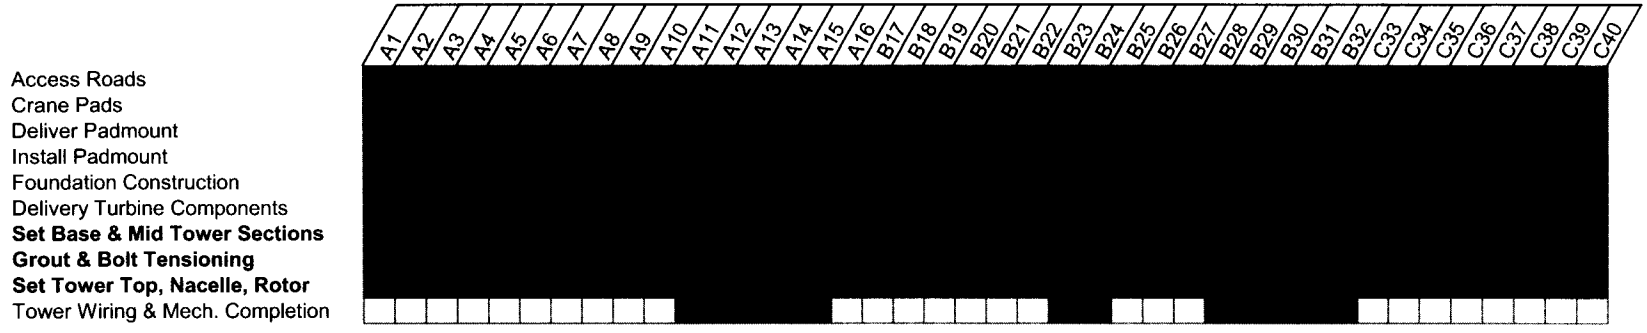

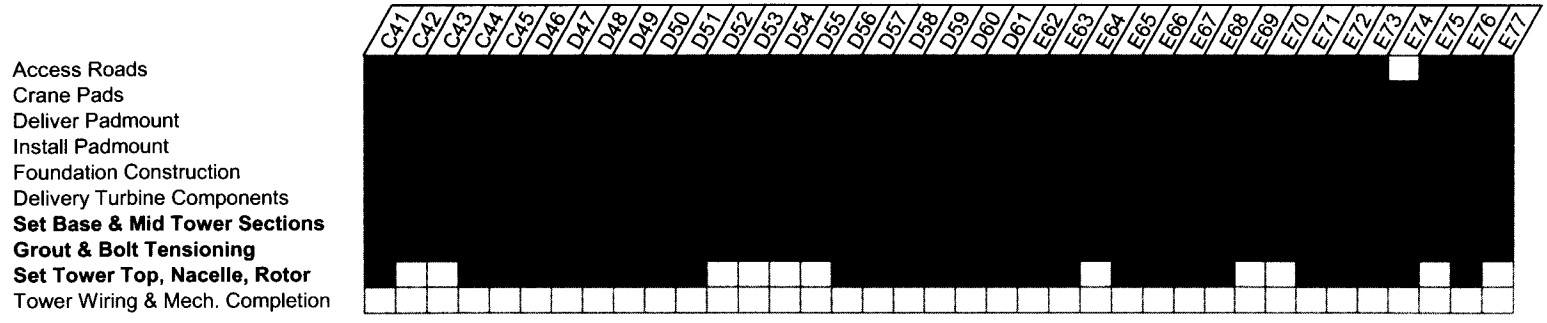

*Access roads to turbines recognised in this report are not final product, as this just reflects access for construction.

Wind Connect Staffing	214
Management	9
Safety	3
Civil	179
Electrical	13
Logistics / QA	10

Subcontractor Staffing	43
Building Dimensions Inc.	0
L & H Utility Contractors Inc.	17
World Wind Services Inc.	26
TimberLine	0
Great Western Erectors (rebar)	0
Brundage Bone Concrete Pumping	0

Complete Unit ----------> ■

Staffing not accurate due to lack of POD's
