Progress Report for Week Ending

Date: 12/05/09

PU-08-75

BASIN ELECTRIC POWER COOPERATIVE
A Touchstone Energy® Cooperative

PrairieWinds 1 Project

	Units Complete	% Complete
Access Roads	77	100%
Crane Pads	77	100%
Deliver Padmount	77	100%
Install Padmount	77	100%
Foundation Construction	77	100%
Delivery Turbine Components	77	100%
Set Base & Mid Tower Sections	77	100%
Grout & Bolt Tensioning	77	100%
Set Tower Top, Nacelle, Rotor	77	100%
Tower Wiring & Mech. Completion	22	29%

End of Week Units Complete

	08/01/2009	08/08/2009	08/15/2009	08/22/2009	08/29/2009	09/05/2009	09/12/2009	09/19/2009	09/26/2009	10/03/2009	10/10/2009	10/17/2009	10/24/2009	10/31/2009	11/07/2009	11/14/2009	11/21/2009	11/28/2009	12/05/2009	12/12/2009	12/19/2009	12/26/2009	01/02/2010	01/09/2010	01/16/2010	01/23/2010	01/30/2010	02/06/2010	02/13/2010	02/20/2010	02/27/2010	03/06/2010	
Access Roads	0	0	0	2	3	4	2	5	4	9	11	3	9	10	5	9	0	0	1														77
Crane Pads	0	0	0	0	0	0	0	4	3	10	5	5	8	7	6	17	7	5															77
Deliver Padmount	0	0	0	0	18	29	17	13																									77
Install Padmount	0	0	0	0	0	0	0	0	0	0	5	16	5	6	16	16	11	2															77
Foundation Construction	0	0	0	0	0	2	2	6	15	13	8	5	7	19																			77
Delivery Turbine Components	0	0	0	0	0	0	0	0	0	2	14	8	13	9	11	10	9	1															77
Set Base & Mid Tower Sections	0	0	0	0	0	0	0	0	0	1	1	5	4	16	23	17	5	5															77
Grout & Bolt Tensioning	0	0	0	0	0	0	0	0	0	0	0	2	1	13	9	29	16	7															77
Set Tower Top, Nacelle, Rotor	0	0	0	0	0	0	0	0	0	0	0	1	1	9	10	20	8	17	11														77
Tower Wiring & Mech. Completion	0	0	0	0	0	0	0	0	0	0	0	0	0	0	3	9	0	0	10														22

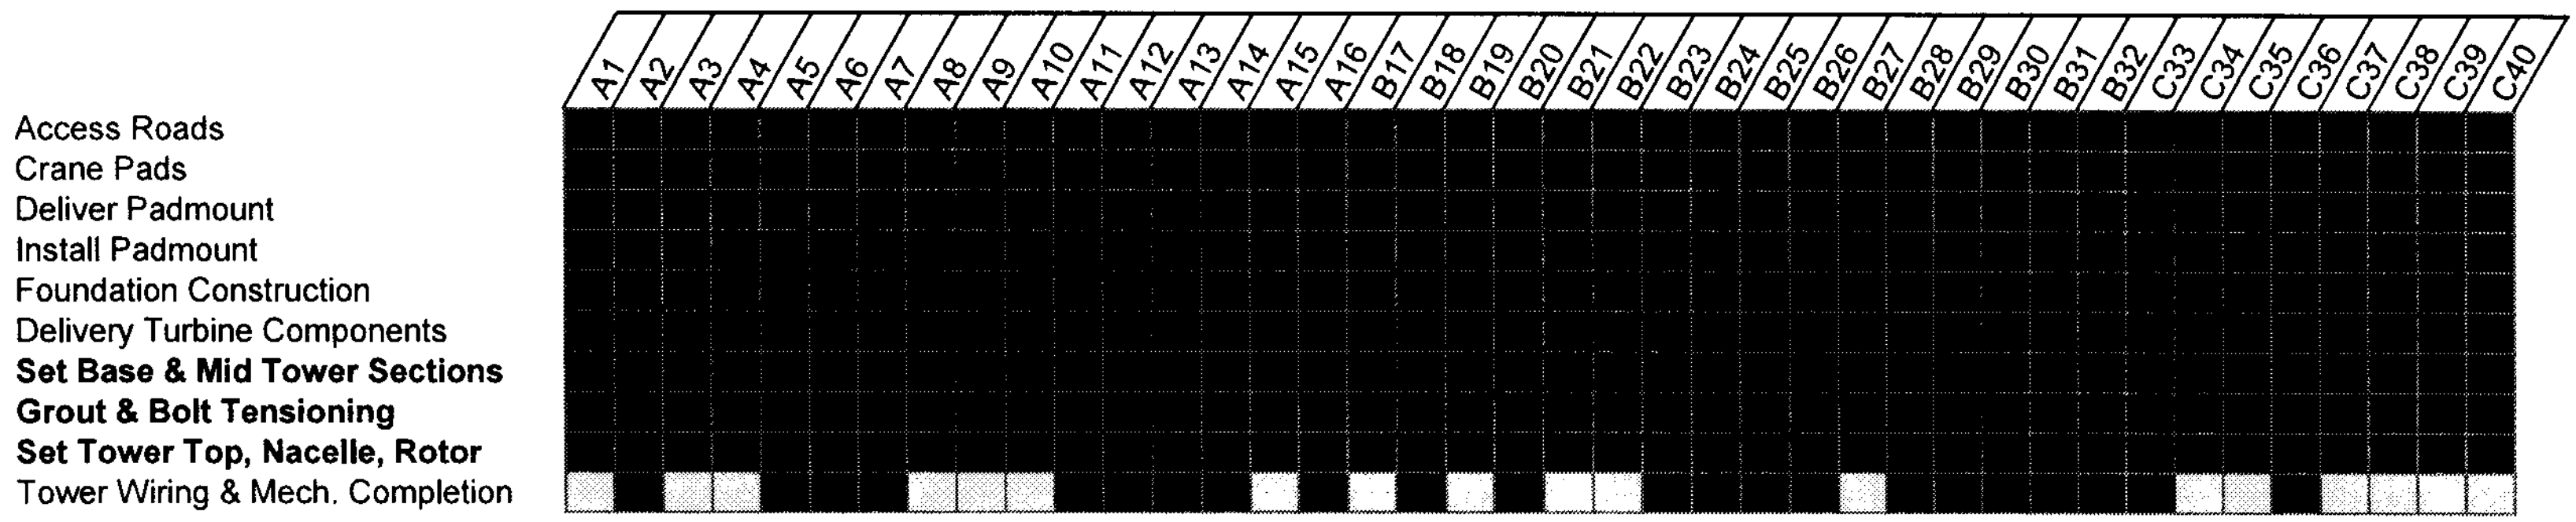

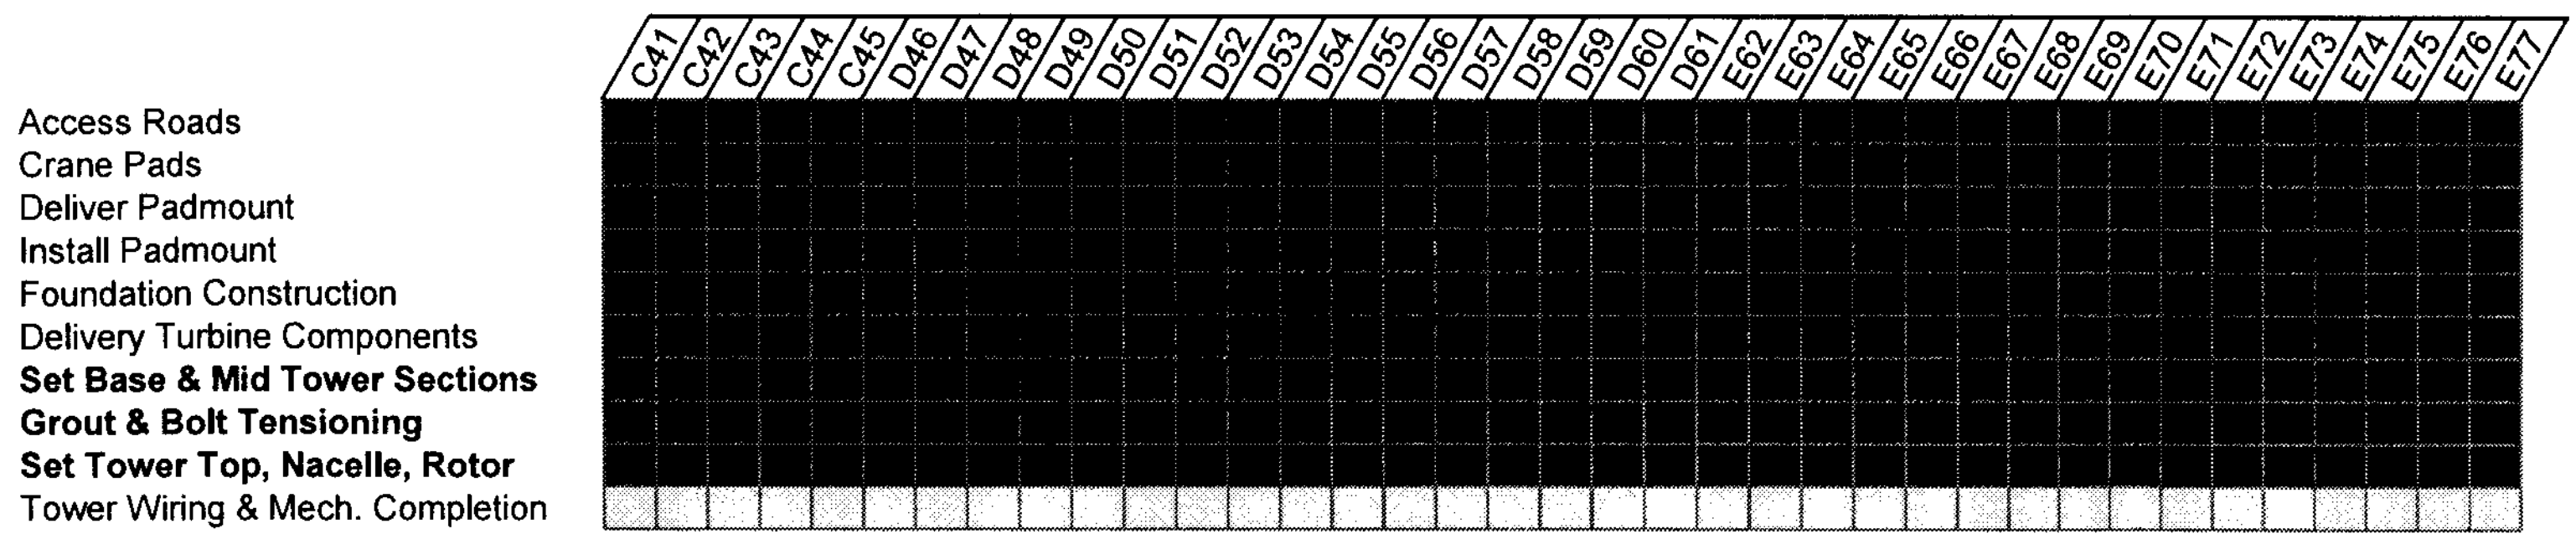

*Access roads to turbines recognised in this report are not final product, as this just reflects access for construction.

Wind Connect Staffing	214	Subcontractor Staffing	62
Management	9	Building Dimensions Inc.	0
Safety	3	L & H Utility Contractors Inc.	17
Civil	179	World Wind Services Inc.	45
Electrical	13	TimberLine	0
Logistics / QA	10	Great Western Erectors (rebar)	0
		Brundage Bone Concrete Pumping	0

Complete Unit ----------------> ■

Staffing not accurate due to lack of POD's

67 **PU-08-75** Filed: 12/7/2009 Pages: 1
Prairie Winds 1 Project Progress Report for Week Ending 12-05-2009
Basin Electric Power Cooperative
