NextEra™ Energy Resources
Ashtabula Wind II

NEXTera Energy

Plan of the Day (POD)

Date: Thursday, 7/16/2009 **COD:** 10-31-09 **Days to COD:** 108
High: 72 **Low:** 45 **Winds:** WNW @ 11 mph
Precipitation Chances: 2% **Weather Forecast:** Cloudy

NextEra™ Energy Resources **Otter Tail** **Blattner Energy** **GE**

Safety/Environmental:
- Wear proper PPE while on the job site
- Use correct procedure when offloading any material
- Keep your speed to a minimum
- Traffic congestion in the north laydown yard, use caution and make sure to have a spotter
- SWPPP inspection
- Wetland markings

Civil/Erection:
- Subgrade at 179-183, & 192-194
- Gravel at 184-187
- Approach at 192

Foundations:
- Excavation on foundation at 185-187
- Mud mat at 185-187
- Install bottom rebar mat at 198-199
- Install anchor bolts at 196-198
- Install top rebar mat at 195-197
- Form base at 195-197

Collection:

Electrical:

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	81	81	0
Grounding XFR	5	5	0
4/0 Cable	441,000	257,812	183,188
500 KCM	36,000	27,755	8,245
Copperclad	84,000	0	84,000
1000 KCM	333,000	274,970	58,030
12 Fiber SM FOC	270,000	135,000	135,000
1000-2km (Low Voltage)	30,500	31,330	-830
XFR Box Pads	81	81	0
Controllers	80	80	0
Bases	80	80	0
Mids	80	80	0
Tops	80	80	0
Nacelles	80	80	0
Hubs	80	80	0
Blade Sets	80	80	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	12,375	117,188	10.6%
Gravel Roads (6")	8,525	117,188	7.3%
Roads Complete	7,025	117,188	6.0%
Silt Fence Installed	5,219	17,700	29.5%
Foundations Excavated	7	80	8.8%
Foundations Poured	0	80	0.0%
Foundations Backfilled	0	80	0.0%
Crane Pads Completed	0	80	0.0%
Tower Base Sections Erected	0	80	0.0%
Tower Mid Sections Erected	0	80	0.0%
Tower Top Sections Erected	0	80	0.0%
Nacelles Installed	0	80	0.0%
Rotors Installed	0	80	0.0%
Tower Wiring Complete	0	80	0.0%
Mechanically Complete	0	80	0.0%
Final Commissioned	0	80	0.0%
4/0 Cable Trenched	0	441,000	0.0%
500 Cable Trenched	0	36,000	0.0%
1000 Cable Trenched	0	333,000	0.0%
Copperclad	0	84,000	0.0%
1000 Low Voltage Trenched	0	30,500	0.0%
Fiber Optic 12 Fiber SM	0	270,000	0.0%
Transformers Set/Terminated	0	80	0.0%

(as of COB yesterday)

Contents shall not be forwarded or distributed without prior written consent of NEXTEra™ Energy Resources

NextEra™ Energy Resources
Ashtabula Wind II

Otter Tail

Plan of the Day (POD)

Date: Thursday, 7/16/2009
High: 72
Precipitation Chances: 2%

COD: 10-15-09
Low: 45

Days to COD: 92
Winds: WNW @ 11 mph
Weather Forecast: Cloudy

NextEra™ Energy Resources | **Otter Tail** | **Blattner Energy** | **GE**

Safety/Environmental:
- Wear proper PPE while on the job site
- Make sure not to use any equipment if it is tagged out
- Narrow roads; use caution when passing
- Keep your speed to a minimum
- Uneven surfaces; use caution when using equipment
- SWPPP inspection

Civil/Erection:

Foundations:
- Pour base at 150 & 152
- Form pedestal at 151, 153 & 154
- Pour pedestal at 153, 154 & 158
- Backfill at 141 & 159
- Build Crane pad at 141, 143-145

Collections:
- Boring at 158-163
- Trench & cable install 4/0 at 139-158

Electrical:
- Pedestal Conduit at 151 & 153
- Smurf tube at 150 & 195
- Grounding Grid at 151 & 153
- Install box pad at 138-142

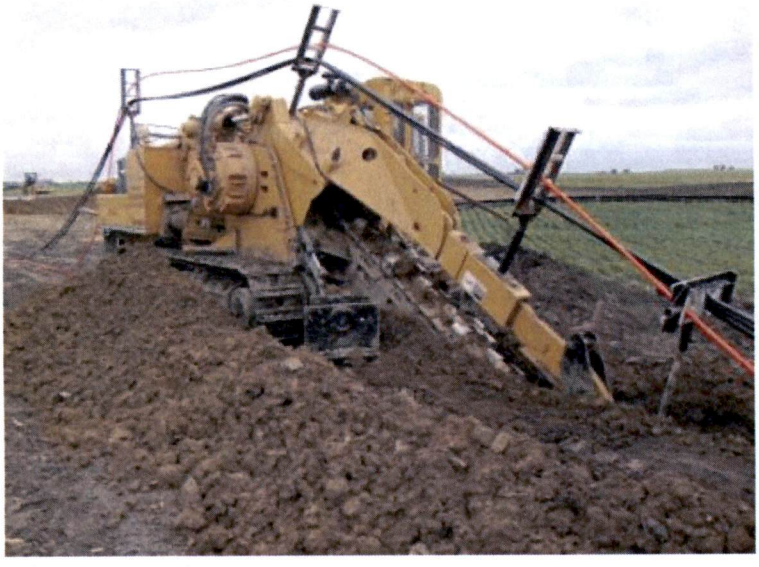

RECEIVING (As of COB yesterday)			
	Total	Received	Balance
PMT XFR	33	0	33
Grounding XFR	3	0	3
4/0 Cable	189,000	122,723	66,277
500 KCM	117,000	120,206	-3,206
1000-2kv (Low Voltage)	12,750	0	12,750
12 Fiber SM FOC	105,000	104,394	606
XFR Box Pads	33	0	33
Controllers	33	0	33
Bases	33	0	33
Mids	33	0	33
Tops	33	0	33
Nacelles	33	0	33
Hubs	33	0	33
Blade Sets	33	0	33
Negative Number Indicates Overage of Cable			

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	41,232	49,614	83.1%
Gravel Road (6")	41,232	49,614	83.1%
Roads Complete	32,975	49,614	66.5%
Silt Fence Installed	10,000	7,300	137.0%
Foundations Excavated	33	33	100.0%
Foundations Poured	24	33	72.7%
Foundations Backfilled	15	33	45.5%
Crane Pads Completed	4	33	12.1%
Tower Base Sections Erected	0	33	0.0%
Tower Mid Sections Erected	0	33	0.0%
Tower Top Sections Erected	0	33	0.0%
Nacelles Installed	0	33	0.0%
Rotors Installed	0	33	0.0%
Tower Wiring Complete	0	33	0.0%
Mechanically Complete	0	33	0.0%
Final Commissioned	0	33	0.0%
4/0 Cable Trenched	20,573	189,000	10.9%
500 Cable Trenched	0	117,000	0.0%
1000 Low Voltage Trenched	0	18,000	0.0%
Fiber Optic 12 Fiber SM	0	105,000	0.0%
Transformers Set/Terminated	0	33	0.0%
(as of COB yesterday)			

Contents shall not be forwarded or distributed without prior written consent of NEXTEra™ Energy Resources
