NEXTera® ENERGY RESOURCES

NextEra™ Energy Resources

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Saturday, 10-2-10
High: 61
Precipitation Chances: 10 %

COD: 11-30-10
Low: 34

Days to COD: 60
Winds: SSE @ 10 mph
Weather Forecast: Sunny

NextEra™ Energy Resources | Blattner Energy | Paradigm | GE

Safety/Environmental:
- Do not go under suspended loads
- Fence off wetland as needed
- Installing silt fence as needed

Civil/Erection:
- Reclaim at 56
- Rotor assembly at 40-41
- Erect base & mid at 42-43
- Erect top, nacelle, & rotor at 33 & 36

Foundations:
- Backfill at 5 & 24
- Build crane pad at 5 & 24

Collection:
- Setting transformer at 18-21 & 23
- Terminating HV at Substation & LV at 52
- DTA to controller terminating at 48-52

Electrical:
- Tower wiring at 32-33
- Mechanical Completion Pre-walk at 53-54

Substation:
- Bus fabrication
- Spread surface rock
- Testing 62 & 64

RECEIVING (As of COB yesterday)

	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	3	3
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

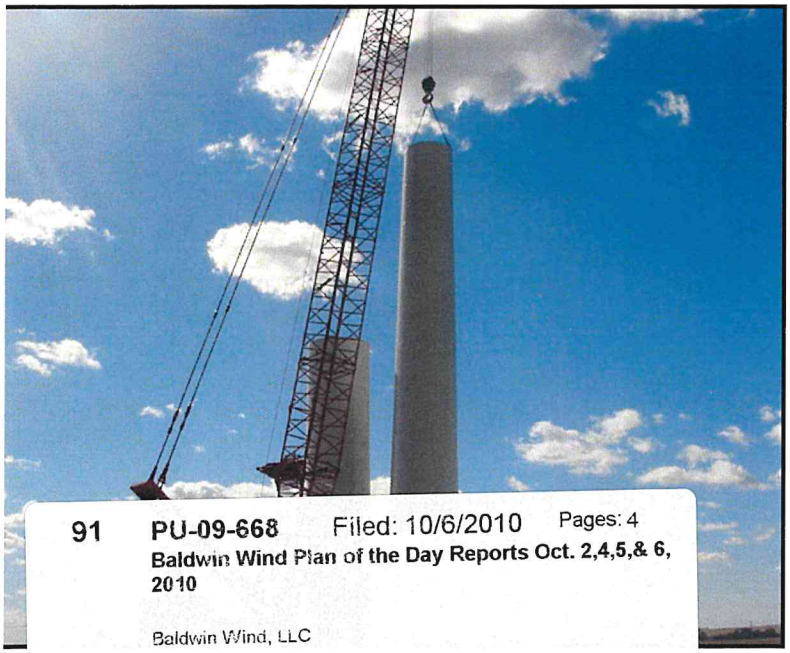

91 PU-09-668 Filed: 10/6/2010 Pages: 4
Baldwin Wind Plan of the Day Reports Oct. 2,4,5,& 6, 2010
Baldwin Wind, LLC

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	56	64	87.5%
Crane Pads Completed	56	64	87.5%
Tower Base Sections Erected	22	64	34.4%
Tower Mid Sections Erected	22	64	34.4%
Tower Top Sections Erected	14	64	21.9%
Nacelles Installed	14	64	21.9%
Rotors Installed	14	64	21.9%
Tower Wiring Complete	12	64	18.8%
Mechanically Complete	10	64	15.6%
Pre-Commissioned	3	64	4.7%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	140,184	157,430	89.0%
500 Cable Trenched	13,965	15,455	90.4%
1000 Cable Trenched	76,996	77,170	99.8%
Transformers Set/Terminated	32	64	50.0%

(as of COB yesterday)

Contents shall not be forwarded or distributed without prior written consent of NEXTEra™ Energy Resources

NEXTera® ENERGY RESOURCES

NextEra™ Energy Resources

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Monday, 10-4-10
High: 73
Precipitation Chances: 0 %

COD: 11-30-10
Low: 43

Days to COD: 58
Winds: SE @ 14 mph
Weather Forecast: Sunny

NextEra™ Energy Resources | Blattner Energy | Paradigm | GE

Safety/Environmental:
- Do not go under suspended loads
- Fence off wetland as needed
- Installing silt fence as needed

Civil/Erection:
- Reclaim at 56, 57 & 59
- Erect base & mid at 42-43
- Erect top, nacelle, & rotor at 37

Foundations:
- Backfill at 5 & 24
- Build crane pad at 5 & 24

Collection:
- Trench and install 4/0 at 5-6
- Underground splicing at SP1001, SP1101 & SP901
- Setting transformer box pads at 8-12
- Terminating HV at 30-31 & LV at 29-31
- DTA to controller terminating at 29-31
- Grounding grid testing at 16-20

Electrical:
- Tower wiring at 33-34
- Mechanical Completion Pre-walk at 53
- IIP at 53-54
- GE Pre-commissioning at 58-59

Substation:
- Bus fabrication
- Spread surface rock
- Start conduit run into Wilton II

RECEIVING (As of COB yesterday)

	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	3	3
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	57	64	89.1%
Crane Pads Completed	57	64	89.1%
Tower Base Sections Erected	22	64	34.4%
Tower Mid Sections Erected	22	64	34.4%
Tower Top Sections Erected	17	64	26.6%
Nacelles Installed	17	64	26.6%
Rotors Installed	17	64	26.6%
Tower Wiring Complete	12	64	18.8%
Mechanically Complete	10	64	15.6%
Pre-Commissioned	3	64	4.7%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	140,184	157,430	89.0%
500 Cable Trenched	13,965	15,455	90.4%
1000 Cable Trenched	76,996	77,170	99.8%
Transformers Set/Terminated	33	64	51.6%

(as of COB yesterday)

Contents shall not be forwarded or distributed without prior written consent of NEXTEra™ Energy Resources

NEXTera ENERGY RESOURCES

NextEra™ Energy Resources

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Tuesday, 10-5-10
High: 78
Precipitation Chances: 0 %

COD: 11-30-10
Low: 39

Days to COD: 57
Winds: W @ 12 mph
Weather Forecast: Mostly Sunny

NextEra™ Energy Resources | Blattner Energy | Paradigm | GE

Safety/Environmental:
- Do not go under suspended loads
- Fence off wetland as needed
- Installing silt fence as needed

Civil/Erection:
- Reclaim at 53-56
- Erect base & mid at 44-45
- Erect nacelle, & rotor at 37-39

Foundations:
- Backfill at 1, 3 & 4
- Build crane pad at 1, 3 & 4

Collection:
- Trench and install 4/0 at 24-26
- Underground splicing at SP905 & SP906
- Setting transformer box pads at 7-9
- Terminating HV at 27 & 29 & LV at 29 & 31
- DTA to controller terminating at 29-31
- Grounding grid testing at 17-19 & 23

Electrical:
- Tower wiring at 34-35
- Mechanical Completion Pre-walk at 32-33
- IIP at 32-33
- GE Pre-commissioning at 56-57

Substation:
- Bus fabrication
- Spread surface rock
- Control wire installation
- Start conduit run into Wilton II

RECEIVING (As of COB yesterday)

	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	3	3
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	60	64	93.8%
Crane Pads Completed	60	64	93.8%
Tower Base Sections Erected	24	64	37.5%
Tower Mid Sections Erected	24	64	37.5%
Tower Top Sections Erected	18	64	28.1%
Nacelles Installed	17	64	26.6%
Rotors Installed	17	64	26.6%
Tower Wiring Complete	15	64	23.4%
Mechanically Complete	12	64	18.8%
Pre-Commissioned	7	64	10.9%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	142,380	157,430	90.4%
500 Cable Trenched	13,965	15,455	90.4%
1000 Cable Trenched	76,996	77,170	99.8%
Transformers Set/Terminated	34	64	53.1%

(as of COB yesterday)

Contents shall not be forwarded or distributed without prior written consent of NEXTEra™ Energy Resources

NEXTera ENERGY RESOURCES

NextEra™ Energy Resourc

Baldwin Wind, LLC

Plan of the Day (POD)

Date: Wednesday, 10-6-10
High: 70
Precipitation Chances: 0 %

COD: 11-30-10
Low: 37

Days to COD: 56
Winds: W @ 7 mph
Weather Forecast: Mostly Sunny

NextEra™ Energy Resources | Blattner Energy | Paradigm | GE

Safety/Environmental:
- Do not go under suspended loads
- Fence off wetland as needed
- Installing silt fence as needed

Civil/Erection:
- Reclaim at 53-56
- Erect base & mid at 46-47
- Erect top & nacelle at 38
- Erect rotor at 37-38

Foundations:
- Backfill at 2 & 4
- Build crane pad at 2 & 4

Collection:
- Trench and install 4/0 at 2-4
- Underground splicing at SP906, SP1006 & SP1106
- Setting transformer at 7-15
- Terminating HV at 16-18 & LV at 27-28
- DTA to controller terminating at 27-28
- Grounding grid testing at 17-19

Electrical:
- Tower wiring at 39
- Mechanical Completion Pre-walk at 34-35
- IIP at 35-36
- GE Pre-commissioning at 54-57

Substation:
- Bus fabrication
- Spread surface rock
- Control wire installation
- Conduit run into Wilton II

RECEIVING (As of COB yesterday)

	Total	Received	Balance
PMT XFR	65	65	0
Grounding XFR	6	3	3
4/0 Cable	519,519	500,688	18831
500 KCM	51,002	58,397	-7395
Copperclad	65,280	68,882	-3602
1000 KCM	254,661	280,360	-25699
1000 KCM LVC	24,000	38,230	-14230
12 Fiber SM FOC	289,504	294,530	-5026
XFR Box Pads	64	64	0
Controllers	64	64	0
Bases	64	64	0
Mids	64	64	0
Tops	64	64	0
Nacelles	64	64	0
Hubs	64	64	0
Blade Sets	64	64	0

Negative Number Indicates Overage of Cable

General Construction Status

	Complete	Total	% Complete
Roads Subgraded	76,066	76,066	100.0%
Roads Built	76,066	76,066	100.0%
Silt Fence Installed	3,584	11,417	31.4%
Foundations Excavated	64	64	100.0%
Foundations Poured	64	64	100.0%
Foundations Backfilled	62	64	96.9%
Crane Pads Completed	62	64	96.9%
Tower Base Sections Erected	26	64	40.6%
Tower Mid Sections Erected	26	64	40.6%
Tower Top Sections Erected	19	64	29.7%
Nacelles Installed	19	64	29.7%
Rotors Installed	18	64	28.1%
Tower Wiring Complete	17	64	26.6%
Mechanically Complete	13	64	20.3%
Pre-Commissioned	7	64	10.9%
Final Commissioned	0	64	0.0%
4/0 Cable Trenched	146,608	157,430	93.1%
500 Cable Trenched	13,965	15,455	90.4%
1000 Cable Trenched	76,996	77,170	99.8%
Transformers Set/Terminated	36	64	56.3%

(as of COB yesterday)

Contents shall not be forwarded or distributed without prior written consent of NEXTEra™ Energy Resources
