



PLAINS
ALL AMERICAN
PIPELINE, L.P.

Weekly Construction Progress Report

Case # **PU-12-40**

Project: Nelson to Ross

Week Ending: 7/1/2012

Report # 1

Title	Name	Company	Office Phone	Cell Phone
Project Manager	Jim Fleetwood	Plains Pipeline	307-472-9911	
Project Coordinator	Ron McCreery	Plains Pipeline	307-760-1705	
Project Coordinator	Terry Wainwright	PPI	501-940-0672	
Contractor Spread	Ron Marsh	Pro-Pipe	406-239-0996	
Brief Description of Week's Activities				
Survey completed out marking RoW 6-29-2012, Mowing Complete 6-29-2012				
Fence Building, Building Approaches, Grading RoW is at 8,900ft				
Project Completion Spread				
Description	Week Complete	% Week Complete	Total Complete	% Total Complete
Clear & Grade lft.				
ROW Finished lft.			8,900ft	0.10
Stringing lft.	n/a			
Welding	n/a			
Ditching	n/a			
Lowering In	n/a			
Backfill	n/a			
Clean-up	n/a			
Coating (Welds)	n/a			
ECDs Installed	n/a			
Silt Fence lft.	n/a	n/a		n/a
Hay bales ea.	n/a	n/a		n/a
Mats ea.	29	n/a	29	n/a
Waddles ea.	n/a	n/a		n/a
Project construction / reclamation activities				
Description	Week Complete	% Week Complete	Total Complete	% Total Complete
Roadway / Bores ea.	n/a	n/a		n/a
Erosion / Sediment	n/a	n/a		n/a
Topsoil	n/a	n/a		n/a
Restoration/Cleanup	n/a	n/a		n/a
Roadway Restoration	n/a	n/a		n/a
Fence / Gate	n/a	n/a		n/a
Fertilizing / Seeding	n/a	n/a		n/a
Project Site Safety				
On Staff personal, we are acting as Safety, working together & good communication to head off any safety concerns				

Signature: _____

Date: 7-2-2012

52 PU-12-40 Filed: 7/5/2012 Pages: 3
Plains Pipeline Nelson to Ross Pipeline progress report - week ending 7-1-2012



PLAINS
ALL AMERICAN
PIPELINE, L.P.

Weekly Construction Progress Report

Case # PU-12-40

Report # 1

Project: Nelson to Ross

Week Ending: 7/1/2012

Dates of construction	Startup	Shutdown
	6/15/2012	

Temperature high and low for week.	High	Low
	91°	53°

Landowner / Public Concerns	Addressing Individual	Phone
none		

Suspension of project activities (when, where, why ,how long)

On 06-26-2012/ Between 86th st & 87th st/ Due to Piping Plover Bird/Until we here from the USACE & USFWS

Identify Cultural Resources not previously identified.

n/a

Critical Habitat or Threatened or Endangered Species.

All proper authorities have been notified, & are waiting on response, all area's of concern has been taped off on count of Piping Plover, main areas of interest seems to be between 86th & 87th.

Cathodic Protection Installed	When	Where
n/a		


Special Coordination	Who	When
n/a		

Pipeline in-service date	Date
n/a	

Stripping topsoil west side of HWY 8



Stripping topsoil between 82nd ave & HWY 8

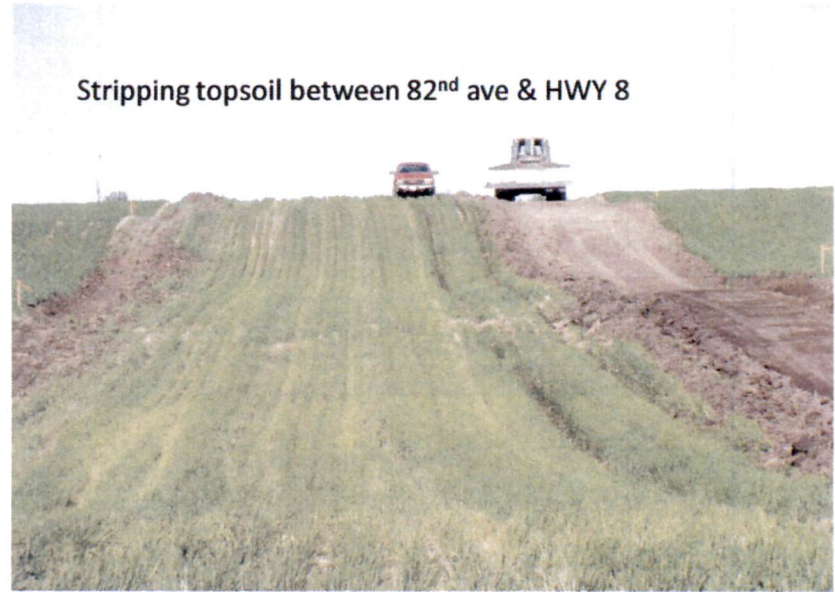

Drainage between 82nd ave & HWY 8 flume installed



Track Hoe hauled in & Building Approach at 82nd AVE

