




414 Nicollet Mall
Minneapolis, MN 55401

May 17, 2013



—Via Electronic Filing—

Burl W. Haar
Executive Secretary
Minnesota Public Utilities Commission
121 7th Place East, Suite 350
St. Paul, MN 55101

RE: SHERCO UNIT 3 RESTORATION UPDATE
DOCKET NO. E002/AA-11-1173

Dear Dr. Haar:

Northern States Power Company, doing business as Xcel Energy, provides this update to the Minnesota Public Utilities Commission on restoration activities at the Sherburne County Generating Station Unit 3 after the event that occurred on November 19, 2011. We recently committed to provide bi-weekly updates to the Commission until Sherco 3 is returned to service.

We previously reported that we expect Unit 3 to return to service on or before September 30, 2013. We continue to make good progress and we now expect a mid-September return to service date. Below we provide a summary of the current status of each major component and additionally provide Attachment A which is a visual summary of our progress to date.

- *Generator Rotor and Stator (77% complete)*

Assembly of the generator continues. Various internal components have been installed and preparations are proceeding to allow the installation of the generator end shields (end bells) when they are returned to site at the end of May. After the end shields are trial fitted and tested, the rotor will be inserted. Consistent with what we reported in our last update, we continue to expect mechanical completion of the generator assembly to occur by the end of July.

- *High Pressure and Reheat Turbines (80% complete)*

Pipe welding to the high pressure and reheat turbines has started. The combined

reheat valves have been welded to the reheat turbine and the main steam leads have been welded to the high pressure turbine. We currently forecast the high pressure and reheat turbines to be substantially assembled by early-August.

- *Low Pressure Turbines (LP-A and LP-B) (83% complete)*

Minor repairs continue (for all parts of the turbine) as additional work is identified when the parts are fully assembled. Final fit up, alignment, and installation of internal components continues. Trial installation of the LP-B rotor was completed to allow final diaphragm adjustments to commence. Assembly of the two low pressure turbines is forecasted to be substantially complete by early-August.

- *Generator Exciter (74% complete)*

The exciter assembly is nearing completion. The rotor, bearings, and end shields have been trial assembled and aligned.

- *Balance of Plant Systems and Components*

The balance of plant systems and components, like piping and cable, continue to be installed and restored. We have established a schedule for the walk-down and valve line-up confirmation process for all balance of plant systems and components in preparation for the return to service. That schedule supports the turbine/generator restoration and return to service schedule and those system checks are in-progress.

We will continue to provide bi-weekly updates to the Commission, with our next update expected to be filed in early June 2013. We appreciate the opportunity to update the Commission on our work to restore Sherco 3 to service. Please contact me at christoper.b.clark@xcelenergy.com or (612) 215-4593 if there are any questions regarding this update.


Sincerely,

/s/

CHRISTOPHER B. CLARK
REGIONAL VICE PRESIDENT
RATES AND REGULATORY AFFAIRS

Enclosures
c: Service List

Xcel Energy
 SHERCO 3
 Restoration Project
 Update: May 14, 2013

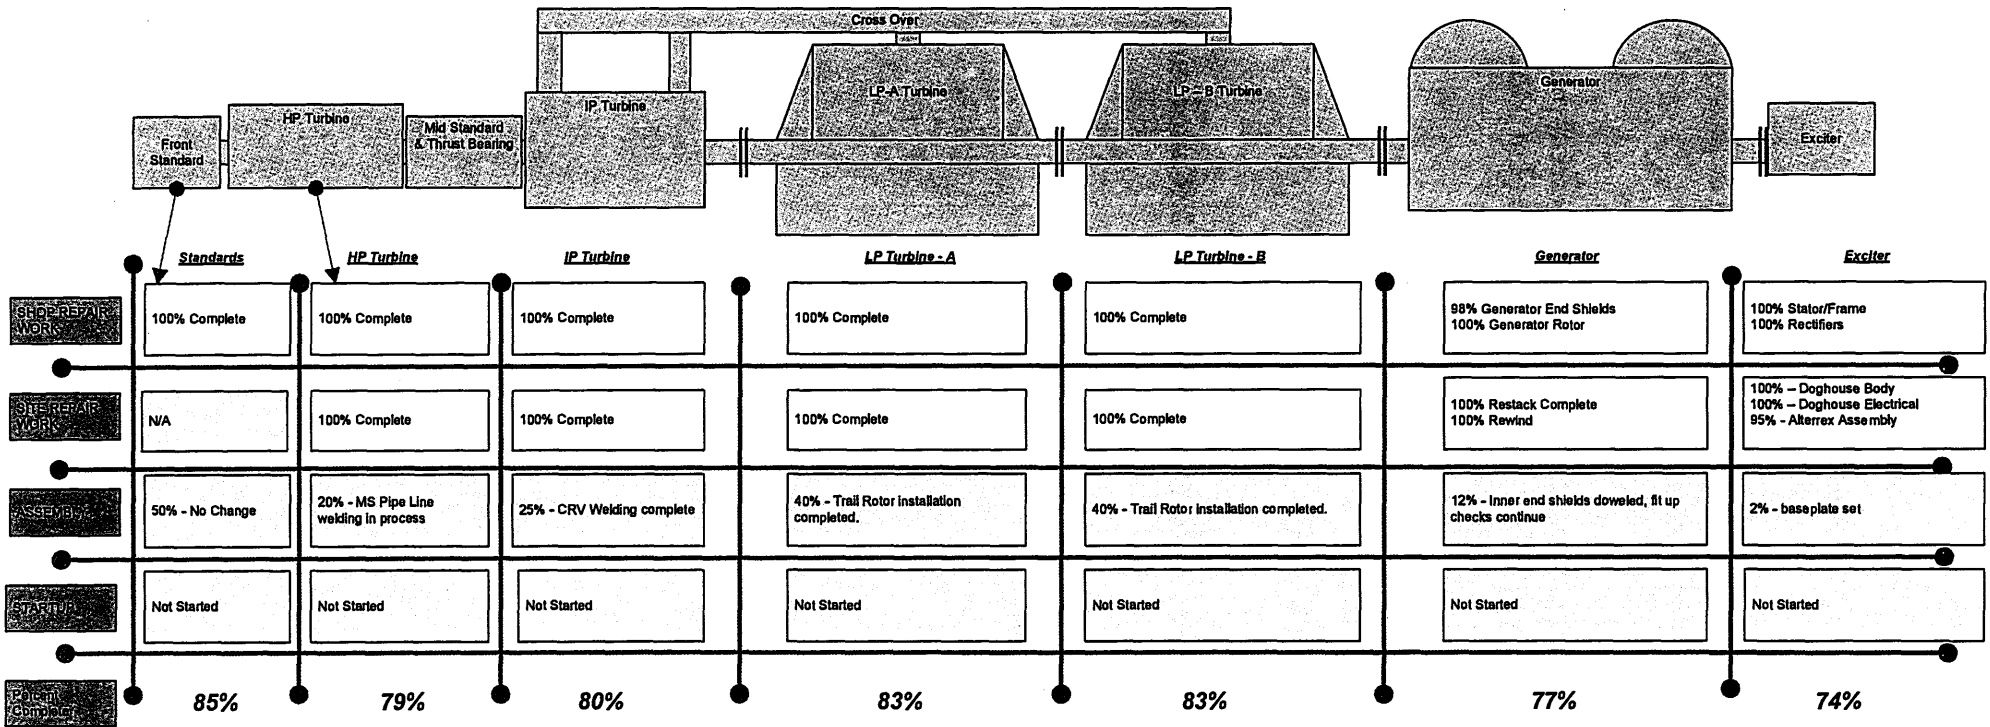

Notes:
 1. BOP Mech/Electrical/Controls/Instrumentation/New Parts orders work not represented here, however, all is on track to support the re-assembly and startup of unit.

CERTIFICATE OF SERVICE

I, Ketti Lindberg, hereby certify that I have this day served copies of the foregoing document on the attached list of persons.

by depositing a true and correct copy thereof, properly enveloped with postage paid in the United States mail at Minneapolis, Minnesota;

by email; or

by electronic filing.

Docket Nos.: E002/AA-11-1173 Sherco Unit 3 Restoration Update

Dated this 17th day of May 2013.

/s/

Ketti Lindberg

First Name	Last Name	Email	Company Name	Address	Delivery Method	View Trade Secret	Service List Name
Christopher	Anderson	canderson@allete.com	Minnesota Power	30 W Superior St Duluth, MN 558022191	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Julia	Anderson	Julia.Anderson@ag.state.mn.us	Office of the Attorney General-DOC	1800 BRM Tower 445 Minnesota St St. Paul, MN 551012134	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
James J.	Bertrand	james.bertrand@leonard.com	Leonard Street & Deinard	150 South Fifth Street, Suite 2300 Minneapolis, MN 55402	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Michael	Bradley	bradley@moss-barnett.com	Moss & Barnett	4800 Wells Fargo Ctr 90 S 7th St Minneapolis, MN 55402-4129	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Jeffrey A.	Daugherty	jeffrey.daugherty@centerpointenergy.com	CenterPoint Energy	800 LaSalle Ave Minneapolis, MN 55402	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Sharon	Ferguson	sharon.ferguson@state.mn.us	Department of Commerce	85 7th Place E Ste 500 Saint Paul, MN 551012198	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Ronald	Giteck	ron.giteck@ag.state.mn.us	Office of the Attorney General-RUD	Antitrust and Utilities Division 445 Minnesota Street, BRM Tower St. Paul, MN 55101	Electronic Service 1400	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Lloyd	Grooms	lgrooms@winthrop.com	Winthrop and Weinstine	Suite 3500 225 South Sixth Street Minneapolis, MN 554024629	Paper Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Burl W.	Haar	burl.haar@state.mn.us	Public Utilities Commission	Suite 350 121 7th Place East St. Paul, MN 551012147	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Alan	Jenkins	aj@jenkinsatlaw.com	Jenkins at Law	2265 Roswell Road Suite 100 Marietta, GA 30062	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric

First Name	Last Name	Email	Company Name	Address	Delivery Method	View Trade Secret	Service List Name
Richard	Johnson	johnsonr@moss-barnett.com	Moss & Barnett	4800 Wells Fargo Center South Seventh Street Minneapolis, MN 55402	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Mark J.	Kaufman	mkaufman@ibewlocal949.org	IBEW Local Union 949	12908 Nicollet Avenue South Burnsville, MN 55337	Paper Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Thomas G.	Koehler	N/A	Local Union #160, IBEW	2909 Anthony Ln Minneapolis, MN 55418-3238	Paper Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Michael	Krikava	mkrikava@briggs.com	Briggs And Morgan, P.A.	2200 IDS Center 80 S 8th St Minneapolis, MN 55402	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Douglas	Larson	dlarson@dakotaelectric.com	Dakota Electric Association	4300 220th St W Farmington, MN 55024	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
John	Lindell	agorud.ecf@ag.state.mn.us	Office of the Attorney General-RUD	1400 BRM Tower 445 Minnesota St St. Paul, MN 551012130	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Pam	Marshall	pam@energycents.org	Energy CENTS Coalition	823 7th St E St. Paul, MN 55106	Paper Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Andrew	Moratzka	apmoratzka@stoel.com	Stoel Rives LLP	33 South Sixth Street Suite 4200 Minneapolis, MN 55402	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
David W.	Niles	david.niles@avantenergy.com	Minnesota Municipal Power Agency	Suite 300 200 South Sixth Street Minneapolis, MN 55402	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Joseph V.	Plumbo		Local Union 23, I.B.E.W.	932 Payne Avenue St. Paul, MN 55130	Paper Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric

First Name	Last Name	Email	Company Name	Address	Delivery Method	View Trade Secret	Service List Name
Richard	Savelkoul	rsavelkoul@martinsquires.com	Martin & Squires, P.A.	332 Minnesota Street Ste W2750 St. Paul, MN 55101	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Ken	Smith	ken.smith@districtenergy.com	District Energy St. Paul Inc.	76 W Kellogg Blvd St. Paul, MN 55102	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Ron	Spangler, Jr.	rlspangler@otpc.com	Otter Tail Power Company	215 So. Cascade St. PO Box 496 Fergus Falls, MN 565380496	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Byron E.	Starns	byron.starns@leonard.com	Leonard Street and Delnard	150 South 5th Street Suite 2300 Minneapolis, MN 55402	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
James M.	Strommen	jstrommen@kennedy-graven.com	Kennedy & Graven, Chartered	470 U.S. Bank Plaza 200 South Sixth Street Minneapolis, MN 55402	Paper Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Eric	Swanson	eswanson@winthrop.com	Winthrop Weinstine	225 S 6th St Ste 3500 Capella Tower Minneapolis, MN 554024629	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
SaGonna	Thompson	Regulatory.Records@xcelenergy.com	Xcel Energy	414 Nicollet Mall FL 7 Minneapolis, MN 554011993	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
Lisa	Veith	lisa.veith@ci.stpaul.mn.us	City of St. Paul	400 City Hall and Courthouse 15 West Kellogg Blvd. St. Paul, MN 55102	Electronic Service	No	GEN_SL_Northern States Power Company dba Xcel Energy-Elec_Xcel Misc Electric
